

Water Supplies Department

New Works Branch Construction Division

11 Tai Yip Lane Kowloon Bay

Kowloon Hong Kong

Attention: Mr Y M Chan

Your reference:

Our reference:

HKWSD201/50/105270

Date:

28 September 2018

BY POST

Quotation No.: WQ/17/A071

Independent Environmental Checker for Water Supplies Department

-Proposed Desalination Plant in TKO Area 137 for Contract No. 13/WSD/16

Verification of Monthly EM&A Report No.1

We refer to emails of 30 August, 13, 26 and 27 September 2018 attaching Monthly EM&A Report No.1 for the captioned project prepared by the ET.

We have no further comment and hereby verify the Monthly EM&A Report No.1 in accordance with Clause 3.5 of the Environmental Permit no. EP-503/2015/A.

Should you have any queries regarding the above, please do not hesitate to contact the undersigned or our Mr Derek Wong on 2618 2831.

Yours faithfully ANEWR CONSULTING LIMITED

Nic Lam

Independent Environmental Checker

LHHN/lhmh

Web: www.anewr.com

Acuity Sustainability

Acuity Sustainability Consulting Limited

Unit 1908, Nos. 301-305 Castle Peak Road, Kwai Chung, N.T. O: 2333-6823 | F: 2333-1316 | E: general@acuityhk.com | www.acuityhk.com



Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

Monthly EM&A Report No.1 (Period from 30 Aug to 31 Aug 2018)

September 2018 (Rev. 0)

	Prepared by:	Certified by:
Name	Nelson Tsui	Jacky Leung
Position	Environmental Team	Environmental Team Leader
Signature	74	
Date:	27 September 2018	27 September 2018



Revision History

0	1st Submission	
Rev.	DESCRIPTION OF MODIFICATION	DATE



CONTENT

1.	Basic Project Information
2.	Noise Monitoring
3.	Summary of Monitoring Exceedance, Complaints, Notification of Summons and Prosecutions
4.	EM&A Site Inspection
5.	Future Key Issues
6.	Conclusion and Recommendations 21

Appendix A	Construction Programme
Appendix B	Summary of Implementation Status of Environmental Mitigation
Appendix C	Impact Monitoring Schedule of the Reporting Month (Blank)
Appendix D	Noise Monitoring Equipment Calibration Certificate (Blank)
Appendix E	Event/Action Plan for Noise Exceedance
Appendix F	Noise Monitoring Data (Blank)
Appendix G	Complaint Log and Regulatory Compliance Proforma
Appendix H	Site Inspection Proforma
Appendix I	Proactive Environmental Protection Proforma
Appendix J	Impact Monitoring Schedule of Next Reporting Month (Blank)



EXECUTIVE SUMMARY

Introduction

- A1. Penta-Ocean Concentric Joint Venture (POCJV) is contracted to carry out the Mainlaying in Tseung Kwan O under Contract No. 13/WSD/16 (hereinafter known as "the Project").
- A2. In accordance with the Environmental Monitoring and Audit (EM&A) Manual for the Project, EM&A works should be carried out by Environmental Team (ET), Acuity Sustainability Consulting Limited (ASCL), during the construction phase of the Project.
- A3. This is the 1st Monthly EM&A Report, prepared by ASCL, for the Project summarizing the monitoring results and audit findings of the EM&A programme at and around Tseung Kwan O (TKO) during the reporting period from 30 August 2018 to 31 August 2018.
- A4. The EM&A programme for this contract has covered environmental monitoring on construction noise level at selected NSRs and Contractor's environmental performance auditing in the aspects of construction dust, construction noise, water quality, waste management, Landscape and Visual and Ecology.

Summary of Main Works Undertaken & Key Mitigation Measures Implemented

- A5. Key works carried out in this reporting period for the Project included the following:
 - The erection of temporary fencing and gates
 - Erection of the site accommodation (Portion G of the Site)
 - Set up of TTA as per the approved Temporary Traffic Management Scheme (TTMS) for mainlaying works by open trench method between CHA670 to CHA714 (30 Aug 2018)
 - Underground utilities detection conducted by a Competent Person between CHA670 to CHA714 (31 Aug 2018)
- A6. The major environmental impacts brought by the above construction works include:
 - Construction dust and noise generation from open trenching
 - Waste generation from construction activities
- A7. The key environmental mitigation measures implemented for the Project in this reporting period associated with the above construction works include:
 - Dust suppression by regular wetting and water spraying in the open trench area
 - Reduction of noise from equipment and machinery on-site



Sorting and storage of general refuse and construction waste

Summary of Exceedance & Investigation & Follow-up

A8. No noise monitoring was conducted during the reporting period due to the over distant monitoring station from the works location. No project-related exceedance of the Action Level was recorded during the reporting period.

Complaint Handling and Prosecution

- A9. No project-related environmental complaint was received during the reporting period.
- A10. Neither notifications of summons nor prosecution was received for the Project.

Reporting Change

A11. There were no changes to be reported that may affect the on-going EM&A programme.

Summary of Upcoming Key Issues and Key Mitigation Measures

- A12. Key works anticipated in the next reporting period for the Project will include the following:
 - Erection of the site accommodation (Portion G of the Site)
 - Mainlaying by open trench method
- A13. The major environmental impacts brought by the above construction works will include:
 - · Construction dust and noise generation from open trenching
 - Waste generation from construction activities
- A14. The key environmental mitigation measures for the Project in the coming reporting period associated with the above construction works will include:
 - Dust suppression by regular wetting and water spraying in the open trench area
 - Reduction of noise from equipment and machinery on-site
 - Sorting and storage of general refuse and construction waste



1. Basic Project Information

1.1 Background

- 1.1.1 The proposed Desalination Plant at Tseung Kwan O (DPTKO) will produce potable water with an initial capacity of 135 million liters per day (MLD), expandable to an ultimate capacity of 270 MLD in the future to provide a secure and alternative fresh water resource complying with the World Health Organization (WHO) standards. The plant will adopt the Seawater Reverse Osmosis (SWRO) technology, which dominates the market due to its reliability and progressive reduction in cost as the technology advances.
- 1.1.2 Pursuant to the Environmental Impact Assessment Ordinance (EIAO), the Director of Environmental Protection granted the Variation of Environmental Permit (No. EP-503/2015/A) to Water Supplies Department (WSD) for the Project on 26 January 2018.
- 1.1.3 The scope of the Contract may be considered in brief, to consist of the laying of about 10km long 1200mm diameter fresh water mains and the associated works along the alignment of the Project as shown with the overall view in **Figure 1.1**.



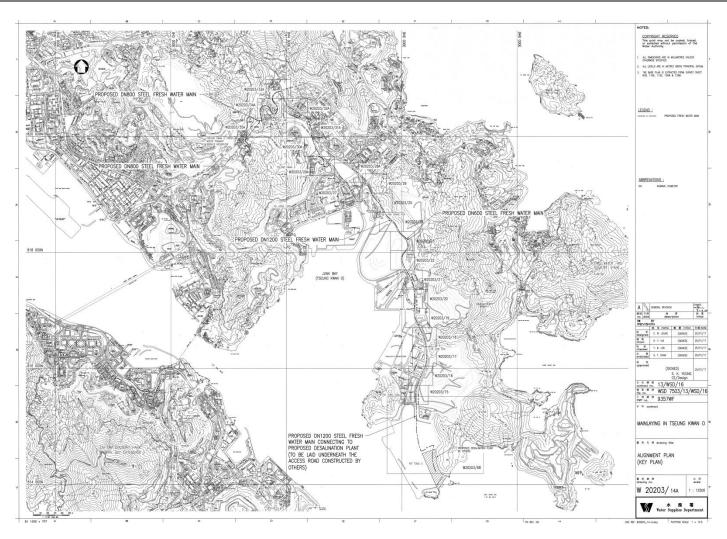


Figure 1.1 Overview of Mainlaying in TKO



- 1.2 The Reporting Scope
- 1.2.1 This is the 1st Monthly EM&A Report for the Project which summarizes the key findings of the EM&A programme during the reporting period from 30 August 2018 to 31 August 2018.
- 1.3 Project Organization
- 1.3.1 The Project Organization structure for Construction Phase is presented in **Figure 1.2**.

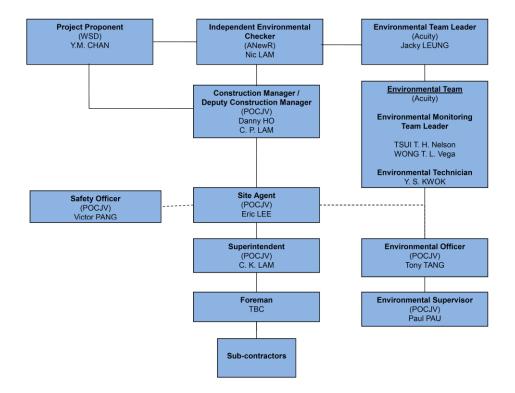


Figure 1.2 Project Organization Chart

1.3.2 Contact details of the key personnel are presented in **Table 1.1** below:

Table 1.1 Contact Details of Key Personnel

Party	Position	Name	Telephone no.
Penta-Ocean -Concentric Joint Venture	Environmental Officer	Tony Tang	9433-2628
Acuity Sustainability Consulting Limited	Environmental Team Leader	Jacky Leung	2698-6833



Party	Position	Name	Telephone no.
ANewR Consulting Limited	Independent Environmental Checker	Nic Lam	2618-2831

- 1.4 Summary of Construction Works
- 1.4.1 Details of the major construction works undertaken in this reporting period are shown in **Table 1.2** and **Figure 1.3** below. The construction programme is presented in **Appendix A**.

Table 1.2 Summary of the Construction Works Undertaken during the Reporting Month

Location of works	Construction works undertaken	Remarks on progress	
Portion A, B, C & D of the Project Site	Initial Joint Survey with Water Supplies Department	Completed	
Portion F & G of the Project Site	Erection of Temporary Fencing and Gates	In progress	
and i reject one	Erection of the Site Accommodation	In progress	
Portion J of the Project Site (Figure 1.3)	Set up of Temporary Traffic Arrangement (TTA) as per the approved Temporary Traffic Management Scheme (TTMS) for mainlaying works by open trench method	completed on 30 th	
	Detection of Underground Utilities conducted by Competent Person	Commenced and completed on 31st August 2018	



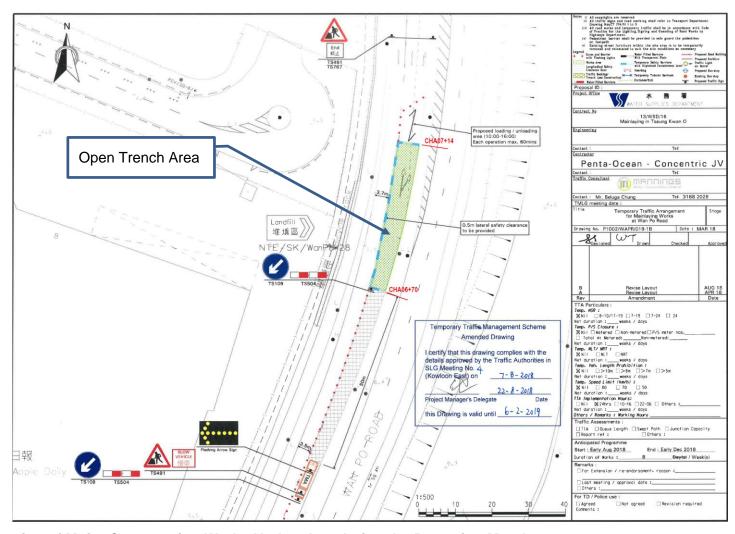


Figure 1.3 Location of Major Construction Works Undertaken during the Reporting Month



- 1.5 Summary of Environmental Status
- 1.5.1 A summary of the valid permits, licences, and /or notifications on environmental protection for this Project is presented in **Table 1.3**

Table 1.3 Summary of the Status of Valid Environmental Licence, Notification, Permit and Documentations

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
Variation of Environmental Permit	EP no.: EP-503/2015/A	Throughout the Contract	-
Notification of Construction Works under the Air Pollution Control (Construction Dust) Regulation (Form NA)	Ref no.: 423775	Throughout the Contract	-
Chemical Waste Producer Registration	WPN: 5213-839-P3287-01	Throughout the Contract	-
Billing Account for Disposal of Construction Waste	A/C no.: 7029491	Throughout the Contract	-

1.5.2 The status for all environmental aspects is presented **Table 1.4**.

Table 1.4 Summary of Status for Key Environmental Aspects under the EM&A Manual

Parameters	Status		
	Noise		
Baseline Monitoring	The baseline noise monitoring result has been reported in Baseline Monitoring Report and submitted to EPD under VEP		
	Condition 3.4		
Impact Monitoring	On-going		
	Waste Management		
Mitigation Measures in	On-going		
Waste Monitoring Plan			
	Environmental Audit		
Site Inspection On-going			

- 1.5.3 Other than the EM&A works by ET, regular environmental management meetings were conducted in order to enhance environmental awareness and closely monitor the environmental performance of the contractors.
- 1.5.4 The EM&A programme has been implemented in accordance with the recommendations presented in the approved EIA Report and the EM&A Manual. A summary of implementation status of the environmental mitigation measures for the construction phase of the Project during the reporting period is provided in **Appendix B**.



2. Noise Monitoring

- 2.1 Monitoring Requirements
- 2.1.1 To ensure no adverse noise impact, noise monitoring is recommended to be carried out within 300m radius from the nearby noise sensitive receivers (NSRs), during construction phase. The NSRs selected as monitoring station are (i) NSR4 Creative Secondary School, (ii) NSR24 PLK Laws Foundation College, and (iii) NSR31 School of Continuing and Professional Studies CUHK respectively.
- 2.1.2 In accordance with the EM&A Manual, baseline noise level at the noise monitoring stations were established as presented in the Baseline Monitoring Report. Impact noise monitoring will be conducted once per week in the form of 30-minutes measurements Leq, L10 and L90 levels recorded at each monitoring station between 0700 and 1900 hours on normal weekdays.
- 2.2 Noise Monitoring Parameters, Time, Frequency
- 2.2.1 Impact noise monitoring will be conducted weekly in the reporting period between 0700-1900 hours on normal weekdays. No construction works were carried out during 1900-0700 hours all days or any time on Sundays or general holidays during the reporting period.
- 2.2.2 Construction noise level measured in terms of the A-weighted equivalent continuous sound pressure level (LAeq). Leq 30min was used as the monitoring parameter for the time period between 0700 and 1900 hours on normal weekdays. Table 2.1 summarizes the monitoring parameters, frequency and duration of the impact noise monitoring. The monitoring schedule is provided in Appendix C. Appendix C is intentionally left blank since no impact monitoring was conducted in the reporting month.

Table 2.1 Noise Monitoring Parameters, Time, Frequency and Duration

Time	Frequency	Duration	Parameters
Daytime: 0700-1900 hours	Once per week	Continuously in $L_{\text{eq 5min}}/L_{\text{eq 30min}}$ (average of 6 consecutive $L_{\text{eq 5min}}$)	$L_{eq}, L_{10} \& L_{90}$

2.3 Noise Monitoring Locations


- 2.3.1 The monitoring locations should normally be made at a point 1m from the exterior of the NSRs building façade and be at a position 1.2m above the ground. A correction of +3dB(A) should be made to the free-field measurements.
- 2.3.2 According to the environmental findings detailed in the EIA report and Baseline Monitoring Report, the designated locations for the construction noise monitoring are listed in **Table 2.2** below.




Table 2.2 Noise Monitoring Location

NSR ID	Noise Sensitive Receivers	Monitoring Location	Position
NSR 4 Creative Secondary School		Roof Floor	1 m from facade
NSR 24	PLK Laws Foundation College	Pedestrian Road on Ground Floor	Free-field
NSR 31	School of Continuing and Professional Studies - CUHK	Roof Floor	1 m from facade

2.3.3 Three noise monitoring locations for impact monitoring at the nearby sensitive receivers are shown in **Figure 2.1-2.3.**

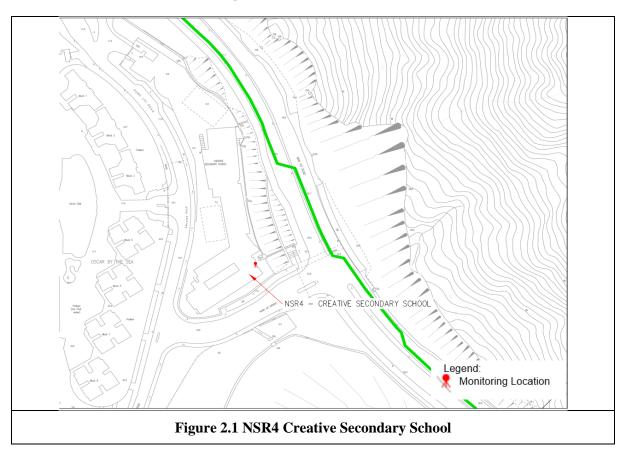



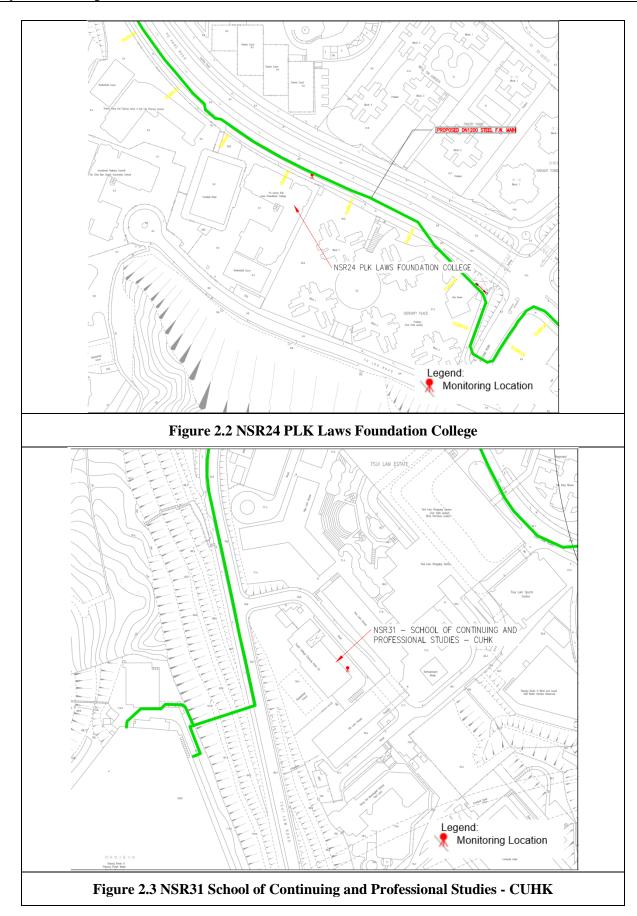



- 2.4 Impact Monitoring Methodology
- 2.4.1 Integrated sound level meter shall be used for the noise monitoring. The meter shall be in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications. Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration level before and after the noise measurements agree to within 1.0 dB(A). Calibration certificates of the instruments used are presented in Appendix D. Appendix D is intentionally left blank since no impact monitoring equipment was used in the reporting month.
- 2.4.2 Noise measurements shall not be made in the presence of fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

Table 2.3 Impact Noise Monitoring Equipment

Equipment	Brand and Model	Detection Limit
Sound Level Meter	Nti XL2	30-130 dB(A)
Sound Level Meter Calibrator	Rion NC-74	Nil
Pocket Wind Meter Anemometer	Kestrel 1000 Wind Meter	Nil

- 2.5 Action and Limit Levels
- 2.5.1 The Action/Limit Levels in line with the criteria of Practice Note for Professional Persons (ProPECC PN 2/93) "Noise from Construction Activities Non-statutory Controls" and Technical Memorandum on Environmental Impact Assessment Process issued by HKSAR Environmental Protection Department ["EPD"] under the Environmental Impact Assessment Ordinance, Cap 499, S.16 are presented in Table 2.4.

Table 2.4 Action and Limit Levels for Noise

Time Period	Action	Limit (dB(A))
normal weekdays	When one documented complaint is received from any one of the noise sensitive receivers	 70 dB(A) for school and 65 dB(A) during examination period

Notes:

- (a) Limits specified in the GW-TM and IND-TM for construction and operation noise, respectively.
- 2.5.2 If exceedances were found during noise monitoring. The actions in accordance with the Event and Action Plan shall be carried out according to **Appendix E**.



- 2.6 Monitoring Results and Observations
- 2.6.1 Noise monitoring data shall be recovered in real-time as it is a manned-event with data display from the sound level meters.
- 2.6.2 Referring to EM&A manual Section 4.1.2, the impact noise monitoring should be carried out at all the designated monitoring stations when there are project-related construction activities undertaken within a radius of 300m from the monitoring stations. No impact monitoring for noise impact was conducted in the reporting period due to the over distant monitoring station from the works location, where they were farther than 1 km from the closest monitoring station NSR4 and the works location.
- 2.6.3 Detailed monitoring results are presented in **Appendix F**. **Appendix F** is intentionally left blank since no impact monitoring for noise impact in this reporting month.



3. SUMMARY OF MONITORING EXCEEDANCE, COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTIONS

3.1 The Environmental Complaint Handling Procedure is shown in below Figure 3.1:

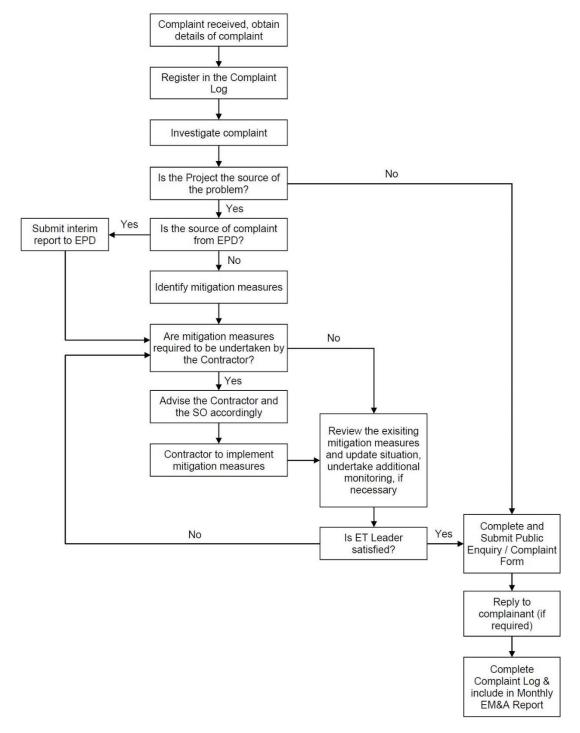


Figure 3.1 Environmental Complaint Handling Procedure



- 3.2 No noise monitoring was conducted during the reporting period due to the over distant monitoring station from the works location. No project-related exceedance of the Action Level was recorded during the reporting period.
- 3.3 No notification of summons and prosecution was received in the reporting period.
- 3.4 Statistics on complaints and regulatory compliance are summarized in **Appendix G**.



4. EM&A SITE INSPECTION

4.1 Site inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures under the Contract. In the reporting period, site inspections were carried out on 30 August 2018 at the site portions list in **Table 4.1** below.

Table 4.1 Site Inspection Record

Date		Inspected Site Portion	Time
30 A	August	Portion F & G of the Site	9:45am - 11:00am
2018			

- 4.2 One joint site inspection with IEC was carried out on 30 August 2018.
- 4.3 Minor deficiencies were observed during weekly site inspection. Key observations during the site inspections are summarized in **Table 4.2**.

Table 4.2 Site Observations

Date	Environmental Observations	Follow-up Status
30 August 2018	 Observation(s) and Recommendation(s) 1. At the under-construction site office, construction debris was observed scatteredly next to the gullies. 2. The gullies next to the construction area for site office were not properly covered and there is no clear diversion of site runoff on-site. 3. The contractor was request to post Environmental Permit at all vehicle site entrance. 4. Used paint drums were observed inside the site area and it should be placed inside lockable chemical store on site. 5. Stagnant water were found inside the site office and it should be diverted to the waste water treatment tank. 	 Construction debris were cleaned up by the contractor. Sandbags were placed to protect the gullies. The Environmental Permit was posted by the contractor at the required work area. The paint drum had been removed.

- 4.4 The Contractor has rectified all of the observations identified during environmental site inspections in the reporting period
- 4.5 According to the EIA Study Report, Environmental Permit, contract documents and EM&A Manual, the mitigation measures detailed in the documents are implemented as much as practical during the reporting period. An updated Implementation Status of Environmental Mitigation Measures (EMIS) is provided in **Appendix B**.
- 4.6 Site inspection proforma of the reporting period is provided in **Appendix H**.



5. FUTURE KEY ISSUES

- 5.1 Key works anticipated in the next reporting period for the Project will include the following:
 - Erection of the site accommodation (Portion G of the Site)
 - Mainlaying by open trench method
- 5.2 The major environmental impacts brought by the above construction works will include:
 - Construction dust and noise generation from open trenching
 - Waste generation from construction activities
- 5.3 The key environmental mitigation measures for the Project in the coming reporting period associated with the above construction works will include:
 - Dust suppression by regular wetting and water spraying in the open trench area
 - · Reduction of noise from equipment and machinery on-site
 - Sorting and storage of general refuse and construction waste
- 5.4 The proactive environmental protection proforma for the next reporting month is listed in **Appendix I.**
- 5.5 The impact monitoring schedule for the next reporting month is attached in **Appendix J**. **Appendix J** is intentionally left blank since no impact monitoring will be conducted in the next reporting month.
- 5.6 Referring to EM&A Manual Section 4.1.2, the impact noise monitoring should be carried out at all the designated monitoring stations when there are project-related construction activities undertaken within a radius of 300m from the monitoring stations. No noise monitoring was scheduled in the next reporting period due to the over distant monitoring station from the works location.



6. CONCLUSION AND RECOMMENDATIONS

- 6.1 This 1st monthly Environmental Monitoring and Audit (EM&A) Report presents the EM&A works undertaken during the period from 30 August 2018 to 31 August2018 in accordance with the EM&A Manual and the requirement under EP-503/2015/A.
- 6.2 No noise monitoring was conducted during the reporting period due to the over distant monitoring station from the works location. No project-related exceedance of the Action Level was recorded during the reporting period.
- 6.3 Weekly environmental site inspection was conducted during the reporting period. Minor deficiencies were observed during site inspection and were rectified. The environmental performance of the Project was therefore considered satisfactory.
- 6.4 According to the environmental site inspections performed in the reporting month, the Contractor is reminded to pay attention on maintaining site tidiness and proper materials storage.
- 6.5 No environmental complaint was received in the reporting period.
- 6.6 No notification of summons or prosecution was received since commencement of the Contract.
- 6.7 The ET will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures.



Appendix A

Construction Programme



13/WSD/16 - Mainlaying in Tseung Kwan O

Outline Construction Programme (As on 31 Aug 2018)

					_																		2020									_									
YEAR		LOCATION	FROM	то	<u> </u>	_		_	2018	_			_	L.,				2019	_			_	Ь.	_	_	_			_	_	_	_	_	_		_	2021		_		\dashv
MONTH	PJ-ID	ROAD			1 2	2 3	4	5	6 7	8	9	10 1	11 12	1	2 3	4	5	6 7	7 8	9	10 1	1 12	1	2	3 4	1 5	6	7	8 9	10	11	12	1 2	3	4	5 (5 7	8	9 1	10 13	1 12
							Ш																																		
Section A (TKO137 to Wan Po Road)																																									
Section A1 (Open-trench)	-	Wan Po Road	0	362																																					
Section A2 (Pipe-Jacking)	A	Wan Po Road	362	530																					Т					Т											
Section A3 (Open-trench)	-	Wan Po Road	530	1379	П		П	Т		#																		П	Т	Т	П		Т	П	П		Т				\Box
Section A4 (Pipe-Jacking)	В	Wan Po Road	1379	2268	П		П	Т			П		Т		Т			Т		П		Т			Т	Т			Т	Т			Т					П		Т	\Box
Section A5 (Open-trench)	-	Wan Po Road	2268	4113				Т																														П	\top	Т	
					П		П	Т		П	П		Т			П				П		Т	П			Т	П	П	Т	Т	П		Т	П	П			П	Т	Т	П
Section B (Po Yap Road to Po Hong Road)					П		П	Т		Т																											Т	П	Т	Т	\Box
Section B1 (Pipe-Jacking)	С	Po Yap Road	4113	4200	П		П	T			П									П		Т				Т				Т	П		Т	П							\Box
Section B2 (Open-trench)	-	Po Yap & Po Hong Rd	4200	5500	П		П	Т		Т																		П	Т	Т	П			П	Т		Т	П	Т	\top	\Box
Section B3 (Pipe-Jacking)	D1 & D2	Po Hong & Ling Hong Rd	5500	5600	П		П	T		Г												Т	П			Т	П	П	T	Т	П			П				П	Т		\Box
Section B4 (Open-trench)	-	Ling Hong Road	5600	5799	П		П	Т												П			П			Т												П			\Box
Section B5 (Pipe-Jacking)	Е	Po Hong Road	5799	5838	П		П	T			П									П								П		Т	П			П							
Section B6 (Open-trench)	-	Po Hong Road	5838	6254	П		П	T		П													П			Т	П	П	Т	Т	П			П	T			П	Т	Т	\Box
Section B7 (Pipe-Jacking)	F	Po Hong Road	6254	6368	П															П		Т																			П
Section B8 (Open-trench)	-	Po Hong Road	6368	7250	П		П	Т		П																				П	П			П	Т			П	П	Т	\Box
					П		П	Т		Г	П		T			П				П		Т	П			Т	П	П	Т	Т	П			П	Т			П	Т	Т	П
Section C (Po Lam Road to Tsui Lam to TKOFWPSR*)					П		П	T		П																											Т	П	\top		\Box
Section C1 (Open-trench)	-	Po Lam Road	7250	7740	П		П																																T		П
Section C2 (Pipe-Jacking)	G	Tsui Lam Road	7740	7770	П		П	T	\top	T	П		T		T	П	П	T		П		T	П			T	Γ	П		Т					T		T	П	T	T	\Box
Section C3 (Open-trench)	-	Tsui Lam Road	7770	8300	П		П	T		T																										T	Т	П	T	\top	\Box
Section C4 (Slope)	-	TKOFWPSR	8300	8376							П				T	П		T		П		T	П			T								П					T		\Box
					П		П	丁		T	П		\top			П				П	\neg		П			Т	Γ	П	T	T	П		\top	П	T		Т	П	\top	\top	\Box

Commencement of works at CH.A 720 on 30 Aug 2018.

^{*}TKOFWPSR - Tseung Kwan O Fresh Water Primiary Service Reservoir

^{**}Remaining 1581m within TKO137 with site possession from Nov 2019



Appendix B

Summary of Implementation Status of Environmental Mitigation



EIA Reference	Recommended Environmental Protection Measures/	Objectives of the recommended measures &	Implementation	Impler Stage	nenta	tion	Relevant Legislation &
LIA Reference	Mitigation Measures	main concerns to address	Agent	D	С	0	Guidelines
Air Quality							
S4.8.1	Impervious dust screen or sheeting will be provided to enclose scaffolding from the ground floor level of building for construction of superstructure of the new buildings.	Land site/ During Construction	Contractor(s)		✓		Air Pollution Control (Construction Dust)
S4.8.1	Impervious sheet will be provided for skip hoist for material transport.	Land site/ During Construction, particularly dry season	Contractor(s)		✓		-
S4.8.1	The area where dusty work takes place should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after dusty activities as far as practicable.	Land site/ During Construction	Contractor(s)		*		-
S4.8.1	All dusty materials should be sprayed with water or a dust suppression chemical immediately prior to any loading, unloading or transfer operation.	Land site/ During Construction	Contractor(s)		√		-
S4.8.1	Dropping heights for excavated materials should be controlled to a practical height to minimise the fugitive dust arising from unloading.	Land site/ During Construction	Contractor(s)		✓		-
S4.8.1	During transportation by truck, materials should not be loaded to a level higher than the side and tail boards, and should be dampened or covered before transport.	Land site/ During Construction	Contractor(s)		√		-
S4.8.1	Wheel washing device should be provided at the exits of the work sites. Immediately before leaving a construction site, every vehicle shall be washed to remove any dusty material from its body and wheels as far as practicable.	Land site/ During Construction	Contractor(s)		√		-



EIA Reference	Recommended Environmental Protection Weasures/	Objectives of the recommended measures &	Implementation	Imple: Stage		tion	Relevant Legislation &
EIA Reference	Mitigation Measures	main concerns to address	Agent	D	С	0	Guidelines
S4.8.1	Road sections between vehicle-wash areas and vehicular entrance will be paved.	Land site/ During Construction	Contractor(s)		1		-
S4.8.1	Hoarding of not less than 2.4m high from ground level will be provided along the length of the Project Site boundary.	Land site/ During construction	Contractor(s)	✓	1		-
S4.8.1	Haul roads will be kept clear of dusty materials and will be sprayed with water so as to maintain the entire road surface wet at all times.	Land site/ During construction	Contractor(s)		✓		
S4.8.1	Temporary stockpiles of dusty materials will be either covered entirely by impervious sheets or sprayed with water to maintain the entire surface wet all the time.	Land site/ During construction	Contractor(s)		1		
S4.8.1	Stockpiles of more than 20 bags of cement, dry pulverised fuel ash and dusty construction materials will be covered entirely by impervious sheeting sheltered on top and 3-sides.	Land site/ During construction	Contractor(s)		√		
S4.8.1	All exposed areas will be kept wet always to minimise dust emission.	Land site/ During construction	Contractor(s)		√		
S4.8.1	Ultra-low-sulphur diesel (ULSD) will be used for all construction plant on-site, as defined as diesel fuel containing not more than 0.005% sulphur by weight) as stipulated in Environment, Transport and Works Bureau Technical Circular (ETWB-TC(W)) No 19/2005 on Environmental Management on Construction Sites.	Land site/ During construction/ During Operation	Contractor(s)		1	√	Environment, Transport and Works Bureau Technical Circular (ETWB- TC(W)) No 19/2005 on Environmental Management on Construction Sites
S4.8.1	The engine of the construction equipment during idling will be switched off.	Land site/ During construction	Contractor(s)		*		



EIA Reference		Objectives of the recommended measures &	Implementation	Implementation Stage		tion	Relevant Legislation &
LIA Nelelelice	Mitigation Measures	main concerns to address	Agent	D	C O Guidelines		Guidelines
S4.8.1	Concrete batching plant will be required on site. control measures recommended in the Guidance Note on a Bes Practicable Means for Cement Works (Concrete Batching Plant) (BPM 3/2 (93)) will be implemented. The control measures recommended in the Guidance Note on a Bes Practicable Means for Cement Works (Concrete Batching Plant) (BPM 3/2 (93)) will be implemented.) -	Contractor(s)		•		Guidance Note on a Best
S4.8.1	Regular maintenance of construction equipment deployed on-site will be conducted to prevent black smoke emission.	Land site/ During construction	Contractor(s)		√		
S4.10	To ensure proper implementation of the recommended dust mitigation measures and good construction site practices during the construction phase, environmental site audits on weekly basis is recommended throughout the construction period.	Land site/ During construction	Contractor(s)/ Environmental Team (ET) & Independent Environmental Checker (IEC)		•		

Note: D – Design stage C – Construction O – Operation



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures &	Implementation	Implementation Stage			Relevant Legislation & Guidelines
	willigation weasures	main concerns to address	Agent	D	С	0	Guidelines
Noise							
S5.7	Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction phase.	All area/ During construction	Contractor(s)		✓		A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Silencers or mufflers on construction equipment will be utilised and will be properly maintained during the construction phase.	Noise control/ During construction	Contractor(s)		✓		A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Mobile plant, if any, will be sited as far away from NSRs as possible.	Noise control/ During construction	Contractor(s)		✓		A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum.	Noise control/ During construction	Contractor(s)		✓		A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Plants known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.	Noise control/ During construction	Contractor(s)		✓		A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities.	Noise control/ During construction	Contractor(s)		✓		A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Use of Quite Powered Mechanical Equipment (QPME).	Noise control/ During construction	Contractor(s)		✓		A Practical Guide for the Reduction of Noise from Construction Works,



EIA Reference	Recommended Environmental Protection Measures/	Objectives of the recommended measures &	Implementation	Impler Stage		tion	Relevant Legislation & Guidelines
	Mitigation Measures	main concerns to address	Agent	D	С	0	Guidelines
S5.7	Movable noise barriers of 3m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater than its height. The noise barrier material should have a superficial surface density of at least 7 kg m-2 and have no openings or gaps.	Noise control/ During construction	Contractor(s)		✓		A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	The noise insulating sheet should be deployed such that there would be no opening or gaps on the joints.	Noise control/ During construction	Contractor(s)		✓		A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Construction activities (e.g. excavation/shoring, reinstatement (asphalt), and pipe jacking) will be planned and carried out in sequence, such that items of PME proposed for these activities will not be operated simultaneously.	Noise control/ During construction	Contractor(s)		*		A Practical Guide for the Reduction of Noise from Construction Works
S5.7	PMEs will not be used at the works areas near educational institutions with residual impact (ie the "influence area" within a radius of 40m) during school hours in order to reduce impact to the educational institutions.	Noise control / During construction	Contractor(s)		√		A Practical Guide for the Reduction of Noise from Construction Works
S5.7	Noise enclosures or acoustic sheds would be used to cover stationary PME such as generators. Portable/Movable noise enclosure made of material with superficial surface density of at least 7 kg m-2 may be used for screening the noise from operation of the saw/groover, concrete.	Noise control/ Pre- construction/ During construction	Contractor(s)	*	✓		
S5.9	Sawcutting pavement, breaking up of pavement, excavation /shoring, pipe laying, backfilling, reinstatement (concrete) and pipe jacking shall be scheduled outside the examination period.	Noise control/ Pre- construction/ During construction	Contractor(s)	√	√		
S5.9	In view the duration of noise exceedance at Creative Secondary School, PLK Laws Foundation College,	Noise control/ Pre- construction/ During	Contractor(s)	*	1		



EIA Reference	Recommended Environmental Protection Weastires/	Objectives of the recommended measures &	Implementation	Implementation Stage			Relevant Legislation & Guidelines
	witigation weasures	main concerns to address	Agent	D	С	0	Guidelines
	TKO Kei Tak Primary School and School of Continuing and Professional Studies-CUHK is limited to 8 weeks, the construction work in the influence areas near the four schools shall be scheduled during long school holidays (eg summer holiday, Easter holiday or Christmas holiday, etc) as far as practicable. Scheduling the construction work for the four schools and	construction					
S5.10	A noise monitoring programme shall be implemented for the construction phase.	Designated monitoring stations as defined in EM&A Manual/During construction phase	Environmental Team (ET)				
S5.10	The effectiveness of on-site control measures could also be evaluated through the regular site audits.	All facilities/ During construction	Contractor(s)/ Environmental Team (ET) & Independent Environmental Checker (IEC)		*		-

Note: D – Design stage C – Construction O – Operation



EIA Reference	Recommended Environmental Protection Measures/	Objectives of the recommended measures &	Implementation	Imple: Stage	menta	tion	Relevant Legislation &
	Mitigation Measures	main concerns to address	Agent	D	С	0	Guidelines
Water Quality		·					•
S6.9	Dredged marine sediment will be disposed of in a gazetted marine disposal area in accordance with marine dumping permit conditions of the Dumping at Sea Ordinance (DASO).	Marine Dredging/ During construction	Contractor(s)		*		Dumping at Sea Ordinance (DASO)
S6.9	Disposal vessels will be fitted with tight bottom seals in order to prevent leakage of material during transport.	Marine Dredging/ During construction	Contractor(s)		1		-
S6.9	Barges will be filled to a level, which ensures that material does not spill over during transport to the disposal site and that adequate freeboard is maintained to ensure that the decks are not washed by wave action.	Marine Dredging/ During construction	Contractor(s)		V		-
S6.9	After dredging, any excess materials will be cleaned from decks and exposed fittings before the vessel is moved from the dredging area.	Marine Dredging/ During construction	Contractor(s)		1		-
S6.9	All vessels should be well maintained and inspected before use to limit any potential discharges to the marine environment.	Marine Dredging/ During construction	Contractor(s)		√		-
S6.9	All vessels must have a clean ballast system.	Marine Dredging/ During construction	Contractor(s)		√		-
S6.9	No discharge of sewage/grey wastewater should be allowed. Waste water from potentially contaminated area on working vessels should be minimized and collected. These kinds of wastewater should be brought back to port and discharged at appropriate collection and treatment system.	Marine Dredging/ During construction	Contractor(s)		•		-
S6.9	No soil waste is allowed to be disposed overboard.	Marine Dredging/ During construction	Contractor(s)		1		-



EIA Reference	Mitigation Measures	Objectives of the recommended measures &	Implementation	Implementation Stage			Relevant Legislation & Guidelines
	Mitigation Measures	main concerns to address	Agent	D	С	0	Guidelines
S6.9	Silt removal facilities such as silt traps or sedimentation facilities will be provided to remove silt particles from runoff to meet the requirements of the TM standard under the WPCO. The design of silt removal facilities will be based on the guidelines provided in ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly.		Contractor(s)		•		ProPECC PN 1/94 TM Standard under the WPCO
S6.9	Earthworks to form the final surfaces will be followed up with surface protection and drainage works to prevent erosion caused by rainstorms.	Land site & drainage/ During construction	Contractor(s)		✓		-
S6.9	Appropriate surface drainage will be designed and provided where necessary.	Land site & drainage/ During construction	Contractor(s)		✓		-
S6.9	The precautions to be taken at any time of year when rainstorms are likely together with the actions to be taken when a rainstorm is imminent or forecasted and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94.	Land site & drainage/ During construction	Contractor(s)		1		ProPECC PN 1/94
S6.9	Oil interceptors will be provided in the drainage system where necessary and regularly emptied to prevent the release of oil and grease into the storm water drainage system after accidental spillages.	Land site & drainage/ During construction	Contractor(s)		√		-
S6.9	Temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge, if any, will be adequately designed for the controlled release of storm flows.	Land site & drainage/ During construction	Contractor(s)		✓		-



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Relevant Legislation &
				D	С	0	Guidelines
S6.9	The temporary diverted drainage, if any, will be reinstated to the original condition when the construction work has finished or when the temporary diversion is no longer required.	Land site & drainage/ During construction	Contractor(s)		√		-
S6.9	Appropriate numbers of portable toilets shall be provided by a licensed contractor to serve the construction workers over the construction site to prevent direct disposal of sewage into the water environment.	Land site & drainage/ During construction	Contractor(s)		√		-
S6.9 and S6.12	The sterilization water should be dechlorinated with total residual chlorine (TRC) level below 1 mg/L before discharge to public sewer. In situ testing of TRC should also be conducted for the discharge of chlorinated water for pipeline disinfection to ensure sufficient dechlorination before discharge to public sewer.	Sterilization of water mains prior to commissioning	Contractor(s)		*	√	Technical Memorandum for Effluents Discharged into Drainage and Sewerage Systems Inland and Coastal Waters
S6.9	The cleaning and flushing water should also be treated and desilted to the relevant discharge requirement stipulated in TM-DSS before discharging.	Sterilization of water mains prior to commissioning	Contractor(s)		√	✓	Technical Memorandum for Effluents Discharged into Drainage and Sewerage Systems Inland and Coastal Waters
S6.9	Site drainage should be well maintained and good construction practices should be observed to ensure that oil, fuels, solvents and other chemicals are managed, stored and handled properly and do not enter the nearby water streams.	Land site & drainage/ During construction/ During operation	Contractor(s)		*	1	-
S6.12	Regular site inspections will be carried out in order to confirm that regulatory requirements are being met and that contractors are implementing the standard site practice and mitigation measures as proposed to reduce potential impacts to water quality.	During construction	Contractor(s)/ Environmental Team (ET) & Independent Environmental Checker (IEC)		✓		-

Note: D – Design stage C – Construction O – Operation



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Relevant Legislation &
				D	С	0	Guidelines
Waste Managemei	nt						
S8.5	Nomination of approved personnel to be responsible for standard site practices, arrangements for collection and effective disposal to an appropriate facility of all wastes generated at the site.	Contract mobilisation/ During construction	Contractor(s)		✓		-
\$8.5	Training of site personnel in proper waste management and chemical handling procedures. Training will be provided to workers on the concepts of site cleanliness and appropriate waste management procedures, including waste reduction, reuse and recycling at the beginning of the construction works.	Contract mobilisation/ During construction	Contractor(s)		*		-
S8.5	Provision of sufficient waste disposal points and regular collection for disposal.	All area/ During construction/ During operation	Contractor(s)		√	√	DEVB TC(W) No. 8/2010, Enhanced Specification for Site Cleanliness and Tidines
S8.5	Appropriate measures to reduce windblown litter and dust transportation of waste by either covering trucks or by transporting wastes in enclosed containers.	All area/ During construction	Contractor(s)		•		DEVB TC(W) No. 8/2010, Enhanced Specification for Site Cleanliness and Tidiness.
S8.5	A waste management plan (WMP) as stated in the "ETWB TC(W) No. 19/2005, Environmental Management on Construction Sites" for the amount of waste generated, recycled and disposed of (including the disposal sites) will be established and implemented during the construction phase as part of the Environmental Management Plan (EMP). The Contractor will be required to prepare the EMP and submits it to the Architect/ Engineer under the Contract for approval prior to implementation.	All area/ During construction	Contractor(s)		✓		ETWB TC(W) No. 19/2005, Environmental Management on Construction Sites



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Relevant Legislation &
				D	С	0	Guidelines
S8.5	Separation of chemical wastes for special handling and appropriate treatment at the Chemical Waste Treatment Centre at Tsing Yi.	All area/ During construction	Contractor(s)		✓		Chapters 2 & 3 Code of Practice on the Packaging, Labelling & Storage of Chemical Wastes published under the Waste Disposal Ordinance (Cap 354), Section 35
S8.5	Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors.	Land site/ During construction	Contractor(s)		✓		Waste Disposal Ordinance (Cap 354)
S8.5	A recording system for the amount of wastes generated/ recycled and disposal sites. The tripticket system will be included as one of the contractual requirements and implemented by the contractor(s).	Land site/ During construction	Contractor(s)		✓		DEVB TC(W) No. 6/2010, Trip Ticket System for Disposal of Construction & Demolition Materials
S8.5	Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of material and their proper disposal.	Land site/ During construction/ During operation	Contractor(s)		✓		WBTC 32/92, The Use of Tropical Hard Wood on Construction Site
S8.5	Encourage collection of aluminium cans and waste paper by individual collectors during construction with separate labelled bins provided to segregate these wastes from other general refuse by the workforce.	Land site/ During construction	Contractor(s)		√		ETWB TCW No. 33/2002, Management of Construction and Demolition Material Including Rock
S8.5	Any unused chemicals and those with remaining functional capacity will be recycled as far as possible.	Land site/ During construction	Contractor(s)		✓		-
S8.5	Use of reusable non-timber formwork to reduce the amount of C&D materials.	All areas/ During construction	Contractor(s)		√		WBTC 32/92, The Use of Tropical Hard Wood on Construction Site



EIA Reference	Recommended Environmental Protection Measures/	Objectives of the recommended measures & main concerns to	Implementation Agent	Imple: Stage		tion	Relevant Legislation &
	Mitigation Measures	address		D	С	0	Guidelines
S8.5	Prior to disposal of construction waste, wood, steel and other metals will be separated to the extent practical, for re-use and/or recycling to reduce the quantity of waste to be disposed of to landfill.	All areas/ During construction	Contractor(s)		√		DEVB TC(W) No. 6/2010, Trip Ticket System for Disposal of Construction & Demolition Materials
S8.5	Proper storage and site practices to reduce the potential for damage or contamination of construction materials.	All areas/ During construction	Contractor(s)		V		-
S8.5	Plan and stock construction materials carefully to reduce amount of waste generated and avoid unnecessary generation of waste.	All areas/ During construction	Contractor(s)		✓		-
S8.5	A Sediment Quality Report (SQR) for sampling and chemical testing of the sediment will be prepared and submitted to the EPD for approval. The approved detailed sampling and chemical testing will be carried out prior to the commencement of the dredging activities to confirm the sediment disposal method.	Marine works/ During construction	Contractor(s)		✓		ETWB TC(W) No. 34/2002 and Dumping at Sea Ordinance (DASO)
S8.5	The management of dredged/ excavated sediment management requirement from ETWB TC(W) No. 34/2002 will be incorporated in the Specification of the Contract Documents.	Marine works/ During construction	WSD/ Contractor(s)		✓		ETWB TC(W) No. 34/2002 and Dumping at Sea Ordinance (DASO)
S8.5	The contractor will open a billing account with EPD in accordance with the Waste Disposal (Charges for Disposal of Construction Waste) Regulation for the payment of disposal charges.	Contract mobilisation/ During construction	Contractor(s)		√		Cap 354N Waste Disposal (Charges for Disposal of Construction Waste) Regulation



EIA Reference	Recommended Environmental Protection Measures/	Objectives of the recommended measures & main concerns to	Implementation Agent	Imple: Stage		tion	Relevant Legislation &
	Mitigation Measures	address		D	С	0	Guidelines
S8.5	A trip-ticket system will be established in accordance with DEVB TC(W) No. 6/2010 to monitor the reuse of surplus excavated materials off-site and disposal of construction waste and general refuse at transfer facilities/ landfills, and to control fly-tipping.	Contract mobilisation/ During construction	Contractor(s)		√		DEVB TC(W) No. 6/2010, Trip Ticket System for Disposal of Construction & Demolition Materials
S8.5	The project proponent will also conduct regular inspection of the waste management measures implemented on site as described in the Waste Management Plan.	All area/ During construction	Contractor(s)/ Environmental Team (ET) & Independent Environmental Checker (IEC)		√		ETWB TC(W) No. 19/2005 Environmental Management on Construction Sites
S8.5	A recording system (similar to summary table as shown in Annex 5 and Annex 6 of Appendix G of ETWB TC(W) No. 19/2005) for the amount of waste generated, recycled and disposed of (including the disposal sites) will be established during the construction phase.	All area/ During construction	Contractor(s)		√		Annex 5 and Annex 6 of Appendix G of ETWB TC(W) No. 19/2005
S8.5	Inert C&D materials (public fill) will be reused within the Project as far as practicable.	All area/ During construction	Contractor(s)		1		-
\$8.5	Public fill and construction waste shall be segregated and stored in different containers or skips to facilitate reuse or recycling of materials and their proper disposal.	All area/ During construction	Contractor(s)		✓		-
S8.5	Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable.	All area/ During construction	Contractor(s)		√		-
\$8.5	To reduce the potential dust and water quality impacts of site formation works, C&D materials will be wetted as quickly as possible to the extent practice after filling.	All area/ During construction	Contractor(s)		✓		Air Pollution Control (Construction Dust) Regulation (Cap 311R); WPCO (Cap 358)



EIA Reference	Recommended Environmental Protection Measures/	Objectives of the recommended measures & main concerns to	Implementation Agent	Imple Stage		tion	Relevant Legislation &
	Mitigation Measures	address		D	С	0	Guidelines
S8.5	Open stockpiles of excavated/ fill materials or construction wastes on-site should be covered with tarpaulin or similar fabric.	Land site/ During Construction, particularly dry season	Contractor(s)		√		Air Pollution Control (Construction Dust) Regulation (Cap 311R)
S8.5	Chemical waste container shall be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed.	All area/ During construction/ During operation	Contractor(s)/WSD		✓	✓	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Chemical waste container shall have a capacity of less than 450 L unless the specifications have been approved by the EPD.	All area/ During construction/ During operation	Contractor(s)/WSD		✓	✓	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	A label in English and Chinese shall be displayed on the chemical container in accordance with instructions prescribed in Schedule 2 of the Regulations.	All area/ During construction/ During operation	Contractor(s)/WSD		V	√	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall be enclosed on at least 3 sides.	All area/ During construction/ During operation	Contractor(s)/WSD		√	√	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes



EIA Reference	Recommended Environmental Protection Measures/	Objectives of the recommended measures & main concerns to	Implementation Agent	Impler Stage		tion	Relevant Legislation & Guidelines
S8.5	Mitigation Measures Storage areas for chemical waste shall have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest.	address All area/ During construction/ During operation	Contractor(s)/WSD	D	C	0	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall have adequate ventilation.	All area/ During construction/ During operation	Contractor(s)/WSD		*	*	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary).	All area/ During construction/ During operation	Contractor(s)/WSD		√	*	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall be arranged so that incompatible materials are appropriately separated.	All area/ During construction/ During operation	Contractor(s)/WSD		✓	√	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	General refuse will be stored in enclosed bins or compaction units separately from construction and chemical wastes.	All area/ During construction/ During operation	Contractor(s)/WSD		✓	√	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes



EIA Reference	Recommended Environmental Protection Measures/	Objectives of the recommended measures & main concerns to	Implementation Agent	Imple Stage		tion	Relevant Legislation &
	Mitigation Measures	address		D	С	0	Guidelines
S8.5	Adequate number of waste containers will be provided to avoid over-spillage of waste.	All area/ During construction/ During operation	Contractor(s)/WSD		√	*	DEVB TC(W) No. 8/2010 Enhanced Specification for Site Cleanliness and Tidiness.
\$8.5	A reputable waste collector will be employed by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily basis to minimise odour, pest and litter impacts.	All area/ During construction/ During operation	Contractor(s)/WSD		√	√	-
S8.5	Recycling bins will be provided at strategic locations within the Site to facilitate recovery of recyclable materials (including aluminium can, waste paper, glass bottles and plastic bottles) from the Site. Materials recovered will be sold for recycling.	All area/ During construction/ During operation	Contractor(s)/WSD		✓	*	-
S8.5	To avoid any odour and litter impact, accurate number of portable toilets will be provided for workers on-site.	All area/ During construction	Contractor(s)		1		-
S8.5	The burning of refuse on construction sites is prohibited by law.	All area/ During construction	Contractor(s)		1		Air Pollution Control Ordinance (Cap 311)
S8.7	To facilitate monitoring and control over the contractors' performance on waste management, a waste inspection and audit programme will be implemented throughout the construction phase.	All facilities/ During construction	ET/ IEC		√		-

Note: D – Design stage C – Construction O – Operation



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to	Implementation Agent	Imple Stage	menta	tion	Relevant Legislation &
		address		D	С	0	Guidelines
Ecology							
S9.7	For slope mitigation works within the Clear Water Bay Country Park, to avoid tree felling and damages to trees, the exact locations of the flexible barrier foundation plates, soil nails and rock dowels can be adjusted during detailed design, and a setback distance from existing trees is recommended to be maintained as far as practical. A detailed specification describing the exact locations of the flexible barrier foundation plates, soil nails and rock dowels will be prepared to illustrate how the setback distance from existing trees would be implemented for tree avoidance.	Slope mitigation works area/ During detailed design/ During construction	Contractor(s)				-
S9.7	Pruning of tree canopies along the alignment of the flexible barriers shall be limited to a minimum.	Slope mitigation works area/ During construction	Contractor(s)		✓		
S9.7	The alignment of flexible barriers shall be optimized to preserve all species of conservation interest and minimize the impact to the existing vegetation as far as practicable. All individuals of <i>Marsdenia lachnostoma</i> within the slope mitigation areas shall be retained <i>in- situ</i> , by positioning the alignment of flexible barrier at a minimum 1.5m in a radius away from these individuals.	Slope mitigation works area/ During detailed design/ During construction	Contractor(s)	*	1		-
S9.7 and 9.10	At the detailed design stage prior to the commencement of the slope mitigation works, a vegetation survey shall be carried out at the slope mitigation areas within the Clear Water Bay Country Park to assess the condition and identify the location of each individual of <i>Marsdenia lachnostoma</i> and other flora species of conservation interest that may be directly affected by the construction works.	During detailed design/ During construction	Contractor(s)	*	*		-



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to	Implementation Agent	Imple: Stage		tion	Relevant Legislation &
		address		D	С	0	Guidelines
S9.7	Temporary fencing will be installed to fence off the concerned species either in groups of individually within the works area and in the close proximity to prevent from being damaged and disturbed during construction. A sign identifying the site shall be attached to the fence and flagging tape shall be attached to the individuals to visualize their locations.	Slope mitigation works area/ During construction	Contractor(s)		✓		-
S9.7 and S9.10	A specification for fencing and demarcating individuals of <i>Marsdenai lachnostoma</i> (or other flora species of conservation interest, if found) adjacent to the proposed alignment of the flexible barriers will be prepared to protect the species.	Slope mitigation works area/ During construction	Contractor(s)		√		-
S9.7	Induction training shall also be provided to all site personnel in order to brief them on this flora of conservation interest including the locations and their importance.	Slope mitigation works area/ During construction	Contractor(s)		√		-
S9.7	The resident site supervisory staff will closely monitor the conditions of concerned individuals during construction of flexible barriers in the close proximity.	Slope mitigation works area/ During construction	Contractor(s)		V		-
S9.7	Erect fences along the boundary of the works area before the commencement of works to prevent vehicle movements and encroachment of personnel onto adjacent areas.	All area/ During construction	Contractor(s)		√		-
S9.7	Regularly check the work site boundaries to ensure that they are not breached and that damage does not occur to surrounding areas.	All area/ During construction	Contractor(s)/ Environmental Team (ET)		✓		-



EIA Reference	Recommended Environmental Protection Measures/	Objectives of the recommended measures & main concerns to	Implementation Agent	Implementation Stage			Relevant Legislation & Guidelines
	Mitigation Measures	address		D	С	0	Guidelines
S9.7	Avoid any damage and disturbance, particularly those caused by filling and illegal dumping, to the surrounding habitats through proper management of waste disposal.	All area/ During construction	Contractor(s)		*		-
S9.7	Reinstate temporarily affected areas, particularly the habitats of plantation and shrubland-grassland immediately after completion of construction works, through on-site tree/shrub planting. The tree/shrub species will be chosen with reference to those in the surrounding area.	All area/ During construction	Contractor(s)		✓		-
S9.7	Affected habitats within the Clear Water Bay Country Bay shall be reinstated by hydro-seeding and planting of climbers and native shrub seedlings where practical upon completion of the slope mitigation works.	All area/ During construction	Contractor(s)		√		-

Note: D – Design stage C – Construction O – Operation



EIA Reference	Mitigation Measures	Objectives of the recommended measures & main concerns to	Implementation Agent	Imple Stage	menta	tion	Relevant Legislation &
		address		D	С	0	Guidelines
Landscape & Visua	al						
S11.10 & 11.11	The construction area and area allowed for temporary structures, such as the contractor's office, will be minimized to a practical minimum. (MM1)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓		✓	-
S11.10 & 11.11	At the detailed design stage, the design team will seek to minimize the landscape footprint of the Project and above ground facilities, while satisfying all other requirements. (MM2)	All area/ Detailed design/ During construction/ During operation	WSD/Contractor(s)	1	V	√	-
S11.10 & 11.11	Design principles will be adopted to take into account the surrounding area, particularly Clear Water Bay Country Park behind and the nearby waterfront, with due consideration given to: - green roofs where practical (ie without equipment on the roof); - roadside planting; - aesthetic treatment of all structures; - vertical greening; screen planting along application site; and - landscape enhancement with amenity planting where practical including planting along the edge (site boundary) fence with native shrubs where feasible, - to reduce their visual impact and blend them into the surrounding landscape. (MM3)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	*	V	•	-
S11.10 & 11.11	All trees within the Project Site or the potential slope mitigation works area will be carefully protected during construction according to DEVB TCW No. 10/2013 – Tree Preservation (MM4)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	V	V	ETWB TCW No. 3/2006 - Tree Preservation.



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to	Implementation Agent	Imple Stage	menta	tion	Relevant Legislation & Guidelines
		address		D	С	0	
S11.10 & 11.11	No tree within the Country Park will be felled. Trees within the Site unavoidably affected by the works will be transplanted where necessary and practical. For trees that need to be felled, compensatory planting will be provided to the satisfaction of relevant Government departments. A compensatory tree planting proposal including locations of tree compensation will be submitted to seek relevant government department's approval, in	All area/ Detailed design/ During construction/ During operation	WSD/Contractor(s)	✓	\	*	DEVB TC(W) No. 10/2013
	accordance with DEVB TC(W) No. 10/2013. (MM5)						
S11.10 & 11.11	Any slope mitigation works necessary to address natural terrain hazards, will be minimized to minimize any potential environmental impact to the Country Park e.g. soil nailing and rock stabilization will aim to avoid existing trees e.g. should any restoration of vegetation be necessary, the best planting matrix with native species will be established, with the aim of resembling the existing vegetation. (MM6)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	•	•	*	
S11.10 & 11.11	Dredging works for the installation of intake structures and outfall diffusers should be minimized to avoid or reduce any potential environmental impacts to as low as reasonably practicable (ALARP). The intake and outfall structures (e.g. intake openings and diffuser heads) will be prefabricated and transferred to site for installation. (MM7)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	V	√	~	
S11.10 & 11.11	All night-time lighting will be reduced to a practical minimum both in terms of number of level and will be hooded and directional. (MM8)units and lux level and will be hooded and directional. (MM8)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	*	√	√	-

Note: D – Design stage C – Construction O – Operation



EIA Reference	Mitigation Measures	Objectives of the recommended measures & main concerns to	Implementation Agent	Imple Stage	menta	tion	Relevant Legislation & Guidelines
		address		D	С	0	
Landfill Gas Hazar	rd						
S12.7	During all works, safety procedures should be implemented to minimise the risks of fires and explosions, asphyxiation of workers and toxicity effects resulting from contact with contaminated soil and groundwater.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	*	✓	•	-
\$12.7	During trenching and excavation as well as creation of confined spaces at near to or below ground level, precautions should be clearly laid down and rigidly Gas detection equipment and appropriate breathing apparatus should be available and used when entering confined spaces or trenches deeper than 1 metre.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	V	√	√	
S12.7	The Contractor should make the workers are aware of potential hazards of working in confined spaces (any chamber, manhole or culvert which is large enough to permit access to personnel). Such work in confined spaces is controlled by the Factories and Industrial Undertakings (Confined Spaces) Regulations of the Factories and Industrial Undertakings Ordinance. Following the Safety Guide to Working in Confined Spaces ensures compliance with the above regulations.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	~	✓	✓	
S12.7	Safety officers, specifically trained with regard to landfill gas and leachate related hazards and the appropriate actions to take in adverse circumstances, should be present on the site throughout the works, in particular, when works are undertaken below grade.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	*	√	√	
S12.7	All personnel who work on site and all visitors to the site should be made aware of the possibility of ignition of gas in the vicinity of the works, the possible presence of contaminated water and the need to avoid physical contact with it.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	√	1	√	



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to	Implementation Agent	Imple Stage		tion	Relevant Legislation &
		address		D	С	0	Guidelines
S12.7	Monitoring for landfill gas should be undertaken in all excavations, manholes, chambers (particularly during pipe jacking) and any confined spaces through the use of an intrinsically safe portable instrument, appropriately calibrated and capable of measuring the concentrations of methane. carbon dioxide and oxygen.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	√	✓	√	
S12.7	Monitoring frequency and areas to be monitored should be specified prior to commencement of groundwork, either by the Safety Officer, or by an appropriately qualified person. All measurements should be recorded and documented.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	√	√	✓	
S12.7	Proceed drilling with adequate care and precautions against the potential hazards which may be encountered.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	*	1	✓	
S12.7	Prior to the commencement of the site works, the drilling contractor should devise a 'method-of-working' statement covering all normal and emergency procedures (including but not limited to number of operatives, experience and special skills of operatives, normal method of operations, emergency procedures, supervisors responsibilities, storage and use of safety equipment, safety procedures and signs, barriers and guarding). The site supervisor and all operatives must be familiar with this statement.	All area/ During construction/ During operation	Contractor(s)	*	V	*	
S12.7	Where below ground service entries are necessary to the Incoming Switchgear Room, 132 kV Substation and Chlorine Store (I) and (II), the entry point should be sealed to prevent gas entry. In addition, any below grade cable trenches entering the Incoming Switchgear Room and 132 kV Substation can become the pathway for landfill gas and hence grilled metal covers should be used.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	~	√	~	



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to	Implementation Agent	Imple Stage		tion	Relevant Legislation &
		address		D	С	0	Guidelines
S12.7	It is recommended regular landfill gas monitoring should be carried out at the Incoming Switchgear Room, 132 kV Substation and Chlorine Store (I) and (II). The monitoring frequency will be monthly for the first year of operation. If the monitoring results show no sign of landfill gas migration, reduce the monitoring frequency to once every six months.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	√	✓	✓	
S12.7	The manholes and utility pits within the Project Site and along the fresh water mains. Each manhole/ utility pit should be monitored with two measurements (at mid depth and base). Each measurement should be monitored for a minimum of 10 minutes. A steady reading and peak reading should be recorded at each manhole/ utility pit and for each measurement. The need for venting the manhole/ utility pit and further monitoring will be reviewed after the initial monitoring.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	V	*	✓	
S12.7	All construction, operation and maintenance personnel working on-site as well as visitors should be made aware of the hazards of landfill gas and its possible presence on-site. This should be achieved through a combination of posting warning signs in prominent places and also by access to detailed information on landfill gas hazards and the designs and procedural means by which these hazards are being minimised on-site.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	*	*	√	

Note: D – Design stage C – Construction O – Operation



Appendix C

Impact Monitoring Schedule of the Reporting Month



(Blank)



Appendix D

Noise Monitoring Equipment Calibration Certificate



(Blank)



Appendix E

Event/Action Plan for Noise Exceedance



Event and Action Plan for Construction Noise Monitoring

Event	Act	ion						
	ET		IEC		ER		Co	ntractor
Action Level	1.	Carry out investigation to identify the source and cause of the complaint/ exceedance(s)	1. 2.	Review the analyzed results submitted by the ET Review the proposed remedial	1.	Confirm receipt of Notification of Exceedance in writing Require Contractor to propose	1.	Submit noise mitigation proposals, if required, to the IEC and ER Implement noise mitigation
	2.	Notify IEC, ER, and Contractor and report the results of investigation		measures by the Contractor and advise the ER accordingly		remedial measures for the analysed noise problem		proposals.
		to the Contractor, ER and the IEC	3.	Supervise the implementation of	3.	Ensure remedial measures are		
	3.	Discuss with the Contractor and IEC for remedial measures required		remedial measures		properly implemented		
	4.	If the complaint is related to the Project, conduct additional monitoring for checking mitigation effectiveness and report the findings and results to the IEC, ER and the Contractor						



Appendix F

Noise Monitoring Data



(Blank)



Appendix G

Complaint Log and Regulatory Compliance Proforma



Statistical Summary of Environmental Complaints

Reporting Period			
	Frequency	Cumulative	Complaint Nature
30 Aug 2018- 31 Aug 2018	0	0	N/A

Statistical Summary of Environmental Summons

Reporting Period	Environmental Summons Statistics						
	Frequency	Cumulative	Details				
30 Aug 2018- 31 Aug 2018	0	0	N/A				

Statistical Summary of Environmental Prosecution

Reporting Environmental Prosecution Statistics Period							
	Frequency	Cumulative	Details				
30 Aug 2018-	0	0	N/A				
31 Aug 2018							



Appendix H

Site Inspection Proforma



Quotation Ref. No. WQ/17/A071 Provision of Services of Independent Environmental Checker for Water Supplies Department - Contract No. 13/WSD/16 Mainlaying in Tseung Kwan O EM&A Environmental Site Audit Checklist			AP	Œ	WR
Date: 30 10 0 Client:	MK	Chai	h		
Weather: Sunny / Fine / Cloudy / (Rainy) Contractor:	Ton	y Tar	4		
Temperature: °C ET:	Ke	Vin 4			
Wind: Strong / Breeze / Lighty / Calm IEC:		ce la	<i>^</i> ~		
A. Air Quality	Yes	Follow- up	Not Obs.	N/A	Item no.
A1) Are dusty materials, such as excavated materials, building debris and construction materials, and exposed earth surface properly covered to prevent dust emission?		ď			<u> </u>
A2) Are screenings, enclosures, water spraying or vacuum cleaning devices provided to dusty construction works for dust suppression?	Ø				
A3) Are fumes or smoke emitting plants or construction activities shielded by a screen?	Ø				
A4) Are wheel-washing facilities with high-pressure water jets provided at all site exits?	П			Ø	
A5) Is wheel-washing provided to all vehicles leaving the site?					
A6) Are road sections near the site exit free from dusty materials?	Ø,				
A7) Are all main haul roads inside the site paved or sprayed with water to minimise dust emission during vehicle movement?	Ø				
A8) Are water spraying provided immediately prior to any loading or transfer of dusty materials?	Ø				
A9) Are covers provided to all dump trucks carrying dusty materials when entering and leaving the site?			Ø		
A10) Are the working areas for uprooting of trees, shrubs, or vegetation or the removal of boulders, poles, pillars sprayed with water to maintain the entire surface wet?				Ø	
A11) Is exposed earth properly treated within six months after the last construction activity on site?					
A12) Does the operation of plants on site free from dark smoke emission?	Ø				
A13) Are vehicles travelling at speed not exceeding 15km/hr within the site?	Ø				
A14) Are stock of more than 20 bags of cement or dry PFA covered or sheltered on top and 3 sides?		П		Ø	
A15) Are de-bagging, batching and mixing processes of bagged cement carried out in sheltered areas?					
A16) Are hoarding of at least 2.4m high provided along the site boundary adjoining areas accessible by the public?				Ø	
A17) Is open burning prohibited?	Ø				
B, Construction Noise	Yes	Follow- up	Not Obs.	N/A	Item no.
B1) Are quiet plants adopted on site?					VETERALANTA (CERA)
B2) Are the PMEs operating on site well-maintained to minimise the generation of excessive noise?	ď			Ū	
B3) Are plants throttled down or turned off when not in use?	ď				
B4) Are the plants known to emit noise strongly in one direction oriented to face away from NSRs?	Ø		П		

Page 1 of 5



Profor - C	otation Ref. No. WQ/17/A071 vision of Services of Independent Environmental Checker Water Supplies Department ontract No. 13/WSD/16 Mainlaying in Tseung Kwan O &A Environmental Site Audit Checklist			Aľ	Œ	WR
	Are movable barriers provided to screen NSRs from plant or noisy operations?					
B6)	Are silencers, mufflers and enclosures provided to plants?				Ø	
B7)	Are the hoods, cover panels and inspection hatches of PMEs closed during operation?					
B8)	Are purposely-built site hoarding constructed with appropriate materials provided along the site boundary?		П		Ø	
B9)	Are noisy operation properly scheduled to minimise exposure and cumulative impacts to nearby sensitive receivers?	Ø				
B10) Are valid noise emission label(s) affixed to all hand-held breakers operating on site?		□		Ø	
B11)	Are valid noise emission label(s) affixed to all air compressors operating on site?				Ø	
B12	Are construction noise permit(s) applied for percussive pilling works?				Ø	
B13)	Are construction noise permit(s) applied for general construction works during restricted hours?				ď	
B14)	Are valid construction noise permit(s) displayed at all vehicular exits?		D		Ø	
С. И	ater Quality	Yes	Follow- up	Not Obs.	N/A	Item no.
C1)	Is effluent discharge licence obtained for wastewater discharge from site?				\square	
C2)	Is effluent discharged according to the effluent discharge licence?				Ø	
C3)	Is wastewater discharge from site properly treated prior to discharge?				Ø	
	Are perimeter channels provided to intercept storm runoff from outside the site?	Ш	П	Ш	Z.	
C5)	Are sand/silt removal facilities such as sand/silt traps and sediment basins provided to remove sand/silt particles from runoff?	₫				
C6)	Is surface runoff diverted to sedimentation facilities?					(2)_
C7)	Is the drainage system properly maintained?					$_{\mathcal{U}}_{_}$
C8)	Are construction works carefully programmed to minimise soil excavation works during rainy seasons?	2			П	
C9)	Are exposed soil surface protected by paving as soon as possible to reduce the potential of soil erosion?	Ø				
C10)	Are temporary access roads protected by crushed gravel?					
C11)	Are exposed slope surfaces properly protected?				Ø	
C12)	Is trench excavation avoided in the wet season as far as practicable, or if necessary, backfilled in short sections after excavation?				Ø	
C13)	Are open stockpiles of construction materials on site covered by tarpaulin or similar fabric during rainstorms?	Ø				
C14)	Is runoff from wheel-washing facilities avoided?		i Da		Ø	
C15)	Is oil leakage or spillage prevented?	\square		П		
C16)	Are there any measures to prevent the release of oil and grease into the storm drainage system?	ď				
C17)	Are the oil interceptors / grease traps properly maintained?			4	astudiki Mi	W. 10220112222000
	Are debris and rubbish generated on site collected, handled and disposed of properly to avoid them entering the streams?		_ [<u>/</u>	Ò		0
	Are all fuel tanks and storage areas provided with locks and be sited on sealed areas, within bunds of capacity equal to 110% of the storage capacity of the largest tank?			Ø		

Page 2 of 5



Quotation Ref. No. WQ/17/A071 Provision of Services of Independent Environmental Checker for Water Supplies Department — Contract No. 13/WSD/16 Mainlaying in Tseung Kwan O EM&A Environmental Site Audit Checklist			AN	E	WR
C20) Are open storm water drains and culverts near the works area covered to block the entrance of large debris and refuse?	П	ъ			(2)
C21) Are sufficient chemical toilets provided on site to handle sewage from construction work force?					
C22) Are sewage disposal and toilet maintenance of the portable chemical toilets provided by the licensed contractors?	Ø		П		
C23) Is concrete washing water properly collected and treated prior to discharge?	Ø				
D. Chemicals and Waste Management	Yes	Follow-	Not Obs.	N/A	Item
D1) Is a trip-ticket system implemented to monitor the disposal of C&D and solid wastes at public filling facilities and landfills?					
D2) Is a recording system implemented to record the amount of wastes generated, recycled and disposed of?	Ø	П			
D3) Is the Contractor registered as a chemical waste producer?					
D4) Are chemical waste separated from other waste and collected by a licensed chemical waste collector?	◩				
D5) Are trip tickets for chemical waste disposal available for inspection?					
D6) Is chemical waste reused and recycled on site as far as practicable?			a		
D7) Are all containers for chemical waste properly labelled?					
D8) Is chemical waste storage area used solely for storage of chemical waste and properly labelled?			Ø	П	
D9) Are incompatible chemical wastes stored in different areas?					
D10) Is the chemical waste storage area enclosed on at least 3 sides and adequately ventilated?			Ø	П	
D11) Is an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or of 20% by volume of the chemical waste stored in that area, whichever is the greatest, provided?			Q		-
D12) Are a routine cleaning and maintenance programme implemented for drainage systems, sump pits and oil interceptors?		◪			<u>() </u>
D13) Are sufficient general refuse disposal/collection points provided on site?					
D14) Is general refuse disposed of properly and regularly?					
D15) Are appropriate measures adopted to minimise windblown litter and dust during transportation of waste?					
D16) Are individual collectors for aluminium cans, plastic bottles and packaging material and office paper provided to encourage waste segregation?	Ø				<u> </u>
D17) Are C&D wastes sorted on site?					
D18) Are C&D wastes disposed of properly?	Ø				
D19) Are unused C&D materials or chemicals recycled or reused to reduce the quantity of waste?					
D20) Are public fill and C&D waste reuse on site as far as practicable to avoid disposal off-site?	D				
D21) Are the construction materials stored properly to minimise the potential for damage or contamination?					
D22) Is a dumping license obtained to deliver public fill to public filling areas?					

Page 3 of 5



Quotation Ref. No. WQ/17/A071
Provision of Services of Independent Environmental Checker for Water Supplies Department

- Contract No. 13/WSD/16 Mainlaying in Tseung Kwan O EM&A Environmental Site Audit Checklist

ANEWR

<u>E. L</u>	andscape and Visual	Yes	Follow- up	Not Obs.	N/A	Item no.
E1)	Is site hoarding provided? Are vegetation disturbance minimised or soil surface protected to reduce	u wasilika	u osamina			**************************************
152)	potential soil erosion?					
E3)	Is construction light oriented away from the sensitive receivers?	1				
E4)	Is grass hydroseeding provided to slopes as soon as the completion of works?				Ø	
E5)	Are damages to trees outside site boundary due to construction works avoided?					
E6)	Is excavation works carried out manually instead of machinery operation within $2.5m$ vicinity of any preserved trees?				Ø	
E7)	Are the retained and transplanted tree(s) properly protected and in good condition?				Ø	
E8)	Are surgery works carried out for damaged trees?				Q	
<u>F. E.</u>	cology	Yes	Follow-	Not Obs.	N/A	Item
<i>E E</i> .	Is site runoff properly treated to prevent any silty runoff?	Yes	Follow- up		N/A	Item no.
F1)		Yes			n/a	
F1) F2)	Is site runoff properly treated to prevent any silty runoff?	Yes		Obs.	N/A	
F1) F2) F3)	Is site runoff properly treated to prevent any silty runoff? Are silt trap installed and well-maintained?	Yes		Obs.	N/A	
F1) F2) F3)	Is site runoff properly treated to prevent any silty runoff? Are silt trap installed and well-maintained? Are stockpiles properly covered to avoid generating silty runoff? Are construction works restricted to works areas which are clearly defined?	Yes		Obs.	N/A	

Page 4 of 5



Quotation Ref. No. WQ/17/A071 Provision of Services of Independent Environmental Checker for Water Supplies Department — Contract No. 13/WSD/16 Mainlaying in Tseung Kwan O EM&A Environmental Site Audit Checklist

ANEWR.

Remarks

Observations

- O Construction debrir war observed scarteredly next to the gullies at the under-construction sile office. The Centractor was requested to clear up the construction debris to avoid them from entering public drains
- D) The gullier next to the construction area (for site office) were not properly covered or protected. There is no clear diversion of site ranoff on-site. The contractor was requested to provide southags along the construction work boundary and to dwent site runoff to wastewater collection facility for containent and on-site reuse.
- 3) The Contractor was to post environmental permit at all well-ular site entrana.

Client Engineer IEC ET Contractor

Nor Jan (Nic Jahn) (Tony TANG)
30/10/10

Page 5 of 5



Appendix I

Proactive Environmental Protection Proforma



Proactive Environmental Protection for the Next Reporting Month

Reporting Period	Activity	Major Environmental Impact	Environmental Mitigation Measure
	- Erection of the site accommodation (Portion G of the Site)	- Waste generation from construction activities	 Sorting and storage of general refuse and construction waste
30 Aug 2018- 31 Aug 2018	- Mainlaying by open trench method	 Construction dust and noise generation from open trenching Waste generation from construction activities 	 Dust suppression by regular wetting and water spraying in the open trench area Reduction of noise from equipment and machinery on-site Sorting and storage of general refuse and construction waste



Appendix J

Impact Monitoring Schedule of Next Reporting Month



(Blank)
