



Water Supplies Department
New Works Branch
Construction Division
11 Tai Yip Lane
Kowloon Bay
Kowloon
Hong Kong

Your reference:

Our reference: HKWSD201/50/105570

Date: 19 February 2019

Attention: Mr Y M Chan

BY POST

Quotation No.: WQ/17/A071

Independent Environmental Checker for Water Supplies Department

- Proposed Desalination Plant in TKO Area 137 for Contract No. 13/WSD/16

Verification of 1st Quarterly EM&A Report for August to October 2018

We refer to emails of 26 November 2018, 28 January 2019, 18 and 19 February 2019 attaching 1st Quarterly EM&A Report for August to October 2018 for the captioned project prepared by the ET.

We have no further comment and hereby verify the 1st Quarterly EM&A Report for August to October 2018) in accordance with Clause 3.5 of the Environmental Permit no. EP-503/2015/A.

Should you have any queries regarding the above, please do not hesitate to contact the undersigned or our Mr Jacky Chow on 2618 2831.

Yours faithfully
ANewR CONSULTING LIMITED

Nic Lam
Independent Environmental Checker

LHHN/CTKJ/csym




Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

**1st Quarterly EM&A Report
For August to October 2018**

February 2019
(Rev. 0)

	Prepared by:	Certified by:
Name	Nelson Tsui	Jacky Leung
Position	Environmental Team	Environmental Team Leader
Signature		
Date:	19 February, 2019	19 February, 2019

Revision History

0	1 st Submission	19 February,2019
Rev.	DESCRIPTION OF MODIFICATION	DATE

CONTENT

1. NOISE MONITORING
2. WASTE MANAGEMENT
3. SUMMARY OF MONITORING EXCEEDANCE, COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTIONS
4. EM&A SITE INSPECTION
5. LANDFILL GAS MONITORING
6. CONCLUSION AND RECOMMENDATIONS

Appendix A	Overview of Mainlaying in TKO
Appendix B	Project Organization Chart
Appendix C	Construction Programme
Appendix D	Layout of Major Construction Works Undertaken during the Reporting Quarter
Appendix E	Summary of Implementation Status of Environmental Mitigation
Appendix F	Action and Limit Level for Noise and Landfill Gas
Appendix G	Landfill Gas Monitoring Results
Appendix H	Complaint Log and Regulatory Compliance Proforma

EXECUTIVE SUMMARY

- A1. Penta-Ocean - Concentric Joint Venture (POCJV) is contracted to carry out the Mainlaying in Tseung Kwan O under Contract No. 13/WSD/16 (hereinafter known as “the Project”).
- A2. In accordance with the Environmental Monitoring and Audit (EM&A) Manual for the Project, EM&A works should be carried out by Environmental Team (ET), Acuity Sustainability Consulting Limited (ASCL), during the construction phase of the Project.
- A3. The construction works of Mainlaying in Tseung Kwan O commenced on 30 August, 2018. This is the 1st quarterly Environmental Monitoring and Audit (EM&A) summary Report prepared by ASCL. This report presenting the EM&A works carried out during the period of 30 August 2018 to 31 October 2018.
- A4. A summary of the monitoring activities undertaken in this reporting period is listed below:

Monitoring Activities	Frequency
Daytime Noise monitoring	0 times
Landfill Gas Monitoring	210 times
Environmental Site Inspection	10 times

- A5. No project-related exceedance of the Action/Limit Level was recorded during the reporting quarter.
- A6. No noise monitoring was conducted in the reporting quarter since there are no projected-related construction activities undertaken within a radius of 300m from the monitoring locations.
- A7. No exceedance of landfill gas monitoring was recorded during the reporting quarter.
- A8. No summons/ prosecutions were received in the reporting quarter.
- A9. There were no changes to be reported that may affect the on-going EM&A programme.

1 Basic Project Information

1.1 Background

- 1.1.1 The proposed Desalination Plant at Tseung Kwan O (DPTKO) will produce potable water with an initial capacity of 135 million liters per day (MLD), expandable to an ultimate capacity of 270 MLD in the future to provide a secure and alternative fresh water resource complying with the World Health Organization (WHO) standards. The plant will adopt the Seawater Reverse Osmosis (SWRO) technology, which dominates the market due to its reliability and progressive reduction in cost as the technology advances.
- 1.1.2 Pursuant to the Environmental Impact Assessment Ordinance (EIAO), the Director of Environmental Protection granted the Variation of Environmental Permit (No. EP-503/2015/A) to Water Supplies Department (WSD) for the Project on 26 January 2018.
- 1.1.3 The scope of the Contract may be considered in brief, to consist of the laying of about 10km long 1200mm diameter fresh water mains and the associated works along the alignment of the Project as shown with the overall view in **Appendix A**.

1.2 The Reporting Scope

- 1.2.1 This is the 1st Quarterly EM&A Report for the Project which summarizes the key findings of the EM&A programme during the reporting period from 30 August 2018 to 31 October 2018.

1.3 Project Organization

- 1.3.1 The Project Organization structure for Construction Phase is presented in **Appendix B**.
- 1.3.2 Contact details of the key personnel are presented in **Table 1.1** below:

Table 1.1 Contact Details of Key Personnel

Party	Position	Name	Telephone no.
Penta-Ocean -Concentric Joint Venture	Environmental Officer	Tony Tang	9433-2628
Acuity Sustainability Consulting Limited	Environmental Team Leader	Jacky Leung	2698-6833
ANewR Limited Consulting	Independent Environmental Checker	Nic Lam	2618-2831

1.4 Summary of Construction Works

1.4.1 Details of the major construction works undertaken in this reporting quarter are shown in **Table 1.2** and **Appendix D**. The construction programme is presented in **Appendix C**.

**Table 1.2 Summary of the Construction Works Undertaken during
the Reporting quarter**

Location	Works Conducted in the reporting quarter
Portion A, B, C & D of the Project Site	Initial joint survey with WSD
Portion F & G of the Project Site	- Erection of fencing and gates - Site accommodation erection and internal fitting out
Portion J of the Project Site	- Continue utilities checking and detection before road works. - Ground Investigation works at 17 no. of trial pits done at Wan Po Road (CH. A3+50, 5+30, 13+70, 15+40, 16+30, 18+50, 19+00, 22+70, 41+10), Po Hong Road (CH. A44+80, 51+80, 63+60 and 69+60), Ling Hong Road (CH. A55+50 and 56+00), Po Shun Road (CH.A 54+30) and Wan Po Road (CH. A37+25).

1.5 Summary of Environmental Status

1.5.1 A summary of the valid permits, licences, and /or notifications on environmental protection for this Project is presented in **Table 1.3**

Table 1.3 Summary of the Status of Valid Environmental Licence, Notification, Permit and Documentations

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
Variation of Environmental Permit	EP no.: EP-503/2015/A	Throughout the Contract	-
Notification of Construction Works under the Air Pollution Control (Construction Dust) Regulation (Form NA)	Ref no.: 423775	Throughout the Contract	-
Chemical Waste Producer Registration	WPN: 5213-839-P3287-01	Throughout the Contract	-
Billing Account for Disposal of Construction Waste	A/C no.: 7029491	Throughout the Contract	-

1.5.2 The status for all environmental aspects is presented **Table 1.4**.

Table 1.4 Summary of Status for Key Environmental Aspects under the EM&A Manual

Parameters	Status
Noise	
Baseline Monitoring	The baseline noise monitoring result has been reported in Baseline Monitoring Report and submitted to EPD under VEP Condition 3.4
Impact Monitoring	No impact monitoring for noise impact was conducted in the reporting quarter due to the over distant monitoring station from the works location, where they were farther than 1 km from the closest monitoring station NSR4 to the works location.
Waste Management	
Mitigation Measures in Waste Monitoring Plan	On-going
Landfill Gas Monitoring	
Mitigation Measures	On-going
Monitoring	On-going
Environmental Audit	
Site Inspection	On-going

1.5.3 Other than the EM&A works by ET, regular environmental management meetings were conducted in order to enhance environmental awareness and closely monitor the environmental performance of the contractors.

1.5.4 The EM&A programme has been implemented in accordance with the recommendations presented in the approved EIA Report and the EM&A Manual. A summary of implementation status of the environmental mitigation measures for the construction phase of the Project during the reporting period is provided in **Appendix E**.

2 Noise Monitoring

2.1.1 Referring to EM&A manual Section 4.1.2, the impact noise monitoring should be carried out at all the designated monitoring stations when there are project-related construction activities undertaken within a radius of 300m from the monitoring stations. No impact monitoring for noise impact was conducted in the reporting quarter due to the over distant monitoring station from the works location, where they were farther than 1 km from the closest monitoring station NSR4 to the works location.

2.2 Action and Limit Level is provided in **Appendix F**.

2.3 No notification of summons and prosecution related to noise was received in the reporting quarter.

3 Waste Management

3.1.1 Total of 0.599 m³ of inert C&D materials was collected to the Fill Bank, 0.092 m³ C&D waste and general refuse were disposed of at Landfill, 0.194 tonnes of paper/ cardboard packaging was recycled and 0 tonnes chemical waste collected by licensed contractor for disposal in the reporting quarter.

4 Summary of Monitoring Exceedance, Complaints, Notification of Summons and Prosecutions

- 4.1 No monitoring exceedance, notification of summons and prosecution was received in the reporting quarter.

5 EM&A Site Inspection

- 5.1 Site inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures under the Contract. In the reporting quarter, site inspections were carried out 30 August, 4,13,20,27 September, 5,11,18,25,30 October 2018 at the site portions list in **Table 5.1** below.

Table 5.1 Site Inspection Record

Date	Inspected Site Portion	Time
30 August, 4,13,20,27 September, 5,11,18,25,30 October 2018	Portion J, F & G of the Site	10:00am - 11:00am

- 5.2 Three joint site inspection with IEC was carried out on 30 August ,27 September and 30 October , 2018.
- 5.3 Minor deficiencies were observed during weekly site inspection. Key observations during the site inspections are summarized in **Table 5.2**.

Table 5.2 Site Observations

Date	Environmental Observations	Follow-up Status
30 Aug 2018	<u>Observation(s) and Recommendation(s)</u> 1. At the under-construction site office, construction debris was observed scatteredly next to the gullies. 2. The gullies next to the construction area for site office were not properly covered and there is no clear diversion of site runoff on-site. 3. The contractor was request to post Environmental Permit at all vehicle site entrance. 4. Used paint drums were observed inside the site area and it should be placed inside lockable chemical store on site. 5. Stagnant water were found inside the site office and it should be diverted to the waste water treatment tank.	1. Construction debris were cleaned up by the contractor. 2. Sandbags were placed to protect the gullies. 3. The Environmental Permit was posted by the contractor at the required work area. 4. The paint drum had been removed. 5. Pond of water was spread by the contractor to facilitate evaporation.
4 Sep 2018	No observations	-
13 Sep 2018	No observations	-
20 Sep 2018	No observations	-
27 Sep 2018	1. Site area near TVB City- The road section appeared dry and dusty. The contractor was requested to clean up the dust/provide with water spray. The contractor was also	1. The road was cleaned up and sandbags was placed under water horses. 2. Waste was cleaned up on

Date	Environmental Observations	Follow-up Status
	requested to provide sandbags under water hoses before any water spray. 2. Site areas near TVB city and Next Media Co. Ltd.- There are scatter waste on-site. The contractor was requested to remove them.	site.
5 Oct 2018	No observations	-
11 Oct 2018	No observations	-
18 Oct 2018	No observations	-
25 Oct 2018	No observations	-
30 Oct 2018	No observations	-

- 5.4 According to the EIA Study Report, Environmental Permit, contract documents and EM&A Manual, the mitigation measures detailed in the documents are implemented as much as practical during the reporting quarter. An updated Implementation Status of Environmental Mitigation Measures (EMIS) is provided in **Appendix E**.

6 Landfill gas monitoring

- 6.1 In accordance with Section 11 of the EM&A Manual, monitoring of landfill gas is required for construction works within the 250m Consultation Zone. Part of the desalination plant and the indicative area of natural slope mitigation works fall within the SENT Landfill Extension Consultation Zone; and part of the 1,200 mm diameter fresh water mains along Wan Po Road falls within the SENT Landfill and SENT Landfill Extension Consultation Zones, TKO Stage II/III Restored Landfill and TKO Stage I Restored Landfill Consultation Zones. Monitoring conducted in September and October 2018.
- 6.2 Monitoring of oxygen, methane and carbon dioxide was performed for excavations at 1m depth or more within the consultation Zone. In this reporting quarter, 210 times of monitoring was recorded. Action and Limit Level is provided in **Appendix F**
- 6.3 Monitoring Equipment used in the reporting quarter are summarised in Table 6.1

Table 6.1 Landfill Gas Monitoring Equipment

Equipment	Model and Make	Calibration Expiry Date
Gas Detector	Industrial Scientific Corporation M40	28 August 2019
Gas Detector	RAE System QRAE3	17 October 2019

- 6.4 In the reporting quarter, landfill gas monitoring was carried out by the Registered Safety Officer by the Contractor at the excavation locations for 210 times. The monitoring results and Action Level are provided in **Appendix G** and **Appendix F** respectively.

7 Conclusion and Recommendations


- 7.1 This is the 1st quarterly Environmental Monitoring and Audit (EM&A) summary Report prepared by ASCL. This report presenting the EM&A works carried out during the period of 30 August 2018 to 31 October 2018 in accordance with the EM&A Manual and the requirement under EP-503/2015/A.

- 7.2 No noise monitoring was conducted during the reporting period due to the over distant monitoring station from the works location.
- 7.3 No landfill gas exceedance was recorded in the reporting quarter.
- 7.4 No project-related exceedance of the Action Level was recorded during the reporting period.
- 7.5 Weekly environmental site inspection was conducted during the reporting quarter. Minor deficiencies were observed during site inspection and were rectified. The environmental performance of the Project was therefore considered satisfactory.
- 7.6 According to the environmental site inspections performed in the reporting quarter, the Contractor is reminded to pay attention on maintaining site tidiness and proper materials storage.
- 7.7 No environmental complaint was received in the reporting period.
- 7.8 No notification of summons or prosecution was received since commencement of the Contract.
- 7.9 The ET will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures.
- 7.10 Statistics on complaints and regulatory compliance are summarized in **Appendix H**.

Appendix A

Overview of Mainlaying in TKO


Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018

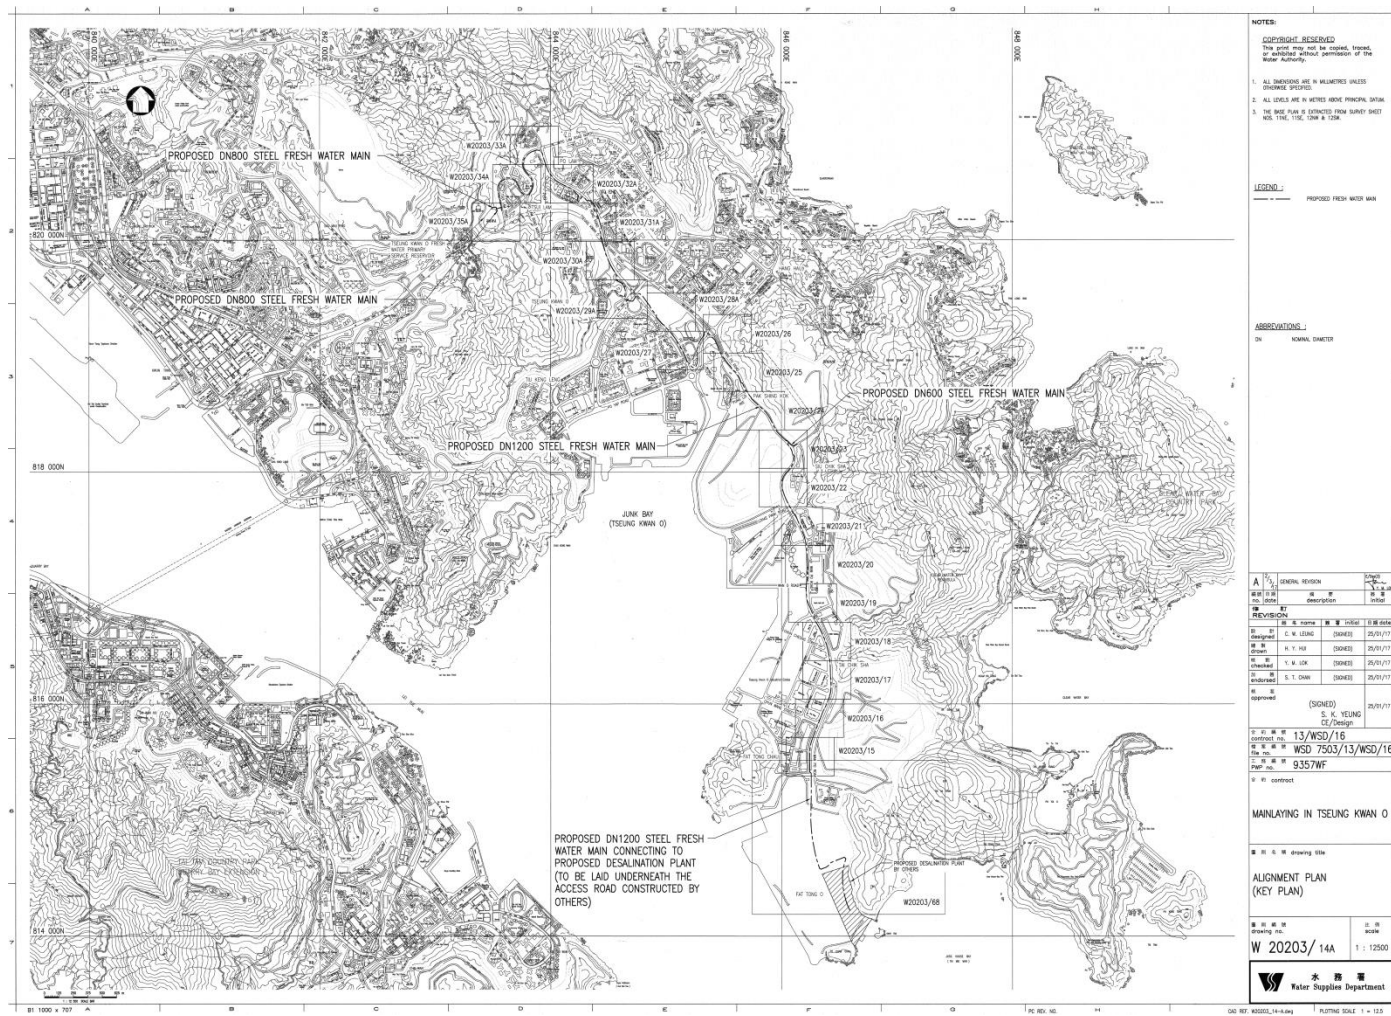

Appendix B

Project Organization Chart

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018

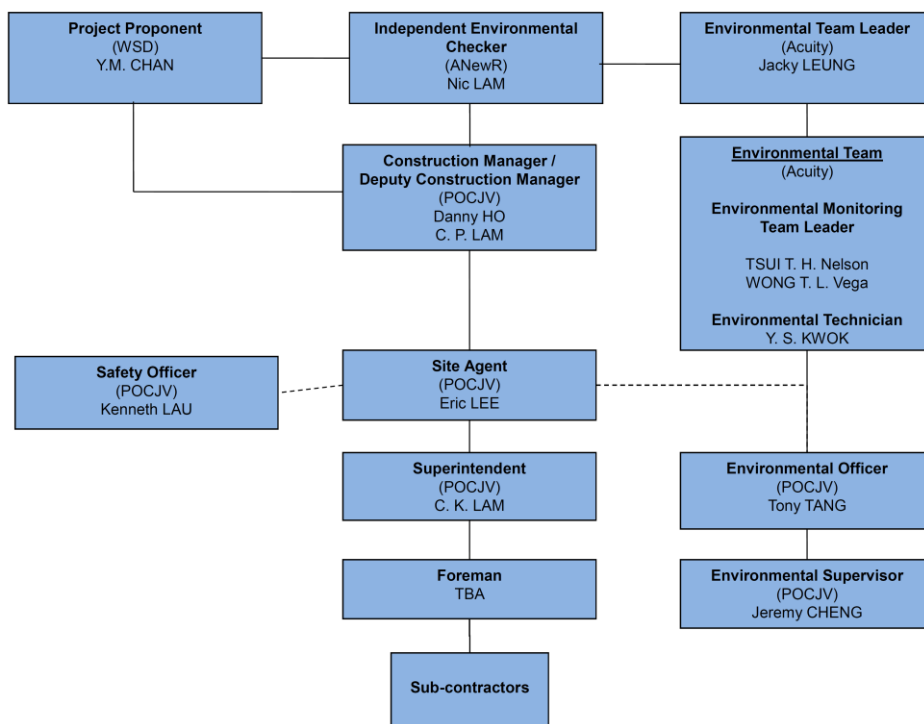

Appendix C

Construction Programme

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



13/WSD/16 - Mainlaying in Tseung Kwan O

Outline Construction Programme (As on 31 Aug 2018)

YEAR	LOCATION		FROM	TO	2018												2019												2020												2021																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
MONTH	PJ-ID	ROAD			1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							

Commencement of works at CHA 720 on 30 Aug 2018.


*TKOFWPSR - Tseung Kwan O Fresh Water Primary Service Reservoir

**Remaining 1581m within TKO137 with site possession from Nov 2019

Appendix D

Layout of Major Construction Works Undertaken during the Reporting Quarter

ACUITY
SUSTAINABILITY
CONSULTING LIMITED

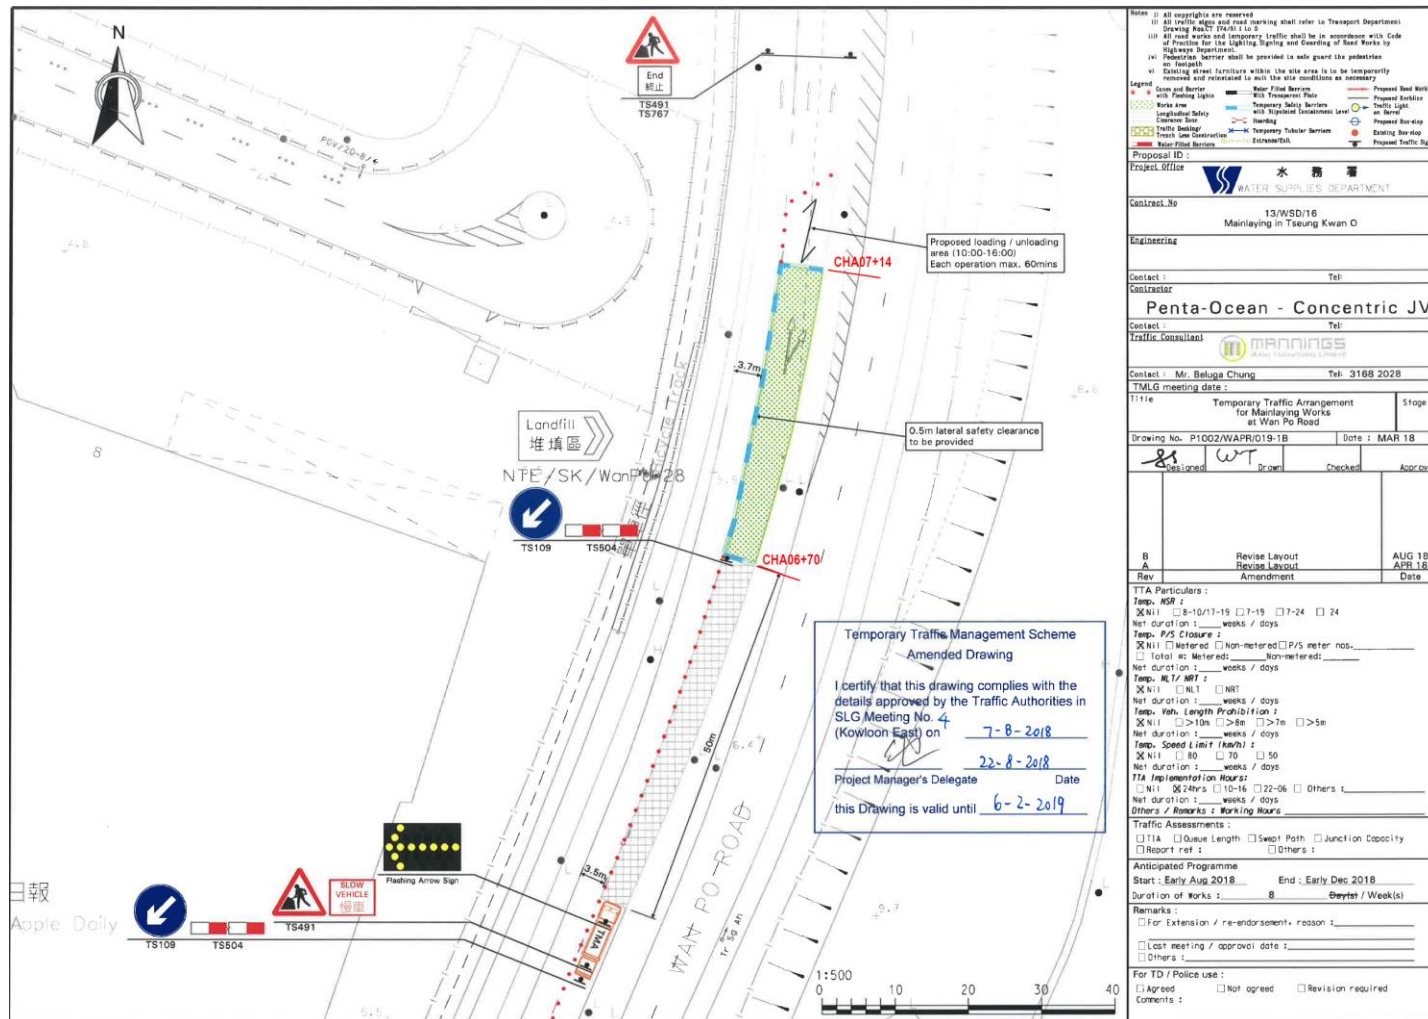

Appendix E

Summary of Implementation Status of Environmental Mitigation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
Air Quality								
S4.8.1	Impervious dust screen or sheeting will be provided to enclose scaffolding from the ground floor level of building for construction of superstructure of the new buildings.	Land site/ During Construction	Contractor(s)		✓		N/A	Air Pollution Control (Construction Dust)
S4.8.1	Impervious sheet will be provided for skip hoist for material transport.	Land site/ During Construction, particularly dry season	Contractor(s)		✓		Implemented	
S4.8.1	The area where dusty work takes place should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after dusty activities as far as practicable.	Land site/ During Construction	Contractor(s)		✓		Implemented	
S4.8.1	All dusty materials should be sprayed with water or a dust suppression chemical immediately prior to any loading, unloading or transfer operation.	Land site/ During Construction	Contractor(s)		✓		Implemented	
S4.8.1	Dropping heights for excavated materials should be controlled to a practical height to minimise the fugitive dust arising from unloading.	Land site/ During Construction	Contractor(s)		✓		Implemented	
S4.8.1	During transportation by truck, materials should not be loaded to a level higher than the side and tail boards, and should be dampened or covered before transport.	Land site/ During Construction	Contractor(s)		✓		Implemented	
S4.8.1	Wheel washing device should be provided at the exits of the work sites. Immediately before leaving a construction site, every vehicle shall be washed to remove any dusty material from its body and wheels as far as practicable.	Land site/ During Construction	Contractor(s)		✓		Implemented	

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S4.8.1	Road sections between vehicle-wash areas and vehicular entrance will be paved.	Land site/ During Construction	Contractor(s)		✓		Implemented	
S4.8.1	Hoarding of not less than 2.4m high from ground level will be provided along the length of the Project Site boundary.	Land site/ During construction	Contractor(s)	✓	✓		Implemented	
S4.8.1	Haul roads will be kept clear of dusty materials and will be sprayed with water so as to maintain the entire road surface wet at all times.	Land site/ During construction	Contractor(s)		✓		Implemented	
S4.8.1	Temporary stockpiles of dusty materials will be either covered entirely by impervious sheets or sprayed with water to maintain the entire surface wet all the time.	Land site/ During construction	Contractor(s)		✓		Implemented	
S4.8.1	Stockpiles of more than 20 bags of cement, dry pulverised fuel ash and dusty construction materials will be covered entirely by impervious sheeting sheltered on top and 3-sides.	Land site/ During construction	Contractor(s)		✓		N/A	
S4.8.1	All exposed areas will be kept wet always to minimise dust emission.	Land site/ During construction	Contractor(s)		✓		N/A	
S4.8.1	Ultra-low-sulphur diesel (ULSD) will be used for all construction plant on-site, as defined as diesel fuel containing not more than 0.005% sulphur by weight) as stipulated in Environment, Transport and Works Bureau Technical Circular (ETWB-TC(W)) No 19/2005 on Environmental Management on Construction Sites.	Land site/ During construction/ During Operation	Contractor(s)		✓	✓	Implemented	Environment, Transport and Works Bureau Technical Circular (ETWB- TC(W)) No 19/2005 on Environmental Management on Construction Sites
S4.8.1	The engine of the construction equipment during idling will be switched off.	Land site/ During construction	Contractor(s)		✓		Implemented	

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S4.8.1	Concrete batching plant will be required on site. control measures recommended in the Guidance Note on a Best Practicable Means for Cement Works (Concrete Batching Plant) (BPM 3/2 (93)) will be implemented. The control measures recommended in the Guidance Note on a Best Practicable Means for Cement Works (Concrete Batching Plant) (BPM 3/2 (93)) will be implemented.	Land site/ During construction	Contractor(s)		✓		N/A	Guidance Note on a Best
S4.8.1	Regular maintenance of construction equipment deployed on-site will be conducted to prevent black smoke emission.	Land site/ During construction	Contractor(s)		✓		Implemented	
S4.10	To ensure proper implementation of the recommended dust mitigation measures and good construction site practices during the construction phase, environmental site audits on weekly basis is recommended throughout the construction period.	Land site/ During construction	Contractor(s)/ Environmental Team (ET) & Independent Environmental Checker (IEC)		✓		Implemented	

Note: D – Design stage C – Construction O – Operation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
	Noise							
S5.7	Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction phase.	All area/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Silencers or mufflers on construction equipment will be utilised and will be properly maintained during the construction phase.	Noise control/ During construction	Contractor(s)		✓		N/A	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Mobile plant, if any, will be sited as far away from NSRs as possible.	Noise control/ During construction	Contractor(s)		✓		N/A	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum.	Noise control/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Plants known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.	Noise control/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities.	Noise control/ During construction	Contractor(s)		✓		N/A	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Use of Quite Powered Mechanical Equipment (QPME).	Noise control/ During	Contractor(s)		✓		N/A	A Practical

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
		construction						Guide for the Reduction of Noise from Construction Works,
S5.7	Movable noise barriers of 3m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater than its height. The noise barrier material should have a superficial surface density of at least 7 kg m ⁻² and have no openings or gaps.	Noise control/ During construction	Contractor(s)		✓		N/A	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	The noise insulating sheet should be deployed such that there would be no opening or gaps on the joints.	Noise control/ During construction	Contractor(s)		✓		N/A	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Construction activities (e.g. excavation/shoring, reinstatement (asphalt), and pipe jacking) will be planned and carried out in sequence, such that items of PME proposed for these activities will not be operated simultaneously.	Noise control/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works
S5.7	PMEs will not be used at the works areas near educational institutions with residual impact (ie the “influence area” within a radius of 40m) during school hours in order to reduce impact to the educational institutions.	Noise control / During construction	Contractor(s)		✓		N/A	A Practical Guide for the Reduction of Noise from Construction Works
S5.7	Noise enclosures or acoustic sheds would be used to cover stationary PME such as generators. Portable/Movable noise enclosure made of material with superficial surface density of at least 7 kg m ⁻² may be used for screening the noise from operation of the saw/groover, concrete.	Noise control/ Pre-construction/ During construction	Contractor(s)	✓	✓		Implemented	
S5.9	Sawcutting pavement, breaking up of pavement,	Noise control/ Pre-	Contractor(s)	✓	✓		N/A	

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
	excavation /shoring, pipe laying, backfilling, reinstatement (concrete) and pipe jacking shall be scheduled outside the examination period.	construction/ During construction						
S5.9	In view the duration of noise exceedance at Creative Secondary School, PLK Laws Foundation College, TKO Kei Tak Primary School and School of Continuing and Professional Studies-CUHK is limited to 8 weeks, the construction work in the influence areas near the four schools shall be scheduled during long school holidays (eg summer holiday, Easter holiday or Christmas holiday, etc) as far as practicable. Scheduling the construction work for the four schools.	Noise control/ Pre-construction/ During construction	Contractor(s)	✓	✓		N/A	
S5.10	A noise monitoring programme shall be implemented for the construction phase.	Designated monitoring stations as defined in EM&A Manual/During construction phase	Environmental Team (ET)		✓		N/A	
S5.10	The effectiveness of on-site control measures could also be evaluated through the regular site audits.	All facilities/ During construction	Contractor(s)/ Environmental Team (ET) & Independent Environmental Checker (IEC)		✓		Implemented	-

Note: D – Design stage C – Construction O – Operation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementatio n Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
Water Quality								
S6.9	Dredged marine sediment will be disposed of in a gazetted marine disposal area in accordance with marine dumping permit conditions of the Dumping at Sea Ordinance (DASO).	Marine Dredging/ During construction	Contractor(s)		✓		N/A	Dumping at Sea Ordinance (DASO)
S6.9	Disposal vessels will be fitted with tight bottom seals in order to prevent leakage of material during transport.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	Barges will be filled to a level, which ensures that material does not spill over during transport to the disposal site and that adequate freeboard is maintained to ensure that the decks are not washed by wave action.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	After dredging, any excess materials will be cleaned from decks and exposed fittings before the vessel is moved from the dredging area.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	All vessels should be well maintained and inspected before use to limit any potential discharges to the marine environment.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	All vessels must have a clean ballast system.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	No discharge of sewage/grey wastewater should be allowed. Waste water from potentially contaminated area on working vessels should be minimized and collected. These kinds of wastewater should be brought back to port and discharged at appropriate collection and treatment system.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	No soil waste is allowed to be disposed overboard.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementatio n Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S6.9	Silt removal facilities such as silt traps or sedimentation facilities will be provided to remove silt particles from runoff to meet the requirements of the TM standard under the WPCO. The design of silt removal facilities will be based on the guidelines provided in ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented	ProPECC PN 1/94 TM Standard under the WPCO
S6.9	Earthworks to form the final surfaces will be followed up with surface protection and drainage works to prevent erosion caused by rainstorms.	Land site & drainage/ During construction	Contractor(s)		✓		N/A	-
S6.9	Appropriate surface drainage will be designed and provided where necessary.	Land site & drainage/ During construction	Contractor(s)		✓		N/A	-
S6.9	The precautions to be taken at any time of year when rainstorms are likely together with the actions to be taken when a rainstorm is imminent or forecasted and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented	ProPECC PN 1/94
S6.9	Oil interceptors will be provided in the drainage system where necessary and regularly emptied to prevent the release of oil and grease into the storm water drainage system after accidental spillages.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented, rectified after observation	-
S6.9	Temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge, if any, will be adequately designed for the controlled release of storm flows.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented	-

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementatio n Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S6.9	The temporary diverted drainage, if any, will be reinstated to the original condition when the construction work has finished or when the temporary diversion is no longer required.	Land site & drainage/ During construction	Contractor(s)		✓		N/A	-
S6.9	Appropriate numbers of portable toilets shall be provided by a licensed contractor to serve the construction workers over the construction site to prevent direct disposal of sewage into the water environment.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented	-
S6.9 and S6.12	The sterilization water should be dechlorinated with total residual chlorine (TRC) level below 1 mg/L before discharge to public sewer. In situ testing of TRC should also be conducted for the discharge of chlorinated water for pipeline disinfection to ensure sufficient dechlorination before discharge to public sewer.	Sterilization of water mains prior to commissioning	Contractor(s)		✓	✓	N/A	Technical Memorandum for Effluents Discharged into Drainage and Sewerage Systems Inland and Coastal Waters
S6.9	The cleaning and flushing water should also be treated and desilted to the relevant discharge requirement stipulated in TM-DSS before discharging.	Sterilization of water mains prior to commissioning	Contractor(s)		✓	✓	N/A	Technical Memorandum for Effluents Discharged into Drainage and Sewerage Systems Inland and Coastal Waters
S6.9	Site drainage should be well maintained and good construction practices should be observed to ensure that oil, fuels, solvents and other chemicals are managed, stored and handled properly and do not enter the nearby water streams.	Land site & drainage/ During construction/ During operation	Contractor(s)		✓	✓	Implemented, rectified after observation	-
S6.12	Regular site inspections will be carried out in order to confirm that regulatory requirements are being met and that contractors are implementing the standard site practice and mitigation measures as proposed to reduce potential impacts to water quality.	During construction	Contractor(s)/ Environmental Team (ET) & Independent Environmental Checker (IEC)		✓		Implemented	-

Note: D – Design stage C – Construction O – Operation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
Waste Management								
S8.5	Nomination of approved personnel to be responsible for standard site practices, arrangements for collection and effective disposal to an appropriate facility of all wastes generated at the site.	Contract mobilisation/ During construction	Contractor(s)		✓		Implemented	-
S8.5	Training of site personnel in proper waste management and chemical handling procedures. Training will be provided to workers on the concepts of site cleanliness and appropriate waste management procedures, including waste reduction, reuse and recycling at the beginning of the construction works.	Contract mobilisation/ During construction	Contractor(s)		✓		Implemented	-
S8.5	Provision of sufficient waste disposal points and regular collection for disposal.	All area/ During construction/ During operation	Contractor(s)		✓	✓	Implemented	DEVB TC(W) No. 8/2010, Enhanced Specification for Site Cleanliness and Tidiness.
S8.5	Appropriate measures to reduce windblown litter and dust transportation of waste by either covering trucks or by transporting wastes in enclosed containers.	All area/ During construction	Contractor(s)		✓		Implemented	DEVB TC(W) No. 8/2010, Enhanced Specification for Site Cleanliness and Tidiness.
S8.5	A waste management plan (WMP) as stated in the “ETWB TC(W) No. 19/2005, Environmental Management on Construction Sites” for the amount of waste generated, recycled and disposed of (including the disposal sites) will be established and implemented during the construction phase as part of the Environmental Management Plan (EMP). The Contractor will be required to prepare the EMP and submits it to the Architect/ Engineer under the Contract for approval prior to implementation.	All area/ During construction	Contractor(s)		✓		Implemented	ETWB TC(W) No. 19/2005, Environmental Management on Construction Sites
S8.5	Separation of chemical wastes for special handling and appropriate treatment at the Chemical Waste Treatment Centre at Tsing Yi.	All area/ During construction	Contractor(s)		✓		Implemented	Chapters 2 & 3 Code of Practice on the Packaging, Labelling, Storage of Chemical Wastes published under the Waste Disposal

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
								Ordinance (Cap 354), Section 35
S8.5	Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors.	Land site/ During construction	Contractor(s)		✓		Implemented	Waste Disposal Ordinance (Cap 354)
S8.5	A recording system for the amount of wastes generated/ recycled and disposal sites. The trip- ticket system will be included as one of the contractual requirements and implemented by the contractor(s).	Land site/ During construction	Contractor(s)		✓		Implemented	DEVB TC(W) No. 6/2010, Trip Ticket System for Disposal of Construction & Demolition Materials
S8.5	Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of material and their proper disposal.	Land site/ During construction/ During operation	Contractor(s)		✓		Implemented, rectified after observation	WBTC 32/92, The Use of Tropical Hard Wood on Construction Site
S8.5	Encourage collection of aluminium cans and waste paper by individual collectors during construction with separate labelled bins provided to segregate these wastes from other general refuse by the workforce.	Land site/ During construction	Contractor(s)		✓		Implemented	ETWB TCW No. 33/2002, Management of Construction and Demolition Material Including Rock
S8.5	Any unused chemicals and those with remaining functional capacity will be recycled as far as possible.	Land site/ During construction	Contractor(s)		✓		Implemented	-
S8.5	Use of reusable non-timber formwork to reduce the amount of C&D materials.	All areas/ During construction	Contractor(s)		✓		N/A	WBTC 32/92, The Use of Tropical Hard Wood on Construction Site
S8.5	Prior to disposal of construction waste, wood, steel and other metals will be separated to the extent practical, for re-use and/or recycling to reduce the quantity of waste to be disposed of to landfill.	All areas/ During construction	Contractor(s)		✓		Implemented	DEVB TC(W) No. 6/2010, Trip Ticket System for Disposal of Construction & Demolition Materials
S8.5	Proper storage and site practices to reduce the potential for damage or contamination of construction materials.	All areas/ During construction	Contractor(s)		✓		Implemented, rectified after observation	-
S8.5	Plan and stock construction materials carefully to reduce amount of waste generated and avoid	All areas/ During construction	Contractor(s)		✓		Implemented	-

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	unnecessary generation of waste.							
S8.5	A Sediment Quality Report (SQR) for sampling and chemical testing of the sediment will be prepared and submitted to the EPD for approval. The approved detailed sampling and chemical testing will be carried out prior to the commencement of the dredging activities to confirm the sediment disposal method.	Marine works/ During construction	Contractor(s)		✓		N/A	ETWB TC(W) No. 34/2002 and Dumping at Sea Ordinance (DASO)
S8.5	The management of dredged/ excavated sediment management requirement from ETWB TC(W) No. 34/2002 will be incorporated in the Specification of the Contract Documents.	Marine works/ During construction	WSD/ Contractor(s)		✓		Implemented	ETWB TC(W) No. 34/2002 and Dumping at Sea Ordinance (DASO)
S8.5	The contractor will open a billing account with EPD in accordance with the Waste Disposal (Charges for Disposal of Construction Waste) Regulation for the payment of disposal charges.	Contract mobilisation/ During construction	Contractor(s)		✓		Implemented	Cap 354N Waste Disposal (Charges for Disposal of Construction Waste) Regulation
S8.5	A trip-ticket system will be established in accordance with DEVB TC(W) No. 6/2010 to monitor the reuse of surplus excavated materials off-site and disposal of construction waste and general refuse at transfer facilities/ landfills, and to control fly-tipping.	Contract mobilisation/ During construction	Contractor(s)		✓		Implemented	DEVB TC(W) No. 6/2010, Trip Ticket System for Disposal of Construction & Demolition Materials
S8.5	The project proponent will also conduct regular inspection of the waste management measures implemented on site as described in the Waste Management Plan.	All area/ During construction	Contractor(s)/ Environmental Team (ET) & Independent Environmental Checker (IEC)		✓		Implemented	ETWB TC(W) No. 19/2005, Environmental Management on Construction Sites
S8.5	A recording system (similar to summary table as shown in Annex 5 and Annex 6 of Appendix G of ETWB TC(W) No. 19/2005) for the amount of waste generated, recycled and disposed of (including the disposal sites) will be established during the construction phase.	All area/ During construction	Contractor(s)		✓		Implemented	Annex 5 and Annex 6 of Appendix G of ETWB TC(W) No. 19/2005
S8.5	Inert C&D materials (public fill) will be reused within	All area/ During construction	Contractor(s)		✓		N/A	-

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	the Project as far as practicable.							
S8.5	Public fill and construction waste shall be segregated and stored in different containers or skips to facilitate reuse or recycling of materials and their proper disposal.	All area/ During construction	Contractor(s)		✓		N/A	-
S8.5	Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable.	All area/ During construction	Contractor(s)		✓		N/A	-
S8.5	To reduce the potential dust and water quality impacts of site formation works, C&D materials will be wetted as quickly as possible to the extent practice after filling.	All area/ During construction	Contractor(s)		✓		Implemented	Air Pollution Control (Construction Dust) Regulation (Cap 311R); WPCO (Cap 358)
S8.5	Open stockpiles of excavated/ fill materials or construction wastes on-site should be covered with tarpaulin or similar fabric.	Land site/ During Construction, particularly dry season	Contractor(s)		✓		N/A	Air Pollution Control (Construction Dust) Regulation (Cap 311R)
S8.5	Chemical waste container shall be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Chemical waste container shall have a capacity of less than 450 L unless the specifications have been approved by the EPD.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	A label in English and Chinese shall be displayed on the chemical container in accordance with instructions	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste)

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	prescribed in Schedule 2 of the Regulations.							(General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall be enclosed on at least 3 sides.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall have adequate ventilation.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary).	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
								Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall be arranged so that incompatible materials are appropriately separated.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	General refuse will be stored in enclosed bins or compaction units separately from construction and chemical wastes.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Adequate number of waste containers will be provided to avoid over-spillage of waste.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	DEVB TC(W) No. 8/2010 Enhanced Specification for Site Cleanliness and Tidiness.
S8.5	A reputable waste collector will be employed by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily basis to minimise odour, pest and litter impacts.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	N/A	-
S8.5	Recycling bins will be provided at strategic locations within the Site to facilitate recovery of recyclable materials (including aluminium can, waste paper, glass bottles and plastic bottles) from the Site. Materials recovered will be sold for recycling.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	-

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
S8.5	To avoid any odour and litter impact, accurate number of portable toilets will be provided for workers on-site.	All area/ During construction	Contractor(s)		✓		Implemented	-
S8.5	The burning of refuse on construction sites is prohibited by law.	All area/ During construction	Contractor(s)		✓		Implemented	Air Pollution Control Ordinance (Cap 311)
S8.7	To facilitate monitoring and control over the contractors' performance on waste management, a waste inspection and audit programme will be implemented throughout the construction phase.	All facilities/ During construction	ET/ IEC		✓		Implemented	-

Note: D – Design stage C – Construction O – Operation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	Ecology							
S9.7	For slope mitigation works within the Clear Water Bay Country Park, to avoid tree felling and damages to trees, the exact locations of the flexible barrier foundation plates, soil nails and rock dowels can be adjusted during detailed design, and a setback distance from existing trees is recommended to be maintained as far as practical. A detailed specification describing the exact locations of the flexible barrier foundation plates, soil nails and rock dowels will be prepared to illustrate how the setback distance from existing trees would be implemented for tree avoidance.	Slope mitigation works area/ During detailed design/ During construction	Contractor(s)	✓	✓		N/A	-
S9.7	Pruning of tree canopies along the alignment of the flexible barriers shall be limited to a minimum.	Slope mitigation works area/ During construction	Contractor(s)		✓		N/A	
S9.7	The alignment of flexible barriers shall be optimized to preserve all species of conservation interest and minimize the impact to the existing vegetation as far as practicable. All individuals of <i>Marsdenia lachnostoma</i> within the slope mitigation areas shall be retained <i>in-situ</i> , by positioning the alignment of flexible barrier at a minimum 1.5m in a radius away from these individuals.	Slope mitigation works area/ During detailed design/ During construction	Contractor(s)	✓	✓		N/A	-
S9.7 and 9.10	At the detailed design stage prior to the commencement of the slope mitigation works, a vegetation survey shall be carried out at the slope mitigation areas within the Clear Water Bay Country Park to assess the condition and identify the location of each individual of <i>Marsdenia lachnostoma</i> and other flora species of conservation interest that may be directly affected by the construction works.	Slope mitigation works area/ During detailed design/ During construction	Contractor(s)	✓	✓		N/A	-
S9.7	Temporary fencing will be installed to fence off the concerned species either in groups of individually within the works area and in the close proximity to prevent from being damaged and disturbed during construction. A sign identifying the site shall be attached to the fence and flagging tape shall be attached to the individuals to visualize their locations.	Slope mitigation works area/ During construction	Contractor(s)		✓		N/A	-
S9.7 and S9.10	A specification for fencing and demarcating individuals of <i>Marsdenia lachnostoma</i> (or other flora species of	Slope mitigation works area/ During construction	Contractor(s)		✓		N/A	-

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	conservation interest, if found) adjacent to the proposed alignment of the flexible barriers will be prepared to protect the species.							
S9.7	Induction training shall also be provided to all site personnel in order to brief them on this flora of conservation interest including the locations and their importance.	Slope mitigation works area/ During construction	Contractor(s)		✓		Implemented	-
S9.7	The resident site supervisory staff will closely monitor the conditions of concerned individuals during construction of flexible barriers in the close proximity.	Slope mitigation works area/ During construction	Contractor(s)		✓		N/A	-
S9.7	Erect fences along the boundary of the works area before the commencement of works to prevent vehicle movements and encroachment of personnel onto adjacent areas.	All area/ During construction	Contractor(s)		✓		N/A	-
S9.7	Regularly check the work site boundaries to ensure that they are not breached and that damage does not occur to surrounding areas.	All area/ During construction	Contractor(s)/ Environmental Team (ET)		✓		N/A	-
S9.7	Avoid any damage and disturbance, particularly those caused by filling and illegal dumping, to the surrounding habitats through proper management of waste disposal.	All area/ During construction	Contractor(s)		✓		N/A	-
S9.7	Reinstate temporarily affected areas, particularly the habitats of plantation and shrubland-grassland immediately after completion of construction works, through on-site tree/shrub planting. The tree/shrub species will be chosen with reference to those in the surrounding area.	All area/ During construction	Contractor(s)		✓		N/A	-
S9.7	Affected habitats within the Clear Water Bay Country Bay shall be reinstated by hydro-seeding and planting of climbers and native shrub seedlings where practical upon completion of the slope mitigation works.	All area/ During construction	Contractor(s)		✓		N/A	-

Note: D – Design stage C – Construction O – Operation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	Landscape & Visual							
S11.10 & 11.11	The construction area and area allowed for temporary structures, such as the contractor's office, will be minimized to a practical minimum. (MM1)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	-
S11.10 & 11.11	At the detailed design stage, the design team will seek to minimize the landscape footprint of the Project and above ground facilities, while satisfying all other requirements. (MM2)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	-
S11.10 & 11.11	Design principles will be adopted to take into account the surrounding area, particularly Clear Water Bay Country Park behind and the nearby waterfront, with due consideration given to: - green roofs where practical (ie without equipment on the roof); - roadside planting; - aesthetic treatment of all structures; - vertical greening; screen planting along application site; and - landscape enhancement with amenity planting where practical including planting along the edge (site boundary) fence with native shrubs where feasible, - to reduce their visual impact and blend them into the surrounding landscape. (MM3)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	-
S11.10 & 11.11	All trees within the Project Site or the potential slope mitigation works area will be carefully protected during construction according to DEVB TCW No. 10/2013 – Tree Preservation (MM4)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	ETWB TCW No. 3/2006 - Tree Preservation.
S11.10 & 11.11	No tree within the Country Park will be felled. Trees within the Site unavoidably affected by the works will be transplanted where necessary and practical. For trees that need to be felled, compensatory planting will be provided to the satisfaction of relevant Government departments. A compensatory tree planting proposal including locations of tree compensation will be submitted to seek relevant government department's approval, in accordance with DEVB TC(W) No. 10/2013. (MM5)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	DEVB TC(W) No. 10/2013

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
S11.10 & 11.11	Any slope mitigation works necessary to address natural terrain hazards, will be minimized to minimize any potential environmental impact to the Country Park e.g. soil nailing and rock stabilization will aim to avoid existing trees e.g. should any restoration of vegetation be necessary, the best planting matrix with native species will be established, with the aim of resembling the existing vegetation. (MM6)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	
S11.10 & 11.11	Dredging works for the installation of intake structures and outfall diffusers should be minimized to avoid or reduce any potential environmental impacts to as low as reasonably practicable (ALARP). The intake and outfall structures (e.g. intake openings and diffuser heads) will be prefabricated and transferred to site for installation. (MM7)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	N/A	
S11.10 & 11.11	All night-time lighting will be reduced to a practical minimum both in terms of number of level and will be hooded and directional. (MM8) units and lux level and will be hooded and directional. (MM8)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	-

Note: D – Design stage C – Construction O – Operation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	Landfill Gas Hazard							
S12.7	During all works, safety procedures should be implemented to minimise the risks of fires and explosions, asphyxiation of workers and toxicity effects resulting from contact with contaminated soil and groundwater.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	-
S12.7	During trenching and excavation as well as creation of confined spaces at near to or below ground level, precautions should be clearly laid down and rigidly Gas detection equipment and appropriate breathing apparatus should be available and used when entering confined spaces or trenches deeper than 1 metre.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	N/A	
S12.7	The Contractor should make the workers are aware of potential hazards of working in confined spaces (any chamber, manhole or culvert which is large enough to permit access to personnel). Such work in confined spaces is controlled by the Factories and Industrial Undertakings (Confined Spaces) Regulations of the Factories and Industrial Undertakings Ordinance. Following the Safety Guide to Working in Confined Spaces ensures compliance with the above regulations.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	Safety officers, specifically trained with regard to landfill gas and leachate related hazards and the appropriate actions to take in adverse circumstances, should be present on the site throughout the works, in particular, when works are undertaken below grade.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	All personnel who work on site and all visitors to the site should be made aware of the possibility of ignition of gas in the vicinity of the works, the possible presence of contaminated water and the need to avoid physical contact with it.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	Monitoring for landfill gas should be undertaken in all excavations, manholes, chambers (particularly during pipe jacking) and any confined spaces through the use of an intrinsically safe portable instrument, appropriately calibrated and capable of measuring the concentrations of methane, carbon dioxide and oxygen.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	N/A	
S12.7	Monitoring frequency and areas to be monitored should be specified prior to commencement of	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	N/A	

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	groundwork, either by the Safety Officer, or by an appropriately qualified person. All measurements should be recorded and documented.	operation						
S12.7	Proceed drilling with adequate care and precautions against the potential hazards which may be encountered.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	Prior to the commencement of the site works, the drilling contractor should devise a 'method-of- working' statement covering all normal and emergency procedures (including but not limited to number of operatives, experience and special skills of operatives, normal method of operations, emergency procedures, supervisors responsibilities, storage and use of safety equipment, safety procedures and signs, barriers and guarding). The site supervisor and all operatives must be familiar with this statement.	All area/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	Where below ground service entries are necessary to the Incoming Switchgear Room, 132 kV Substation and Chlorine Store (I) and (II), the entry point should be sealed to prevent gas entry. In addition, any below grade cable trenches entering the Incoming Switchgear Room and 132 kV Substation can become the pathway for landfill gas and hence grilled metal covers should be used.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	N/A	
S12.7	It is recommended regular landfill gas monitoring should be carried out at the Incoming Switchgear Room, 132 kV Substation and Chlorine Store (I) and (II). The monitoring frequency will be monthly for the first year of operation. If the monitoring results show no sign of landfill gas migration, reduce the monitoring frequency to once every six months.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	N/A	
S12.7	The manholes and utility pits within the Project Site and along the fresh water mains. Each manhole/ utility pit should be monitored with two measurements (at mid depth and base). Each measurement should be monitored for a minimum of 10 minutes. A steady reading and peak reading should be recorded at each manhole/ utility pit and for each measurement. The need for venting the manhole/ utility pit and further	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	N/A	

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
S12.7	monitoring will be reviewed after the initial monitoring. All construction, operation and maintenance personnel working on-site as well as visitors should be made aware of the hazards of landfill gas and its possible presence on-site. This should be achieved through a combination of posting warning signs in prominent places and also by access to detailed information on landfill gas hazards and the designs and procedural means by which these hazards are being minimised on-site.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	

Note: D – Design stage C – Construction O – Operation

Appendix F

Action and Limit Level for Noise and Landfill Gas

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



Action/ Limit Level for Noise Monitoring

Time Period	Action	Limit (dB(A))
0700-1900 hours on normal weekdays	When one documented complaint is received from any one of the noise sensitive receivers	• 70 dB(A) for school and • 65 dB(A) during examination period
Notes: (a) Limits specified in the GW-TM and IND-TM for construction and operation noise, respectively.		

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



Action Level for Landfill Gas Monitoring

Parameters	Level
Oxygen (O ₂)	Action Level < 19% O ₂
	Limit Level < 19% O ₂
Methane (CH ₄)	Action Level >10% LEL
	Limit Level >20% LEL
Carbon Dioxide (CO ₂)	Action Level >0.5% CO ₂
	Limit Level >1.5% CO ₂

Appendix G

Landfill Gas Monitoring Results

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



Date of Measurement	Sampling Location	Depth (m)	Sampling time	Weather Condition	Balance Gas(%)	Flammable gas (methane%)	Carbon Dioxide (%)	Oxygen (%)	Temp (C)	Pressure (m bar)	Measurement Equipment	Remarks
3/9/2018	CHA6588	3.3	08:15	Fine	0	0	0	20.9	30.0	1013	M40	
3/9/2018	CHA6588	3.3	13:00	Fine	0	0	0	20.9	30.0	1011	M40	
4/9/2018	CHA6588	3.3	08:00	Fine	0	0	0	20.9	31.0	1017	M40	
4/9/2018	CHA6588	3.3	13:00	Fine	0	0	0	20.9	31.0	1016	M40	
5/9/2018	CHA6588	3.3	08:00	Fine	0	0	0	20.9	31.0	1015	M40	
5/9/2018	CHA6588	3.3	13:00	Fine	0	0	0	20.9	31.0	1014	M40	
6/9/2018	CHA6588	3.3	08:00	Fine	0	0	0	20.9	31.0	1013	M40	
6/9/2018	CHA6588	3.3	13:00	Fine	0	0	0	20.9	31.0	1012	M40	
7/9/2018	CHA6588	3.3	08:00	Fine	0	0	0	20.9	30.0	1013	M40	
7/9/2018	CHA6588	3.3	13:00	Fine	0	0	0	20.9	30.0	1012	M40	
11/9/2018	CHA6588	3.3	08:00	Fine	0	0	0	20.9	31.0	1014	M40	
11/9/2018	CHA6588	3.3	13:00	Fine	0	0	0	20.9	31.0	1013	M40	
11/9/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	31.0	1014	M40	
11/9/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	31.0	1013	M40	
12/9/2018	CHA6588	3.3	08:00	Fine	0	0	0	20.9	31.0	1013	M40	
12/9/2018	CHA6588	3.3	13:00	Fine	0	0	0	20.9	31.0	1012	M40	
12/9/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	31.0	1013	M40	
12/9/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	31.0	1012	M40	
13/9/2018	CHA6588	3.3	08:00	Fine	0	0	0	20.9	30.0	1017	M40	
13/9/2018	CHA6588	3.3	13:00	Fine	0	0	0	20.9	30.0	1016	M40	
13/9/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	30.0	1017	M40	
13/9/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	30.0	1016	M40	
14/9/2018	CHA6588	3.3	08:00	Rainy	0	0	0	20.9	29.0	1015	M40	
14/9/2018	CHA6588	3.3	13:00	Rainy	0	0	0	20.9	29.0	1014	M40	
14/9/2018	CHA01528	3.3	08:30	Rainy	0	0	0	20.9	29.0	1015	M40	
14/9/2018	CHA01528	3.3	13:30	Rainy	0	0	0	20.9	29.0	1014	M40	
15/9/2018	CHA6588	3.3	08:00	Rainy	0	0	0	20.9	30.0	1015	M40	
15/9/2018	CHA6588	3.3	13:00	Rainy	0	0	0	20.9	30.0	1014	M40	
18/9/2018	CHA6588	3.3	08:00	Rainy	0	0	0	20.9	30.0	1018	M40	
18/9/2018	CHA6588	3.3	13:00	Rainy	0	0	0	20.9	30.0	1017	M40	
18/9/2018	CHA01528	3.3	08:30	Rainy	0	0	0	20.9	30.0	1018	M40	
18/9/2018	CHA01528	3.3	13:30	Rainy	0	0	0	20.9	30.0	1017	M40	
19/9/2018	CHA01528	3.3	08:00	Fine	0	0	0	20.9	30.0	1017	M40	
19/9/2018	CHA01528	3.3	13:00	Fine	0	0	0	20.9	30.0	1016	M40	
20/9/2018	CHA01528	3.3	08:00	Fine	0	0	0	20.9	30.0	1013	M40	
20/9/2018	CHA01528	3.3	13:00	Fine	0	0	0	20.9	30.0	1012	M40	
20/9/2018	CHA6588	3.3	08:30	Fine	0	0	0	20.9	30.0	1013	M40	
20/9/2018	CHA6588	3.3	13:30	Fine	0	0	0	20.9	30.0	1012	M40	
21/9/2018	CHA6588	3.3	08:00	Fine	0	0	0	20.9	30.0	1018	M40	
21/9/2018	CHA6588	3.3	13:00	Fine	0	0	0	20.9	30.0	1017	M40	
21/9/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	30.0	1018	M40	
21/9/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	30.0	1017	M40	
26/9/2018	CHA12555	3.3	08:00	Fine	0	0	0	20.9	30.0	1019	M40	
26/9/2018	CHA12555	3.3	13:00	Fine	0	0	0	20.9	30.0	1018	M40	
26/9/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	30.0	1019	M40	
26/9/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	30.0	1018	M40	
26/9/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	30.0	1019	M40	
26/9/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	30.0	1018	M40	
27/9/2018	CHA12555	3.3	08:00	Fine	0	0	0	20.9	31.0	1016	M40	
27/9/2018	CHA12555	3.3	13:00	Fine	0	0	0	20.9	31.0	1015	M40	
27/9/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	31.0	1016	M40	
27/9/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	31.0	1015	M40	
27/9/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	31.0	1016	M40	
27/9/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	31.0	1015	M40	
28/9/2018	CHA6588	3.3	08:00	Fine	0	0	0	20.9	30.0	1014	M40	
28/9/2018	CHA6588	3.3	13:00	Fine	0	0	0	20.9	30.0	1013	M40	
28/9/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	30.0	1014	M40	

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



Date of Measurement	Sampling Location	Depth (m)	Sampling time	Weather Condition	Balance Gas(%)	Flammable gas (methane%)	Carbon Dioxide (%)	Oxygen (%)	Temp (C)	Pressure (m bar)	Measurement Equipment	Remarks
28/9/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	30.0	1013	M40	
28/9/2018	CHA12555	3.3	09:00	Fine	0	0	0	20.9	30.0	1014	M40	
28/9/2018	CHA12555	3.3	14:00	Fine	0	0	0	20.9	30.0	1013	M40	
29/9/2018	CHA6588	3.3	08:00	Fine	0	0	0	20.9	31.0	1019	M40	
29/9/2018	CHA6588	3.3	13:00	Fine	0	0	0	20.9	31.0	1018	M40	
29/9/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	31.0	1019	M40	
29/9/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	31.0	1018	M40	
29/9/2018	CHA12555	3.3	09:00	Fine	0	0	0	20.9	31.0	1019	M40	
29/9/2018	CHA12555	3.3	14:00	Fine	0	0	0	20.9	31.0	1018	M40	
2/10/2018	CHA6188	3.3	08:00	Fine	0	0	0	20.9	28.0	1019	M40	
2/10/2018	CHA6188	3.3	13:00	Fine	0	0	0	20.9	28.0	1018	M40	
2/10/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	28.0	1019	M40	
2/10/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	28.0	1018	M40	
2/10/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	28.0	1019	M40	
2/10/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	28.0	1018	M40	
3/10/2018	CHA6188	3.3	08:00	Fine	0	0	0	20.9	27.0	1017	M40	
3/10/2018	CHA6188	3.3	13:00	Fine	0	0	0	20.9	27.0	1016	M40	
3/10/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	27.0	1017	M40	
3/10/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	27.0	1016	M40	
3/10/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	27.0	1017	M40	
3/10/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	27.0	1016	M40	
4/10/2018	CHA6188	3.3	08:00	Fine	0	0	0	20.9	28.0	1014	M40	
4/10/2018	CHA6188	3.3	13:00	Fine	0	0	0	20.9	28.0	1013	M40	
4/10/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	28.0	1014	M40	
4/10/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	28.0	1013	M40	
4/10/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	28.0	1014	M40	
4/10/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	28.0	1013	M40	
5/10/2018	CHA6188	3.3	08:00	Fine	0	0	0	20.9	27.0	1016	M40	
5/10/2018	CHA6188	3.3	13:00	Fine	0	0	0	20.9	27.0	1015	M40	
5/10/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	27.0	1016	M40	
5/10/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	27.0	1015	M40	
5/10/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	27.0	1016	M40	
5/10/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	27.0	1015	M40	
6/10/2018	CHA6188	3.3	08:00	Fine	0	0	0	20.9	28.0	1016	M40	
6/10/2018	CHA6188	3.3	13:00	Fine	0	0	0	20.9	28.0	1015	M40	
6/10/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	28.0	1016	M40	
6/10/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	28.0	1015	M40	
6/10/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	28.0	1016	M40	
6/10/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	28.0	1015	M40	
7/10/2018	CHA6188	3.3	08:00	Fine	0	0	0	20.9	28.0	1018	M40	
7/10/2018	CHA6188	3.3	13:00	Fine	0	0	0	20.9	28.0	1017	M40	
7/10/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	28.0	1018	M40	
7/10/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	28.0	1017	M40	
7/10/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	28.0	1018	M40	
7/10/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	28.0	1017	M40	
8/10/2018	CHA6188	3.3	08:00	Fine	0	0	0	20.9	28.0	1018	M40	
8/10/2018	CHA6188	3.3	13:00	Fine	0	0	0	20.9	28.0	1017	M40	
8/10/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	28.0	1018	M40	
8/10/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	28.0	1017	M40	
8/10/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	28.0	1018	M40	
8/10/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	28.0	1017	M40	
9/10/2018	CHA6188	3.3	08:00	Rainy	0	0	0	20.9	28.0	1013	M40	
9/10/2018	CHA6188	3.3	13:00	Rainy	0	0	0	20.9	28.0	1012	M40	
9/10/2018	CHA01528	3.3	08:30	Rainy	0	0	0	20.9	28.0	1013	M40	
9/10/2018	CHA01528	3.3	13:30	Rainy	0	0	0	20.9	28.0	1012	M40	
9/10/2018	CHA6588	3.3	09:00	Rainy	0	0	0	20.9	28.0	1013	M40	
9/10/2018	CHA6588	3.3	14:00	Rainy	0	0	0	20.9	28.0	1012	M40	
10/10/2018	CHA6188	3.3	08:00	Rainy	0	0	0	20.9	28.0	1015	M40	

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



Date of Measurement	Sampling Location	Depth (m)	Sampling time	Weather Condition	Balance Gas(%)	Flammable gas (methane%)	Carbon Dioxide (%)	Oxygen (%)	Temp (C)	Pressure (m bar)	Measurement Equipment	Remarks
10/10/2018	CHA6188	3.3	13:00	Rainy	0	0	0	20.9	28.0	1014	M40	
10/10/2018	CHA01528	3.3	08:30	Rainy	0	0	0	20.9	28.0	1015	M40	
10/10/2018	CHA01528	3.3	13:30	Rainy	0	0	0	20.9	28.0	1014	M40	
10/10/2018	CHA6588	3.3	09:00	Rainy	0	0	0	20.9	28.0	1015	M40	
10/10/2018	CHA6588	3.3	14:00	Rainy	0	0	0	20.9	28.0	1014	M40	
11/10/2018	CHA6188	3.3	08:00	Fine	0	0	0	20.9	27.0	1016	M40	
11/10/2018	CHA6188	3.3	13:00	Fine	0	0	0	20.9	27.0	1015	M40	
11/10/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	27.0	1016	M40	
11/10/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	27.0	1015	M40	
11/10/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	27.0	1016	M40	
11/10/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	27.0	1015	M40	
12/10/2018	CHA6188	3.3	08:00	Fine	0	0	0	20.9	27.0	1017	M40	
12/10/2018	CHA6188	3.3	13:00	Fine	0	0	0	20.9	27.0	1016	M40	
12/10/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	27.0	1017	M40	
12/10/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	27.0	1016	M40	
12/10/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	27.0	1017	M40	
12/10/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	27.0	1016	M40	
15/10/2018	CHA6188	3.3	08:00	Rainy	0	0	0	20.9	23.0	1013	M40	
15/10/2018	CHA6188	3.3	13:00	Rainy	0	0	0	20.9	23.0	1012	M40	
15/10/2018	CHA01528	3.3	08:30	Rainy	0	0	0	20.9	23.0	1013	M40	
15/10/2018	CHA01528	3.3	13:30	Rainy	0	0	0	20.9	23.0	1012	M40	
15/10/2018	CHA6588	3.3	09:00	Rainy	0	0	0	20.9	23.0	1013	M40	
15/10/2018	CHA6588	3.3	14:00	Rainy	0	0	0	20.9	23.0	1012	M40	
16/10/2018	CHA6188	3.3	08:00	Rainy	0	0	0	20.9	24.0	1018	M40	
16/10/2018	CHA6188	3.3	13:00	Rainy	0	0	0	20.9	24.0	1017	M40	
16/10/2018	CHA01528	3.3	08:30	Rainy	0	0	0	20.9	24.0	1018	M40	
16/10/2018	CHA01528	3.3	13:30	Rainy	0	0	0	20.9	24.0	1017	M40	
16/10/2018	CHA6588	3.3	09:00	Rainy	0	0	0	20.9	24.0	1018	M40	
16/10/2018	CHA6588	3.3	14:00	Rainy	0	0	0	20.9	24.0	1017	M40	
18/10/2018	CHA6188	3.3	08:00	Rainy	0	0	0	20.9	23.0	1018	QRAE	
18/10/2018	CHA6188	3.3	13:00	Rainy	0	0	0	20.9	23.0	1017	QRAE	
18/10/2018	CHA01528	3.3	08:30	Rainy	0	0	0	20.9	23.0	1018	QRAE	
18/10/2018	CHA01528	3.3	13:30	Rainy	0	0	0	20.9	23.0	1017	QRAE	
18/10/2018	CHA6588	3.3	09:00	Rainy	0	0	0	20.9	23.0	1018	QRAE	
18/10/2018	CHA6588	3.3	14:00	Rainy	0	0	0	20.9	23.0	1017	QRAE	
19/10/2018	CHA6188	3.3	08:00	Fine	0	0	0	20.9	24.0	1015	QRAE	
19/10/2018	CHA6188	3.3	13:00	Fine	0	0	0	20.9	24.0	1014	QRAE	
19/10/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	24.0	1015	QRAE	
19/10/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	24.0	1014	QRAE	
19/10/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	24.0	1015	QRAE	
19/10/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	24.0	1014	QRAE	
20/10/2018	CHA6188	3.3	08:00	Fine	0	0	0	20.9	25.0	1017	QRAE	
20/10/2018	CHA6188	3.3	13:00	Fine	0	0	0	20.9	25.0	1016	QRAE	
20/10/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	25.0	1017	QRAE	
20/10/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	25.0	1016	QRAE	
20/10/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	25.0	1017	QRAE	
20/10/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	25.0	1016	QRAE	
22/10/2018	CHA6188	3.3	08:00	Fine	0	0	0	20.9	25.0	1018	QRAE	
22/10/2018	CHA6188	3.3	13:00	Fine	0	0	0	20.9	25.0	1017	QRAE	
22/10/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	25.0	1018	QRAE	
22/10/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	25.0	1017	QRAE	
22/10/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	25.0	1018	QRAE	
22/10/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	25.0	1017	QRAE	
23/10/2018	CHA6188	3.3	08:00	Fine	0	0	0	20.9	26.0	1014	QRAE	
23/10/2018	CHA6188	3.3	13:00	Fine	0	0	0	20.9	26.0	1013	QRAE	
23/10/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	26.0	1014	QRAE	
23/10/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	26.0	1013	QRAE	
23/10/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	26.0	1014	QRAE	

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
1st Quarterly EM&A Report for August to October 2018



Date of Measurement	Sampling Location	Depth (m)	Sampling time	Weather Condition	Balance Gas(%)	Flammable gas (methane%)	Carbon Dioxide (%)	Oxygen (%)	Temp (C)	Pressure (m bar)	Measurement Equipment	Remarks
23/10/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	26.0	1013	QRAE	
24/10/2018	CHA6188	3.3	08:00	Fine	0	0	0	20.9	24.0	1016	QRAE	
24/10/2018	CHA6188	3.3	13:00	Fine	0	0	0	20.9	24.0	1015	QRAE	
24/10/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	24.0	1016	QRAE	
24/10/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	24.0	1015	QRAE	
24/10/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	24.0	1016	QRAE	
24/10/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	24.0	1015	QRAE	
25/10/2018	CHA6188	3.3	08:00	Fine	0	0	0	20.9	24.0	1013	QRAE	
25/10/2018	CHA6188	3.3	13:00	Fine	0	0	0	20.9	24.0	1012	QRAE	
25/10/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	24.0	1013	QRAE	
25/10/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	24.0	1012	QRAE	
25/10/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	24.0	1013	QRAE	
25/10/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	24.0	1012	QRAE	
26/10/2018	CHA6188	3.3	08:00	Fine	0	0	0	20.9	25.0	1014	QRAE	
26/10/2018	CHA6188	3.3	13:00	Fine	0	0	0	20.9	25.0	1013	QRAE	
26/10/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	25.0	1014	QRAE	
26/10/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	25.0	1013	QRAE	
26/10/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	25.0	1014	QRAE	
26/10/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	25.0	1013	QRAE	
29/10/2018	CHA6188	3.3	08:00	Fine	0	0	0	20.9	24.0	1012	QRAE	
29/10/2018	CHA6188	3.3	13:00	Fine	0	0	0	20.9	24.0	1011	QRAE	
29/10/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	24.0	1012	QRAE	
29/10/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	24.0	1011	QRAE	
29/10/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	24.0	1012	QRAE	
29/10/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	24.0	1011	QRAE	
30/10/2018	CHA6188	3.3	08:00	Fine	0	0	0	20.9	27.0	1015	QRAE	
30/10/2018	CHA6188	3.3	13:00	Fine	0	0	0	20.9	27.0	1014	QRAE	
30/10/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	27.0	1015	QRAE	
30/10/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	27.0	1014	QRAE	
30/10/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	27.0	1015	QRAE	
30/10/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	27.0	1014	QRAE	
31/10/2018	CHA6188	3.3	08:00	Fine	0	0	0	20.9	27.0	1017	QRAE	
31/10/2018	CHA6188	3.3	13:00	Fine	0	0	0	20.9	27.0	1016	QRAE	
31/10/2018	CHA01528	3.3	08:30	Fine	0	0	0	20.9	27.0	1017	QRAE	
31/10/2018	CHA01528	3.3	13:30	Fine	0	0	0	20.9	27.0	1016	QRAE	
31/10/2018	CHA6588	3.3	09:00	Fine	0	0	0	20.9	27.0	1017	QRAE	
31/10/2018	CHA6588	3.3	14:00	Fine	0	0	0	20.9	27.0	1016	QRAE	

Appendix H

Complaint Log and Regulatory Compliance Proforma

Statistical Summary of Environmental Complaints

Reporting Period	Environmental Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
30 Aug 2018-31 Oct 2018	0	0	N/A

Statistical Summary of Environmental Summons

Reporting Period	Environmental Summons Statistics		
	Frequency	Cumulative	Details
30 Aug 2018-31 Oct 2018	0	0	N/A

Statistical Summary of Environmental Prosecution

Reporting Period	Environmental Prosecution Statistics		
	Frequency	Cumulative	Details
30 Aug 2018-31 Oct 2018	0	0	N/A
