



Water Supplies Department
New Works Branch
Construction Division
11 Tai Yip Lane
Kowloon Bay
Kowloon
Hong Kong

Your reference:

Our reference: HKWSD201/50/106929

Date: 7 December 2020

Attention: Mr Hivan Cheng

BY POST

Quotation No.: WQ/17/A071
Independent Environmental Checker for Water Supplies Department
-Proposed Desalination Plant in TKO Area 137 for Contract No. 13/WSD/16
Verification of 9th Quarterly EM&A Report for August 2020 to October 2020

We refer to emails of 3 and 7 December 2020 attaching 9th Quarterly EM&A Report for August 2020 to October 2020 for the captioned project prepared by the ET.

We have no comment and hereby verify the 9th Quarterly EM&A Report for August 2020 to October 2020 in accordance with Clause 3.5 of the Environmental Permit no. EP-503/2015/A.

Should you have any queries regarding the above, please do not hesitate to contact the undersigned or our Ms Reasonie Cheung on 2618 2831.

Yours faithfully
ANEWR CONSULTING LIMITED

James Choi
Independent Environmental Checker

CPSJ/CYYR/lsm



ACUITY
SUSTAINABILITY
CONSULTING LIMITED



Website: www.acuityhk.com



Unit C, 11/F, Ford Glory Plaza,
Nos. 37-39 Wing Hong Street,
Cheung Sha Wan, Kowloon.



Tel. : (852) 2698 6833
Fax.: (852) 2698 9383



水務署


Water Supplies Department

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report For August 2020 to October 2020

November 2020
(Rev. 0)

	Prepared by:	Certified by:
Name	Karen Cheung	Jacky Leung
Position	Environmental Team	Environmental Team Leader
Signature		
Date:	30 November 2020	30 November 2020

Revision History

0	1 st Submission	03 December 2020
Rev.	DESCRIPTION OF MODIFICATION	DATE

CONTENT

EXECUTIVE SUMMARY

1. BASIC PROJECT INFORMATION	1
2. NOISE MONITORING.....	5
3. WASTE MANAGEMENT	5
4. SUMMARY OF MONITORING EXCEEDANCE, COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTIONS.....	5
5. EM&A SITE INSPECTION.....	5
6. LANDFILL GAS MONITORING	8
7. CONCLUSION AND RECOMMENDATIONS.....	9

Appendix A	Overview of Mainlaying in TKO
Appendix B	Project Organization Chart
Appendix C	Construction Programme
Appendix D	Layout of Major Construction Works Undertaken during the Reporting Quarter
Appendix E	Waste Flow Table
Appendix F	Summary of Implementation Status of Environmental Mitigation
Appendix G	Action and Limit Level for Noise and Landfill Gas
Appendix H	Landfill Gas Monitoring Results
Appendix I	Complaint Log and Regulatory Compliance Proforma
Appendix J	Noise Impact Monitoring Results
Appendix K	Academic School Calander

EXECUTIVE SUMMARY

- A1. Penta-Ocean - Concentric Joint Venture (POCJV) is contracted to carry out the Mainlaying in Tseung Kwan O under Contract No. 13/WSD/16 (hereinafter known as “the Project”).
- A2. In accordance with the Environmental Monitoring and Audit (EM&A) Manual for the Project, EM&A works should be carried out by Environmental Team (ET), Acuity Sustainability Consulting Limited (ASCL), during the construction phase of the Project.
- A3. The construction works of Mainlaying in Tseung Kwan O were commenced on 30 August 2018. This is the 9th quarterly Environmental Monitoring and Audit (EM&A) summary Report prepared by ASCL. This report presents the EM&A works carried out during the period of 1 August 2020 to 31 October 2020.
- A4. A summary of the monitoring activities undertaken in this reporting period is listed below:

Monitoring Activities	Frequency
Daytime Noise monitoring	3 times
Landfill Gas Monitoring	1808 times
Environmental Site Inspection	13 times

- A5. No project-related exceedance of the Action/Limit Level was recorded during the reporting quarter.
- A6. 3 times of noise impact monitoring were conducted on 16,24,30/10/2020 at NSR4 Creative Secondary School since projected-related construction activities were undertaken within a radius of 300m from the monitoring location.
- A7. No exceedance of landfill gas monitoring was recorded during the reporting quarter.
- A8. No summons/ prosecutions were received in the reporting quarter.
- A9. There were no changes to be reported that may affect the on-going EM&A programme.

1 Basic Project Information

1.1.1 Background

1.1.2 The proposed Desalination Plant at Tseung Kwan O (DPTKO) will produce potable water with an initial capacity of 135 million liters per day (MLD), expandable to an ultimate capacity of 270 MLD in the future to provide a secure and alternative fresh water resource complying with the World Health Organization (WHO) standards. The plant will adopt the Seawater Reverse Osmosis (SWRO) technology, which dominates the market due to its reliability and progressive reduction in cost as the technology advances.

1.1.3 Pursuant to the Environmental Impact Assessment Ordinance (EIAO), the Director of Environmental Protection granted the Variation of Environmental Permit (No. EP-503/2015/A) to Water Supplies Department (WSD) for the Project on 26 January 2018.

1.1.4 The scope of the Contract may be considered in brief, to consist of the laying of about 10km long 1200mm diameter fresh water mains and the associated works along the alignment of the Project as shown with the overall view in **Appendix A**.

1.1.5 The Reporting Scope

1.1.6 This is the 9th Quarterly EM&A Report for the Project which summarizes the key findings of the EM&A programme during the reporting period from 1 August 2020 to 31 October 2020.

1.1.7 The Project Organization structure for the Construction Phase is presented in **Appendix B**.

1.1.8 Contact details of the key personnel are presented in **Table 1.1** below:

Table 1.1 Contact Details of Key Personnel

Party	Position	Name	Telephone no.
Penta-Ocean - Concentric Joint Venture	Environmental Officer	Calvin Chik	9863-5630
Acuity Sustainability Consulting Limited	Environmental Team Leader	Jacky Leung	2698-6833
ANewR Consulting Limited	Independent Environmental Checker	James Choi	2618-2831

1.1.9 Summary of Construction Works

1.1.10 Details of the major construction works undertaken in this reporting quarter are shown in **Table 1.2** and **Appendix D**. The construction programme is presented in **Appendix C**.

Table 1.2a Summary of the Construction Works Undertaken during the Reporting quarter (August 2020)

Location	Works Conducted in the reporting month
Portion H of the Project Site	<ul style="list-style-type: none"> • Pipes had been laid from CH.CT0+07~CH.CT2+64. • Concreting work of the top slab and wall of DN900 HSV chamber at CH.CA4+30 was completed in August 2020. • Construction of washout chamber and DAV/IT combined chamber were completed.
Portion J of the Project Site	<ul style="list-style-type: none"> • Laying work of 30 degrees bend DN1200 MS pipe at CH.A6+53 was completed. • Backfilling and road reinstatement work of the bus lay-by and carriageway were completed at CHA12+45. • Sheetpiling work in pit A was completed. • Excavation to 9mBG and installation of 6th layer of waling and strut were completed at Pit C. • Pipes were laid between CH.FB1+98 to CH.FB3+27 and was in progress between CH.FB3+27 to CH.FB3+60 at Area A. • Trench excavation and Pipe mainlaying works were completed at CH.FC2+16 1st work front at the cycle track. • Pipe mainlaying and reinstatement works were completed at CH.FC5+49 2nd work front at the cycle track. • Pipes were laid between CH.FC13+26 and Ch.FC12+05 in Area B. Backfilling work and reinstatement of existing geotextile of these trenches were in-progress. • Excavation work for 1st layer of struts and waling was in-progress at Pit O. • Excavation work for 2nd layer of struts and waling was in-progress at Pit M. • Excavation work for 1st layer of struts and waling was in-progress at Pit N. • The driving work of sheet piles at Pit P was in-progress.

Table 1.2b Summary of the Construction Works Undertaken during the Reporting quarter (September-October 2020)

Location	Location	Works Conducted in the reporting month
Portion H of the Project Site	TKO 137 Fill Bank Desalination Plant & SENTX area	<ul style="list-style-type: none"> Concrete end block casting for MS1200 pipe end at the proposed desalination plant location. Pipe laying and gate valve installation of the remaining NS250 pipeline.
	TKO 137 Pit A	<ul style="list-style-type: none"> Pipe pile for ELS of trenchless receiving pit and grouting works.
	TKO 137 Pit B	<ul style="list-style-type: none"> Grouting works.
	TKO 137 Pit C	N/A
Portion J of the Project Site	Wan Po Rd – Workfront 1	<ul style="list-style-type: none"> Pipe trench excavation and pipe laying.
	Wan Po Rd – Workfront 2	<ul style="list-style-type: none"> Annulus grouting and thrust block casting. Pipe laying and pipe trench excavation for next portion.
	Wan Po Rd – Workfront 3	<ul style="list-style-type: none"> Tial pit works Excavation and ELS works for IT chamber. Construction of base slab with kicker for IT chamber.
	Wan Po Rd – Pit A	<ul style="list-style-type: none"> Hole drilling and grout tube installation for grouting works. Grouting works.
	Wan Po Rd – Pit B	N/A
	Wan Po Rd – Pit C	<ul style="list-style-type: none"> Re-grouting works.
	Landfill Stage 1 – Area A	<ul style="list-style-type: none"> Trench excavation and pipe laying was conducted.
	Landfill Stage 1 – Area B	<ul style="list-style-type: none"> Casting pipe concrete was conducted.
	Cycle Track – Workfront 1	<ul style="list-style-type: none"> Trench excavation and pipe laying works.
	Cycle Track – Workfront 2	<ul style="list-style-type: none"> Trench excavation and pipe laying works.
	Velodrome – Pit L	<ul style="list-style-type: none"> Inspection pit works. Sheetpiling for pit ELS.
	Velodrome – Pit M	<ul style="list-style-type: none"> ELS for trenchless working pit. Trench excavation and pipe laying works.
	Velodrome – Pit N	<ul style="list-style-type: none"> ELS for trenchless working pit. Pit construction was completed.
	Velodrome – Pit O	<ul style="list-style-type: none"> Grouting works was completed. Pit excavation and EIS works.
	Velodrome – Pit P	<ul style="list-style-type: none"> ELS for trenchless working pit Erection for temperature platform for grouting works was in-progress.
	Inspection Pit – Po Lam Road footpath	<ul style="list-style-type: none"> Inspection pit was completed.

1.1.11 Summary of Environmental Status

1.1.12 A summary of the valid permits, licences, and /or notifications on environmental protection for this Project is presented in **Table 1.3**.

Table 1.3 Summary of the Status of Valid Environmental Licence, Notification, Permit and Documentations

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
Variation of Environmental Permit	EP no.: EP-503/2015/A	Throughout the Contract	-
Notification of Construction Works under the Air Pollution Control (Construction Dust) Regulation (Form NA)	Ref no.: 423775	Throughout the Contract	-
Chemical Waste Producer Registration	WPN: 5213-839-P3287-01	Throughout the Contract	-
Billing Account for Disposal of Construction Waste	A/C no.: 7029491	Throughout the Contract	-
Water Discharge License	WT00032336-2018	Until 31 Dec 2023	-
Construction Noise Permit	GW-RE0563-20	Until 28 Sep 2020	-
Construction Noise Permit	GW-RE0846-20	Until 31 Mar 2021	-
Construction Noise Permit (Hong Kong Velodrome)	GW-RE0364-20	Until 17 Nov 2020	-

1.1.13 The status for all environmental aspects is presented **Table 1.4**.

Table 1.4 Summary of Status for Key Environmental Aspects under the EM&A Manual

Parameters	Status
Noise	
Baseline Monitoring	The baseline noise monitoring result has been reported in Baseline Monitoring Report and submitted to EPD under VEP Condition 3.4
Impact Monitoring	3 times of noise impact monitoring were conducted on 16,24,30/10/2020 at NSR4 Creative Secondary School since projected-related construction activities were undertaken within a radius of 300m from the monitoring location
Waste Management	
Mitigation Measures in Waste Monitoring Plan	On-going
Landfill Gas Monitoring	
Mitigation Measures	On-going
Monitoring	On-going
Environmental Audit	
Site Inspection	On-going

- 1.1.14 Other than the EM&A works by ET, regular environmental management meetings were conducted in order to enhance environmental awareness and closely monitor the environmental performance of the contractors.
- 1.1.15 The EM&A programme has been implemented in accordance with the recommendations presented in the approved EIA Report and the EM&A Manual. A summary of implementation status of the environmental mitigation measures for the construction phase of the Project during the reporting period is provided in **Appendix F**.

2 Noise Monitoring

- 2.1.1 Referring to EM&A manual Section 4.1.2, the impact noise monitoring should be carried out at all the designated monitoring stations when there are project-related construction activities undertaken within a radius of 300m from the monitoring stations.
- 2.1.2 3 times of noise impact monitoring were conducted on 16,24,30/10/2020 at NSR4 Creative Secondary School since project-related construction activities were undertaken within a radius of 300m from the monitoring location.
- 2.1.3 Detailed monitoring results are presented in **Appendix J**. Academic School calendar for the reporting quarter was presented in **Appendix K**.
- 2.1.4 No notification of summons and prosecution related to noise was received in the reporting quarter.

3 Waste Management

- 3.1.1 Total of 4.165 m³ of inert C&D materials was collected to the Fill Bank, 0.005 m³ C&D waste and general refuse were disposed of at Landfill, 0.133 tonnes of paper/ cardboard packaging was recycled and 0 tonnes chemical waste collected by licensed contractor for disposal in the reporting quarter. Waste Flow Table is shown in **Appendix E**.

4 Summary of Monitoring Exceedance, Complaints, Notification of Summons and Prosecutions

- 4.1.1 No monitoring exceedance, notification of summons and prosecution was received in the reporting quarter.

5 EM&A Site Inspection

- 5.1.1 Site inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures under the Contract. In the reporting quarter, site inspections were carried out on 6, 13, 20, 24 August 2020, 3, 10, 17, 22 and 30 September 2020, and 8, 15, 21, 27 October 2020 at the site portions list in **Table 5.1** below.

Table 5.1 Site Inspection Record

Date	Inspected Site Portion	Time
6, 13, 20, 24 August 2020, 3, 10, 17, 22 and 30 September 2020, and 8, 15, 21, 27 October 2020	Portion F, H and J	9:15 am – 12:30 pm

5.1.2 Three joint site inspections with IEC was carried out on 24 August 2020, 22 September 2020 and 27 October 2020.

5.1.3 Minor deficiencies were observed during weekly site inspection. Key observations during the site inspections are summarized in **Table 5.2**.

Table 5.2 Site Observations

Date	Environmental Observations	Follow-up Status
06 August 2020	<ol style="list-style-type: none"> 1. Chemicals were not placed inside a drip tray at Pit C. 2. Dust suppression mitigations were not implemented at CHA6+64. 3. Gully was not protected by a geo-textile at CHA6+64. 4. Environmental permit was not observed at the vehicle entrance/exit at the Hong Kong Velodrome. 	<ol style="list-style-type: none"> 1. Chemicals were placed inside a drip tray. 2. Dusty materials were removed. 3. Gully was protected by a geo-textile at CHA6+64. 1. Environmental permit was added at the vehicle entrance/exit at the Hong Kong Velodrome.
13 August 2020	<ol style="list-style-type: none"> 1. Chemicals were not placed inside a drip tray at Pit C. 2. Drainage system was not fully protected by a geo-textile at CHA6+64. 3. Construction boundaries were not protected fully by sandbags at Jacking Pit A. 4. Construction exit/entrance was not free from dusty materials at CHA12+50. 	<ol style="list-style-type: none"> 1. Chemicals were placed inside a drip tray. 2. Gully was fully protected by a geo-textile at CHA6+64. 3. Construction boundaries were protected fully by sandbags at Jacking Pit A. 4. Construction exit/entrance was free from dusty materials at CHA12+50.
20 August 2020	<ol style="list-style-type: none"> 1. Chemicals were not placed inside the drip tray at Pit C and Landfill Stage 1 Area A. 2. Gully was not protected fully by sandbags and geo-textile at CHA6+64. 3. Construction exit/entrance was not free from dusty materials at CHA12+50. 4. Construction boundaries were not protected fully by sandbags at Pit A. 	<ol style="list-style-type: none"> 1. Chemicals were removed or placed inside the drip tray at Pit C and Landfill Stage 1 Area A. 2. Gully was protected fully by sandbags and geo-textile at CHA6+64. 3. Construction exit/entrance was cleaned at CHA12+50. 4. Construction boundaries were protected fully by sandbags at Pit A.

Date	Environmental Observations	Follow-up Status
24 August 2020	1. The contractor was reminded to place an environmental permit at the site entrance/exit at Hong Kong Velodrome.	1. The environmental permit was placed at the site entrance/exit at Hong Kong Velodrome.
03 September 2020	No major observations were observed on the reporting day.	
10 September 2020	1. Chemical was not placed inside a drip tray at CH.FC4+70.	1. Chemicals was removed.
17 September 2020	1. NRMM Label was not added on the NRMM at CHA2+14 to CHA2+66. 2. Gully was not protected by a geo-textile at CHA6+64.	1. NRMM label was added. 2. Gully was fully protected by a geo-textile and sand bag.
22 September 2020	1. Muddy water was observed at the discharge point of the sedimentation tank at the Hong Kong Velodrome.	1. Wastewater was treated before discharge.
30 September 2020	1. Dusty materials were observed directly next to the water barriers. It should be cleaned to prevent the escape of dusty materials from the construction site at 137 Pit A. 2. Wastewater was observed not directed to the sedimentation tank at 137 Pit A and CH.FC0+62. 3. Gully was observed not protected by sandbags at 4 sides and geotextile was not added at CHA2+14-2+66. 4. Dusty materials were observed at the site entrance/exit at CHA6+70.	1. Dusty materials were cleaned to prevent the escape of dusty materials from the construction site at 137 Pit A. 2. Wastewater was not discharged without sedimentation tank at 137 Pit A. Wastewater was directed to the sedimentation tank at 137 Pit A and CH.FC0+62. 3. Gully was protected by sandbags and geotextile. 4. Dusty materials were cleaned at the site entrance/exit at CHA6+70.
08 October 2020	1. Chemicals were not placed inside a drip tray at Portion F. 2. NRMM label was not added on the NRMM at 137 Pit C. 3. Dust suppression mitigations were not implemented at Jacking Pit B.	1. Chemicals were removed. 2. NRMM label was added. 3. Dusty materials were removed.
15 October 2020	1. Chemicals were not placed inside a drip tray at CHA6+64 and Landfill Stage 1 Area A. 2. A sedimentation tank was not placed at the site area even	1. Chemicals were removed from site. 2. There was no water pumping and discharge at CHA6+64.

Date	Environmental Observations	Follow-up Status
	though no water was discharged on the observed day at CHA6+64.	
21 October 2020	1. NRMM label was not observed on the NRMM at Jacking Pit C. 2. Chemicals were not placed inside a drip tray at 137 Pit A and Hong Kong Velodrome. 3. Trapped dusty materials in the sedimentation tank were not cleaned regularly which affected the efficiency of the sedimentation tank at Hong Kong Velodrome. 4. NRMM label was observed damaged at Hong Kong Velodrome.	1. NRMM label was added on the NRMM. 2. Chemicals were removed from 137 Pit A and Hong Kong velodrome. 3. Trapped dusty materials in the sedimentation tank was cleaned. 4. A new NRMM label was added.
27 October 2020	1. Trapped dusty materials were not cleaned regularly at the gully for Hong Kong Velodrome.	1. Trapped dusty materials in the sedimentation tank was cleaned.

5.1.4 According to the EIA Study Report, Environmental Permit, contract documents and EM&A Manual, the mitigation measures detailed in the documents are implemented as much as practical during the reporting quarter. An updated Implementation Status of Environmental Mitigation Measures (EMIS) is provided in **Appendix F**.

6 Landfill gas monitoring

6.1.1 In accordance with Section 11 of the EM&A Manual, monitoring of landfill gas is required for construction works within the 250m Consultation Zone. Part of the desalination plant and the indicative area of natural slope mitigation works fall within the SENT Landfill Extension Consultation Zone; and part of the 1,200 mm diameter fresh water mains along Wan Po Road falls within the SENT Landfill and SENT Landfill Extension Consultation Zones, TKO Stage II/III Restored Landfill and TKO Stage I Restored Landfill Consultation Zones. Monitoring was conducted from August 2020 to October 2020.

6.1.2 Monitoring of oxygen, methane and carbon dioxide was performed for excavations at 1m depth or more within the consultation Zone. In this reporting quarter, 1808 times of monitoring was recorded. Action and Limit Level is provided in **Appendix G**

6.1.3 Monitoring Equipment used in the reporting quarter are summarised in **Table 6.1**.

6.1.4 In the reporting quarter, landfill gas monitoring was carried out by the Registered Safety Officer by the Contractor at the excavation locations for 1808 times. The monitoring results and Action Level are provided in **Appendix H** and **Appendix G** respectively.

Table 6.1 Landfill Gas Monitoring Equipment

Equipment	Model and Make	Calibration Expiry Date
Gas Detector	QRAE II	28 August 2020
Gas Detector	QRAE III	27 July 2021


7 Conclusion and Recommendations

- 7.1.1 This is the 9th quarterly Environmental Monitoring and Audit (EM&A) summary Report prepared by ASCL. This report presenting the EM&A works carried out during the period of 1 August 2020 to 31 October 2020 in accordance with the EM&A Manual and the requirement under EP-503/2015/A.
- 7.1.2 3 times of noise impact monitoring were conducted on 16,24,30/10/2020 at NSR4 Creative Secondary School since projected-related construction activities were undertaken within a radius of 300m from the monitoring location.
- 7.1.3 No landfill gas exceedance was recorded in the reporting quarter.
- 7.1.4 No project-related exceedance of the Action Level was recorded during the reporting period.
- 7.1.5 Weekly environmental site inspection was conducted during the reporting quarter. Minor deficiencies were observed during site inspection and were rectified. The environmental performance of the Project was therefore considered satisfactory.
- 7.1.6 According to the environmental site inspections performed in the reporting quarter, the Contractor is reminded to pay attention on maintaining site tidiness and proper materials storage.
- 7.1.7 No environmental complaint was received in the reporting quarter.
- 7.1.8 No notification of summons or prosecution was received since commencement of the Contract.
- 7.1.9 The ET will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures.
- 7.1.10 Statistics on complaints and regulatory compliance are summarized in **Appendix I**.

Appendix A

Overview of Mainlaying in TKO


Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020

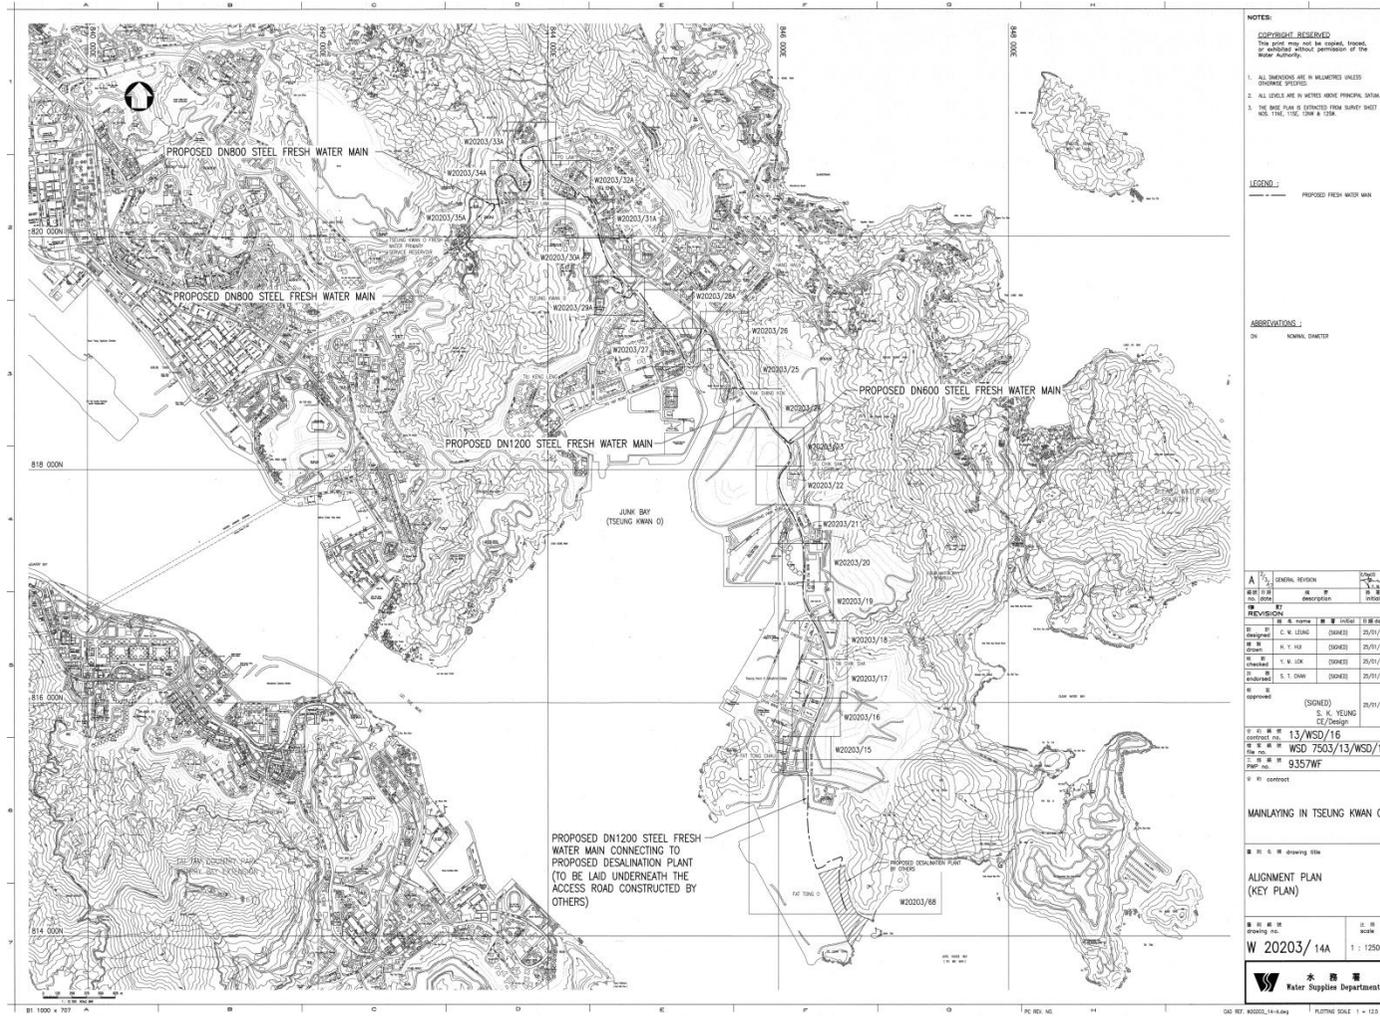

Overview of Mainlaying in TKO

Appendix B

Project Organization Chart

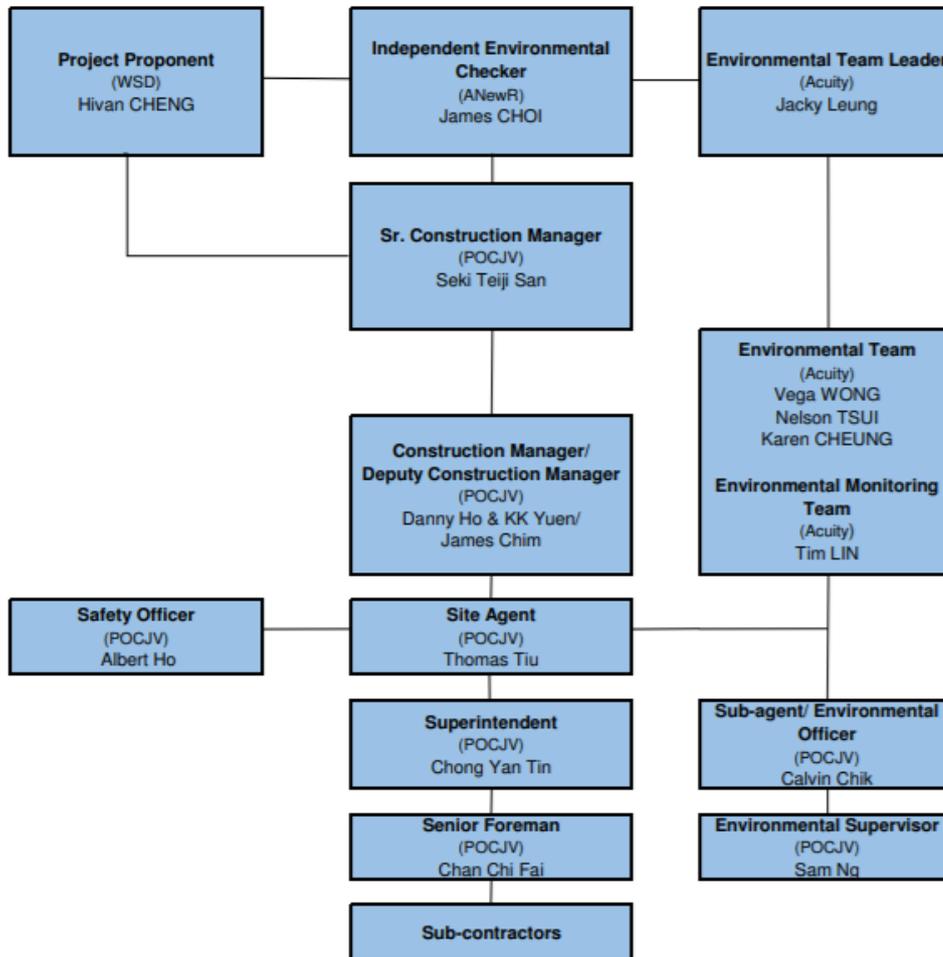

Appendix C

Construction Programme

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



13/WSD/16 - Mainlaying in Tseung Kwan O
 Outline Construction Programme (As on 31 Aug 2018)

YEAR	LOCATION		FROM	TO	2018												2019												2020												2021											
	PJ-ID	ROAD			1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12
Section A (TKO137 to Wan Po Road)																																																				
Section A1 (Open-trench)	-	Wan Po Road	0	362																																																
Section A2 (Pipe-Jacking)	A	Wan Po Road	362	530																																																
Section A3 (Open-trench)	-	Wan Po Road	530	1379																																																
Section A4 (Pipe-Jacking)	B	Wan Po Road	1379	2268																																																
Section A5 (Open-trench)	-	Wan Po Road	2268	4113																																																
Section B (Po Yap Road to Po Hong Road)																																																				
Section B1 (Pipe-Jacking)	C	Po Yap Road	4113	4200																																																
Section B2 (Open-trench)	-	Po Yap & Po Hong Rd	4200	5500																																																
Section B3 (Pipe-Jacking)	D1 & D2	Po Hong & Ling Hong Rd	5500	5600																																																
Section B4 (Open-trench)	-	Ling Hong Road	5600	5799																																																
Section B5 (Pipe-Jacking)	E	Po Hong Road	5799	5838																																																
Section B6 (Open-trench)	-	Po Hong Road	5838	6254																																																
Section B7 (Pipe-Jacking)	F	Po Hong Road	6254	6368																																																
Section B8 (Open-trench)	-	Po Hong Road	6368	7250																																																
Section C (Po Lam Road to Tsui Lam to TKOFWPSR*)																																																				
Section C1 (Open-trench)	-	Po Lam Road	7250	7740																																																
Section C2 (Pipe-Jacking)	G	Tsui Lam Road	7740	7770																																																
Section C3 (Open-trench)	-	Tsui Lam Road	7770	8300																																																
Section C4 (Slope)	-	TKOFWPSR	8300	8376																																																

Commencement of works at CH.A 720 on 30 Aug 2018.
 *TKOFWPSR - Tseung Kwan O Fresh Water Primary Service Reservoir
 **Remaining 1581m within TKO137 with site possession from Nov 2019

Appendix D

Layout of Major Construction Works Undertaken during the Reporting Quarter

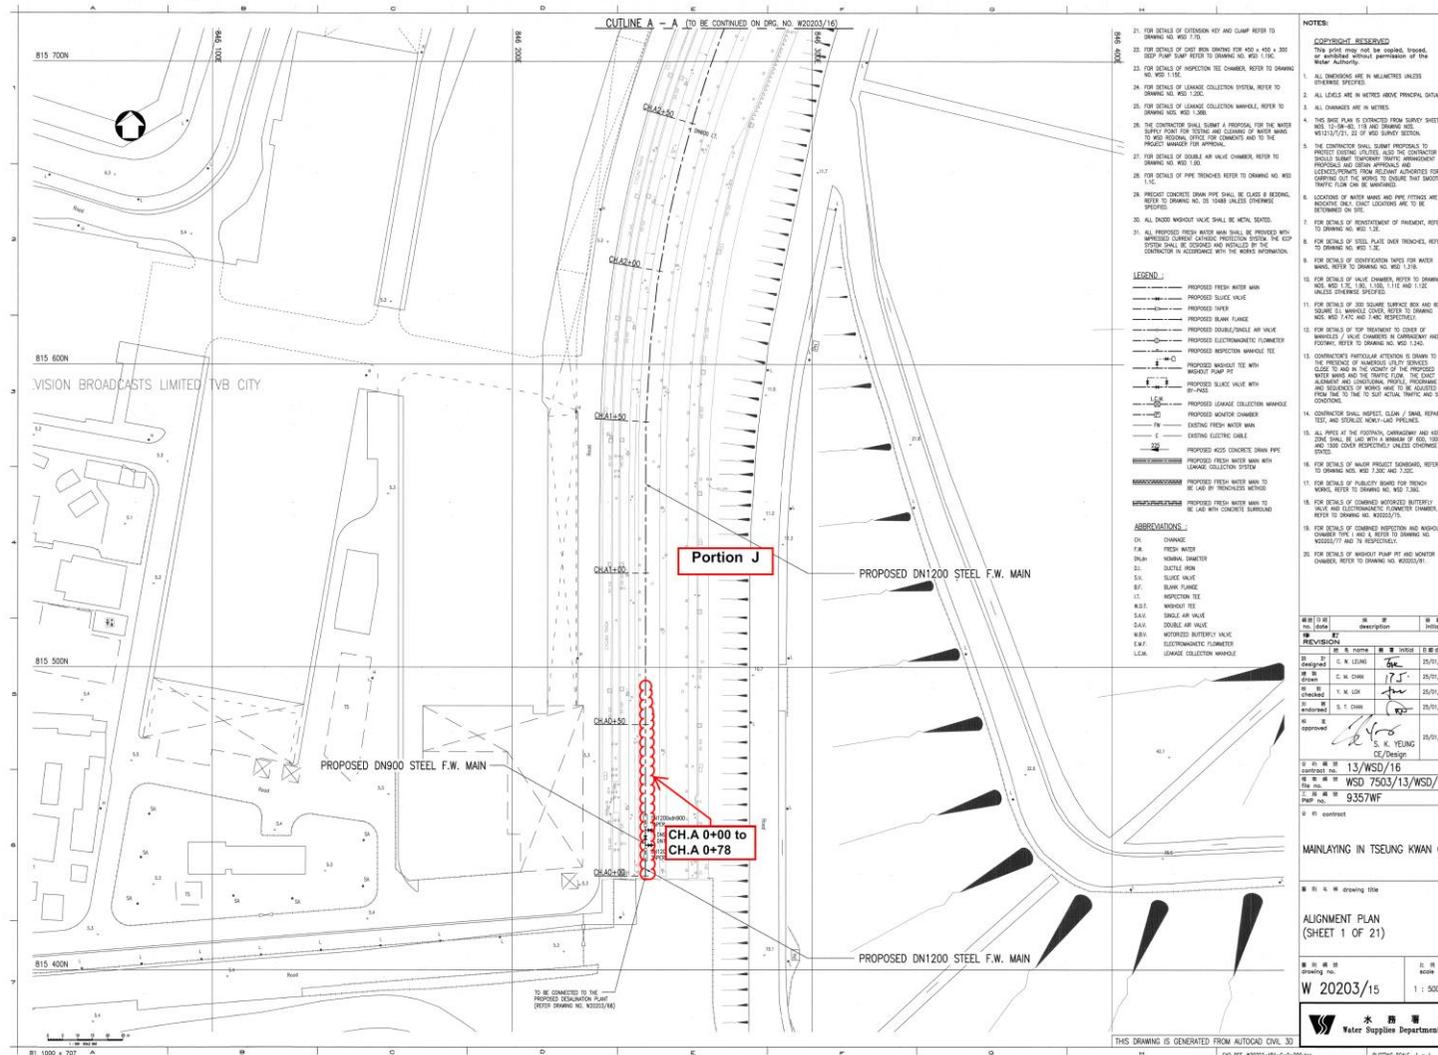


Figure D1. Location Plan for Portion J - CH.A 0+00 to CH.A 0+78

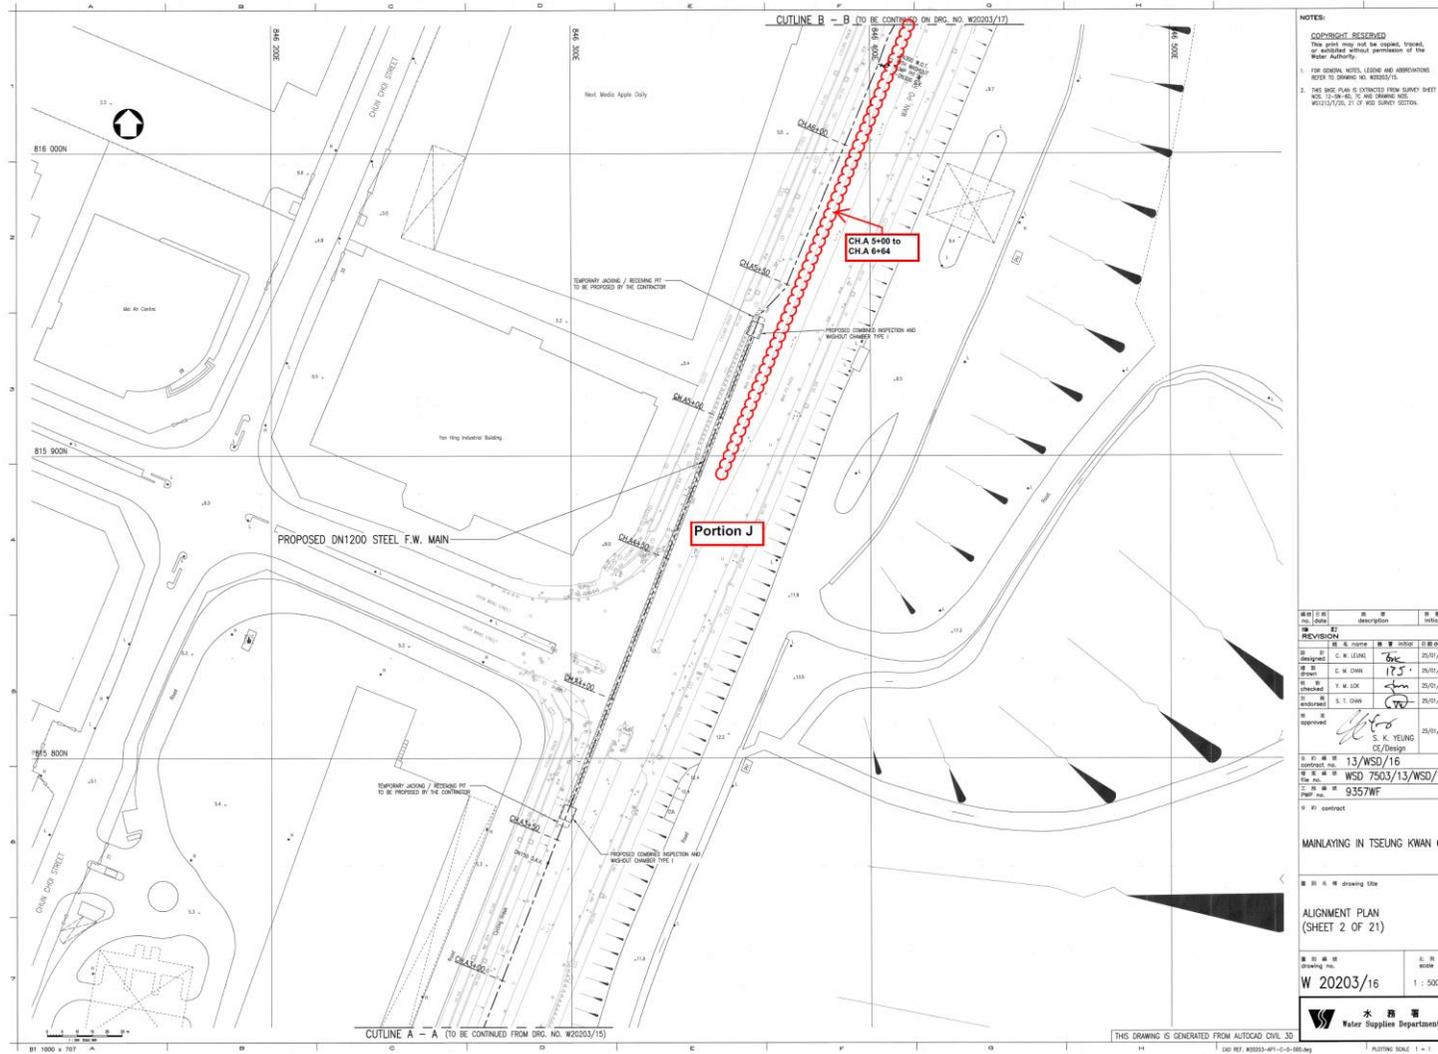


Figure D2a. Location Plan for Portion J - CH.A 5+00 to CH.A 6+70

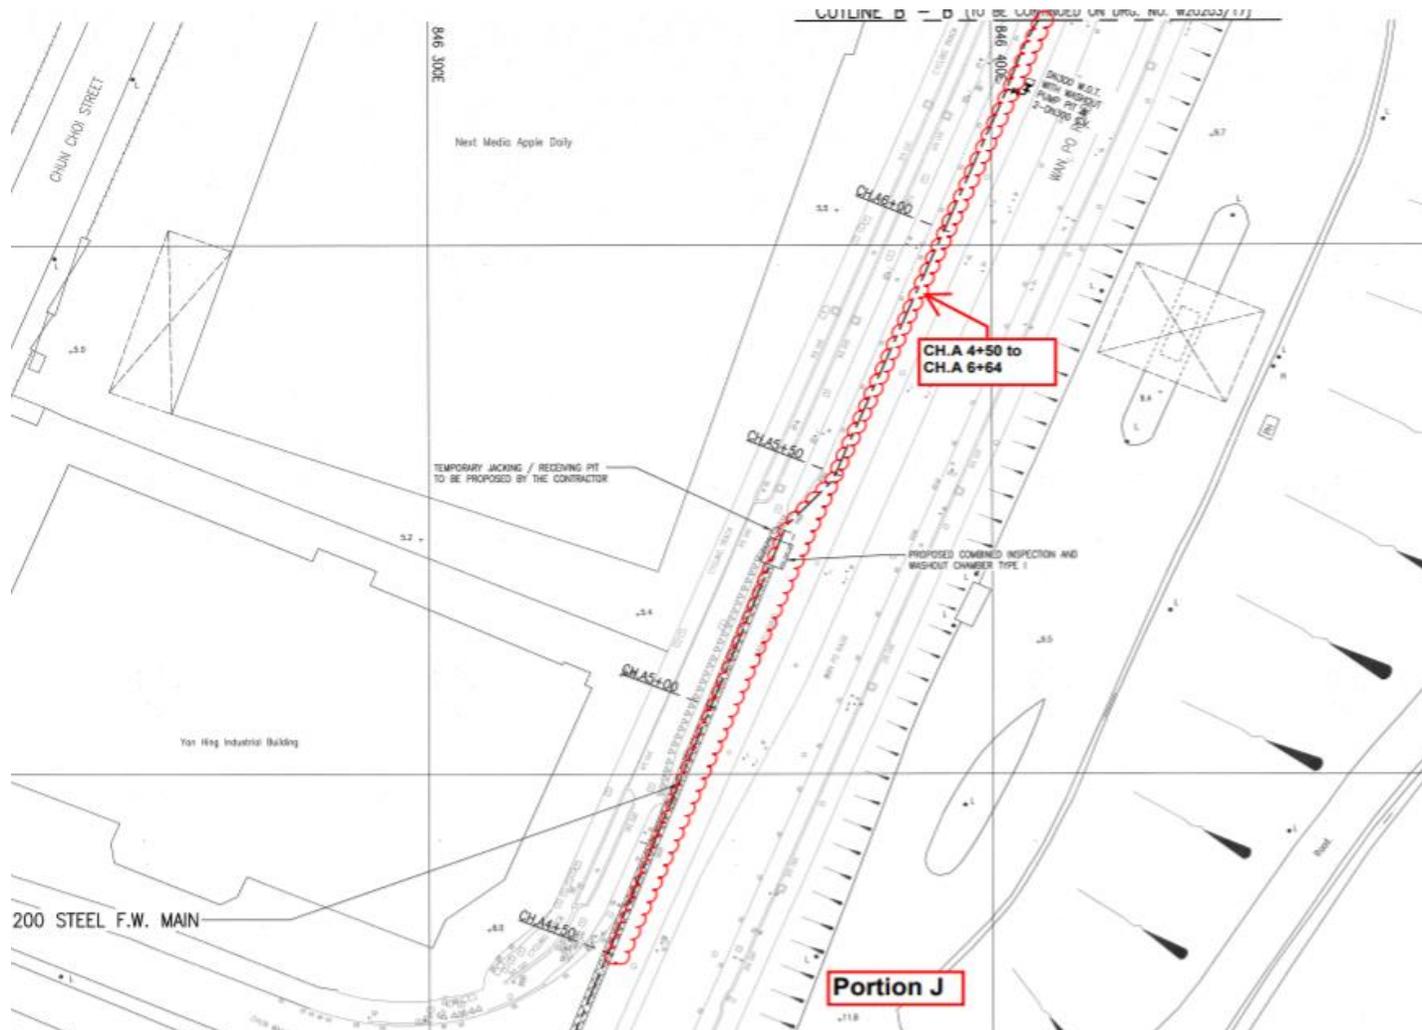


Figure D2b. Location Plan for Portion J - CH.A 4+50 to CH.A 6+64

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020

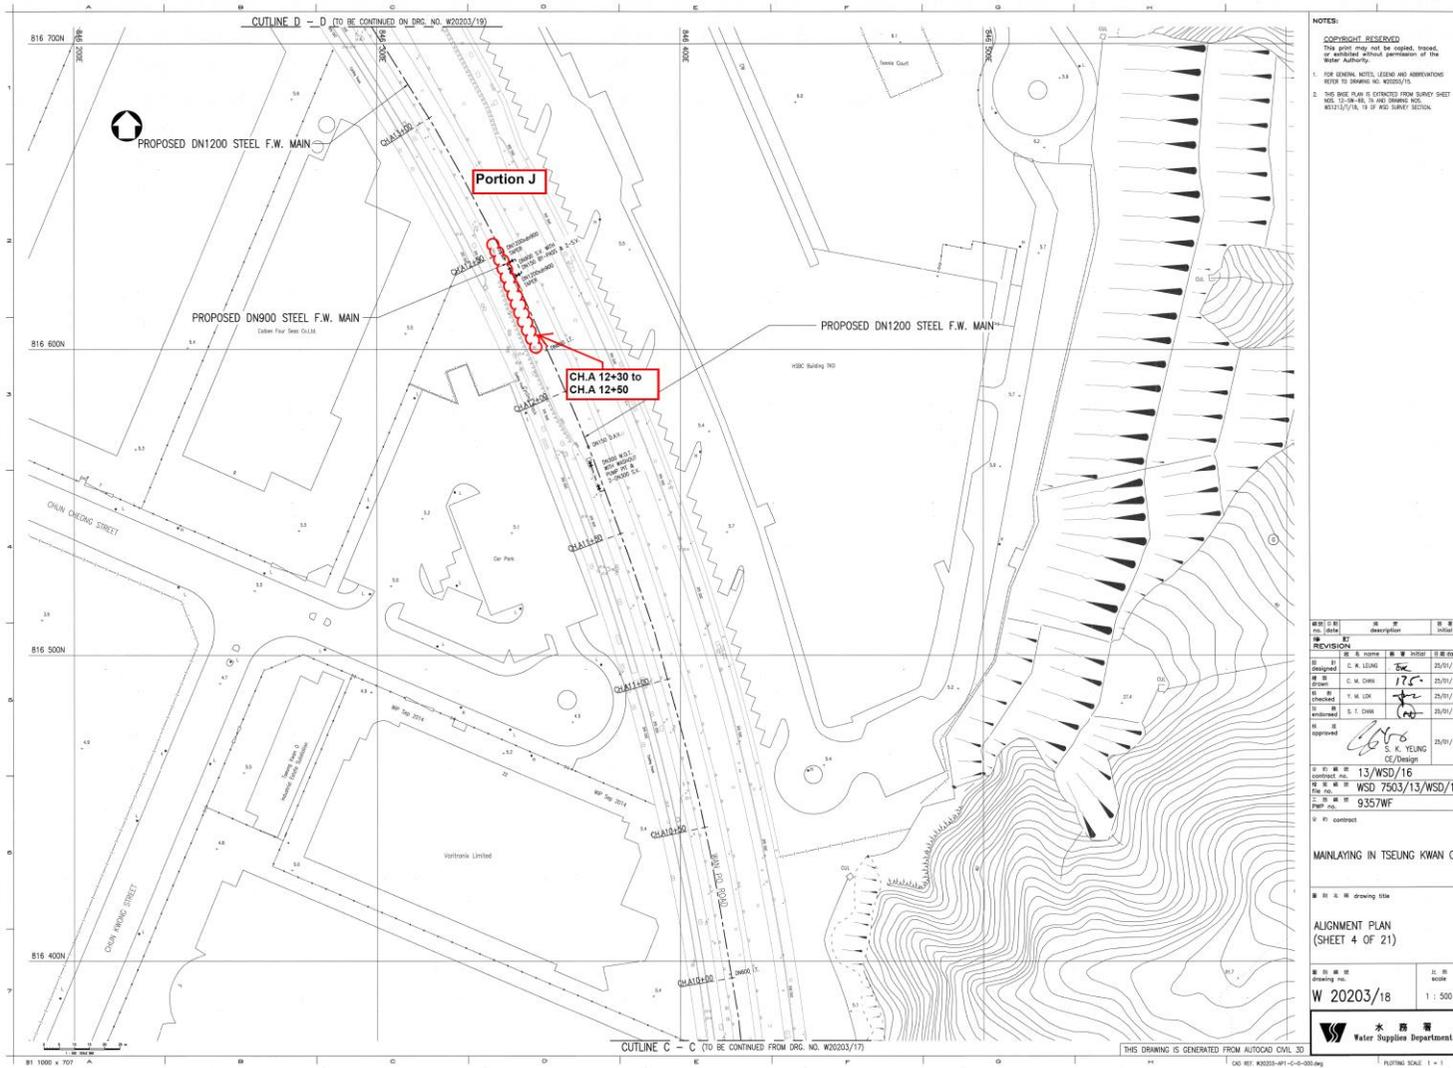


Figure D3. Location Plan for Portion J - CH.A 12+30 to CH.A 12+50

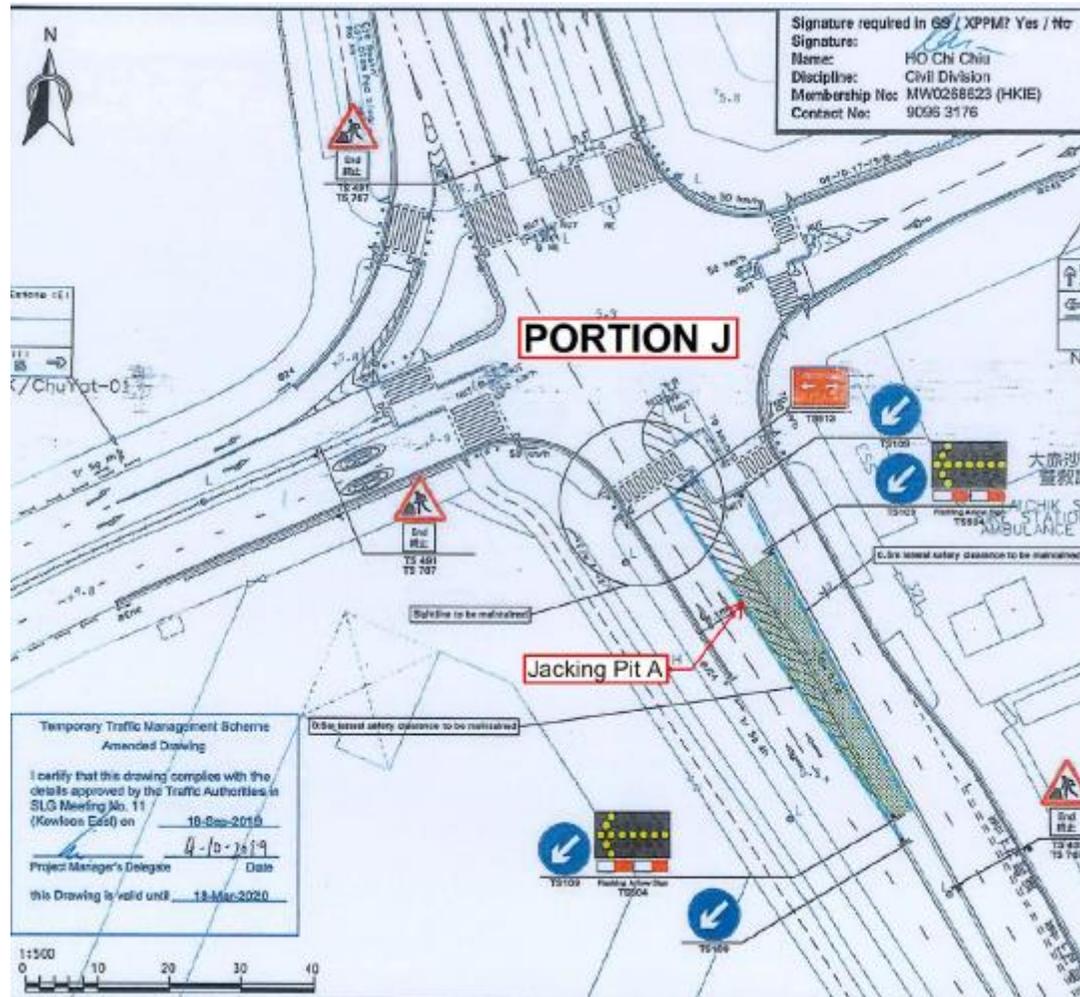


Figure D4. Location Plan for Portion J – (Pit A)



Figure D6. Location Plan for Portion J – (Pit C)

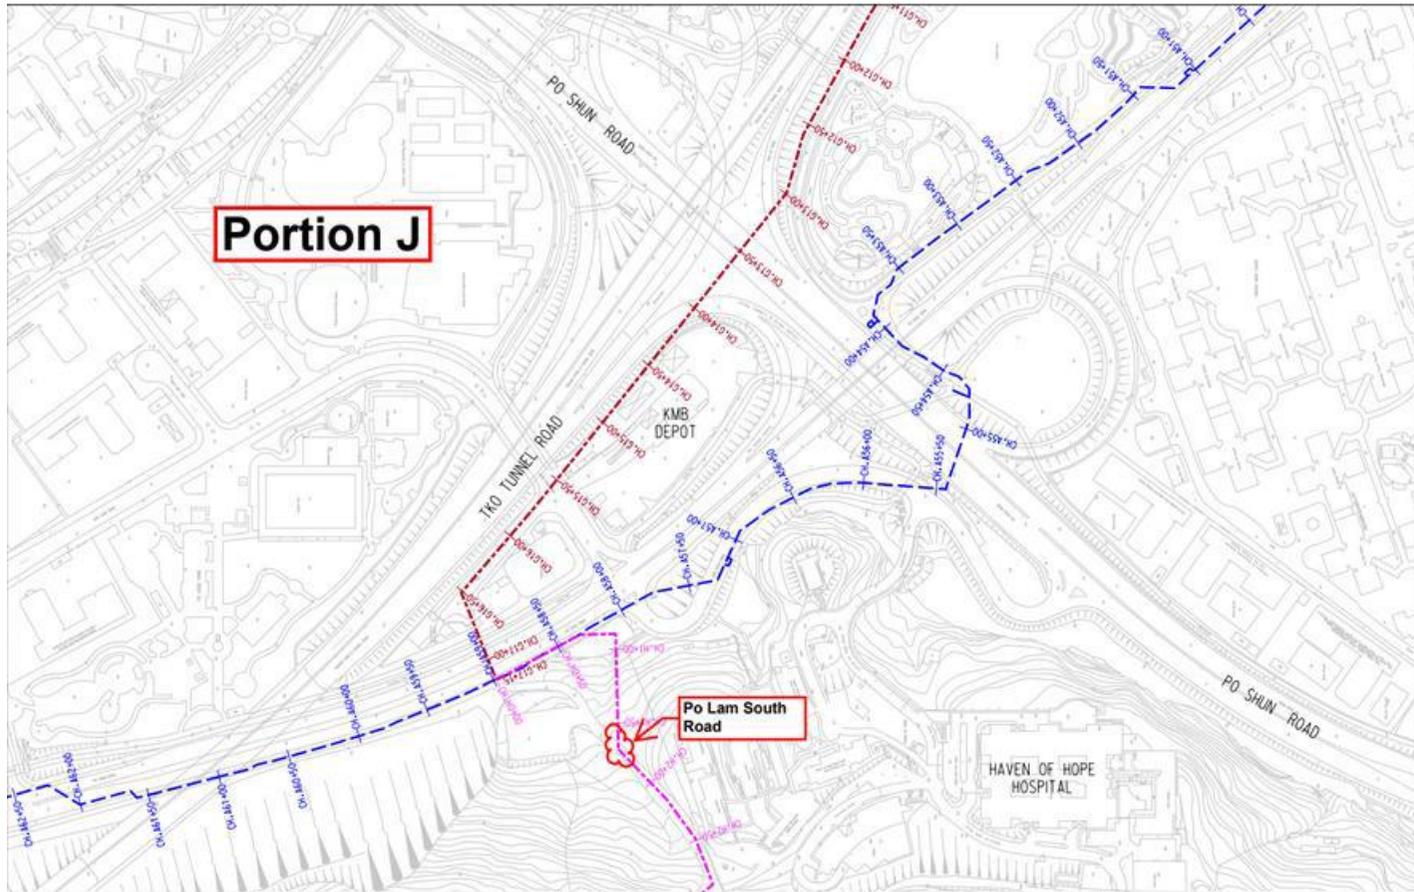


Figure D7a. Location Plan for Portion J - Mau Wu Tsai 1 (Po Lam South Road 1)

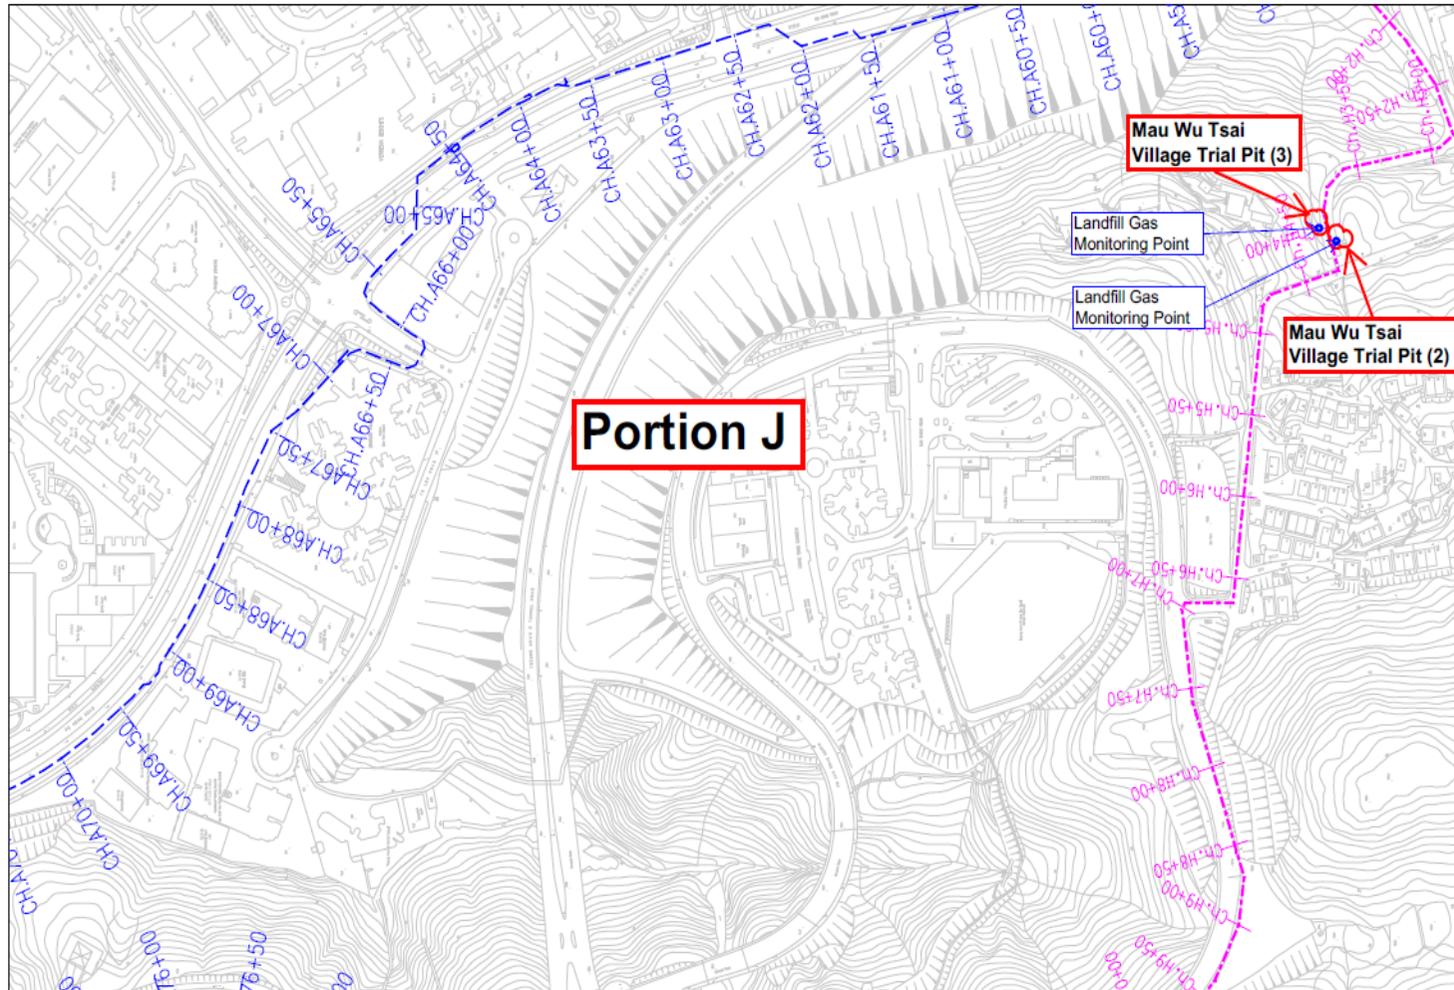


Figure D7c. Location Plan for Portion J - Mau Wu Tsai 2 (Po Lam South Road 3)

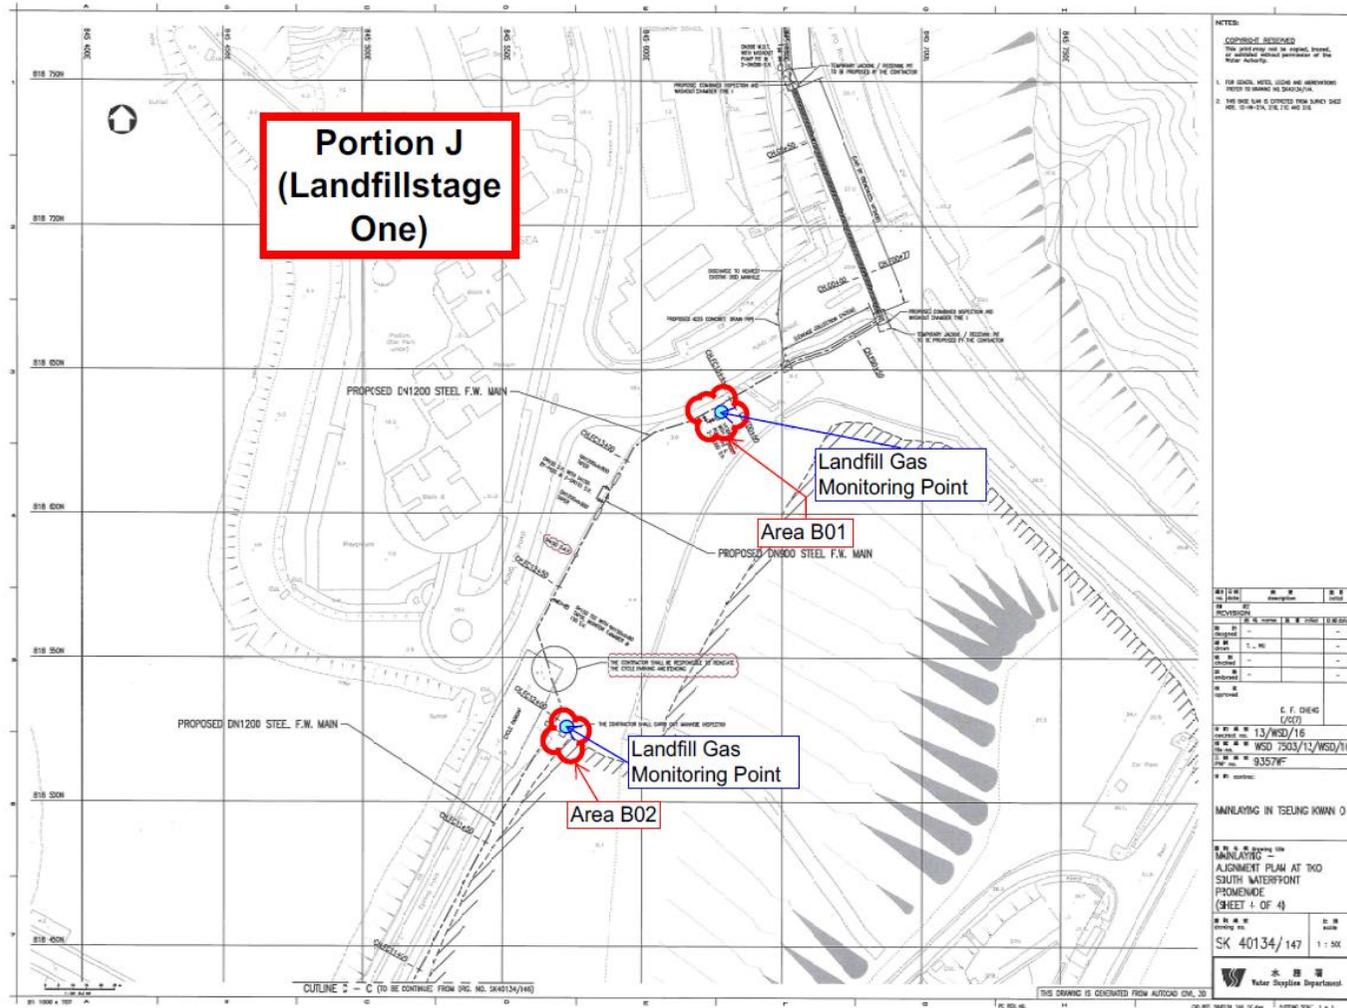


Figure D9a: Location Plan for Portion J – Landfill Stage 1

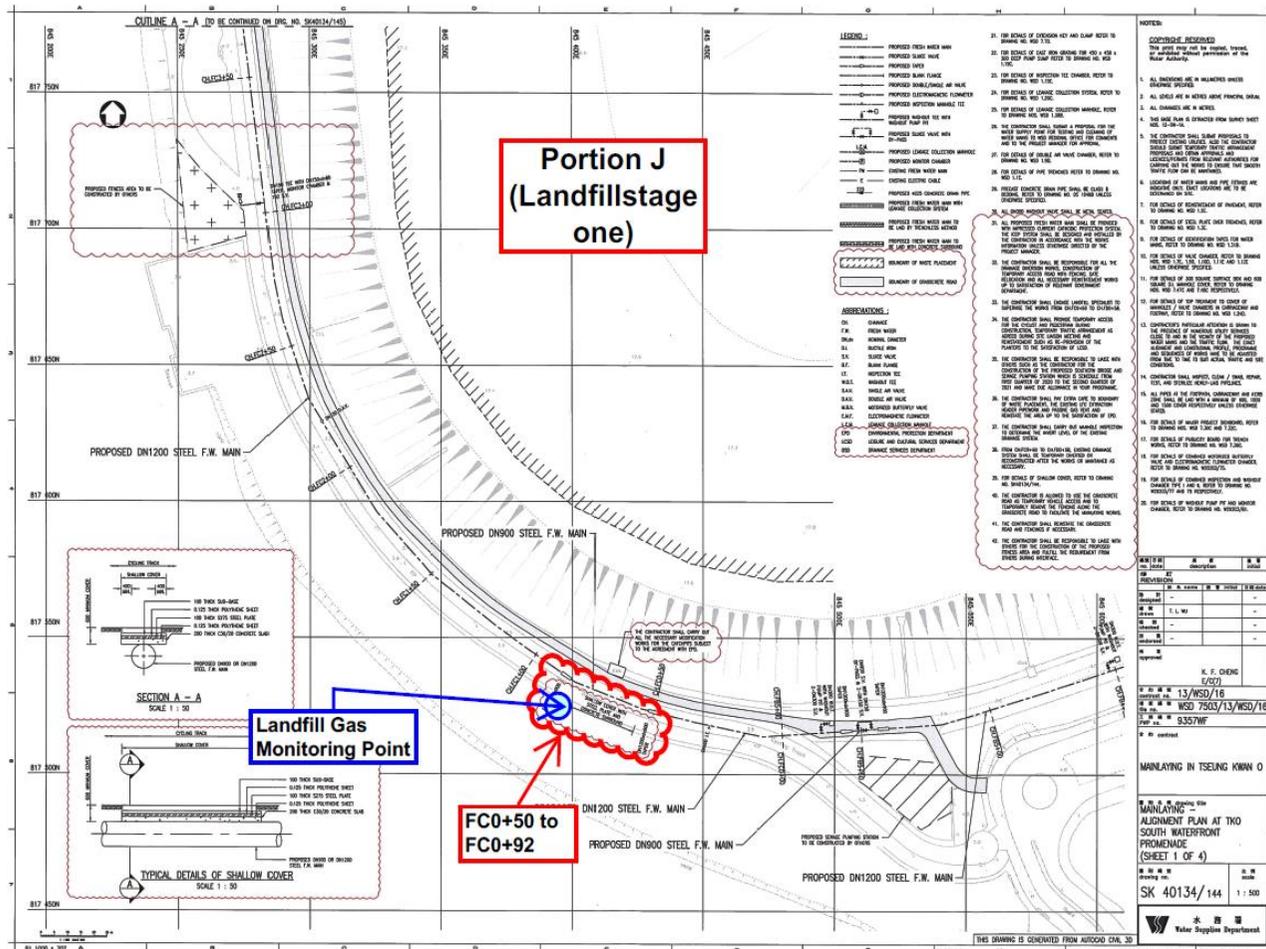


Figure D9b: Location Plan for Portion J – Landfill Stage 1 (FC0+50-FC0+92)

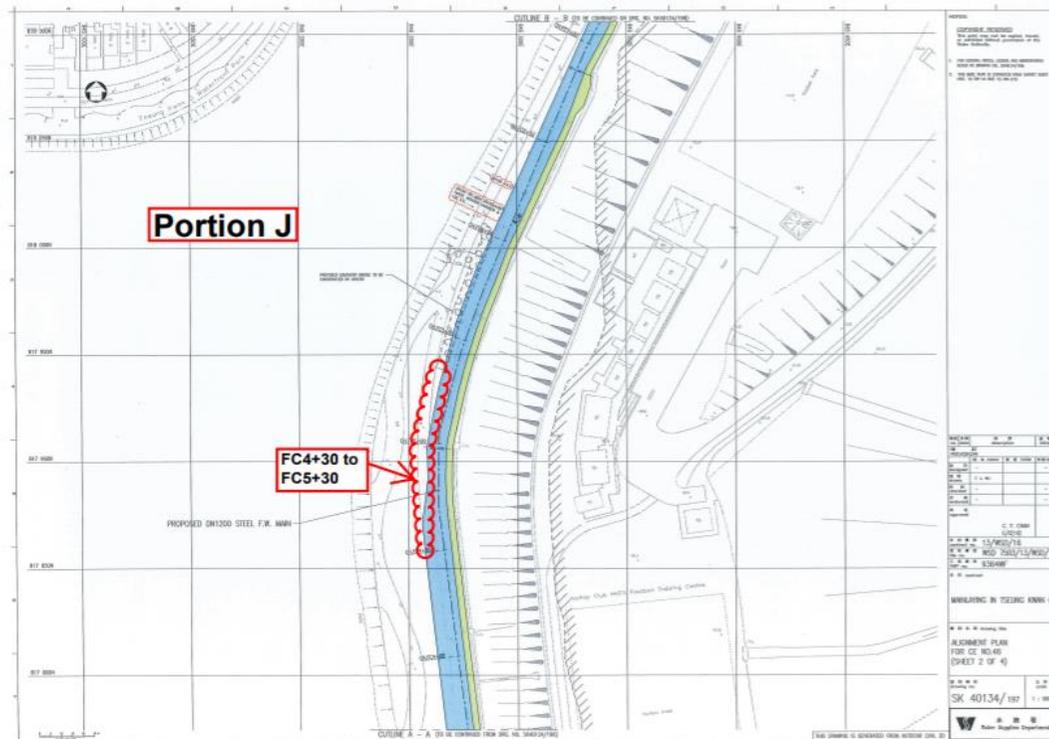


Figure D9c: Location Plan for Portion J – Landfill Stage 1 (FC4+30-FC5+30)

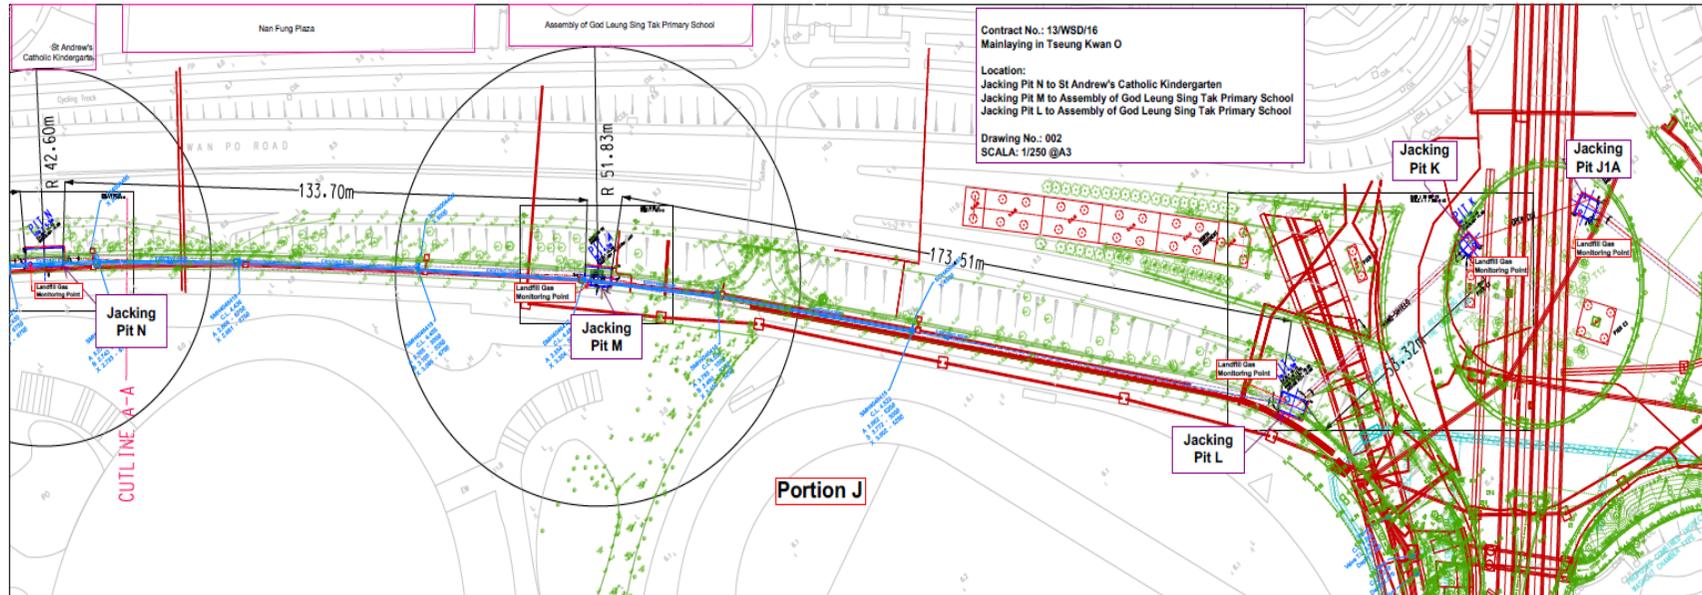


Figure D10a: Location Plan for Portion J – Pit L-M-N, J1A, K

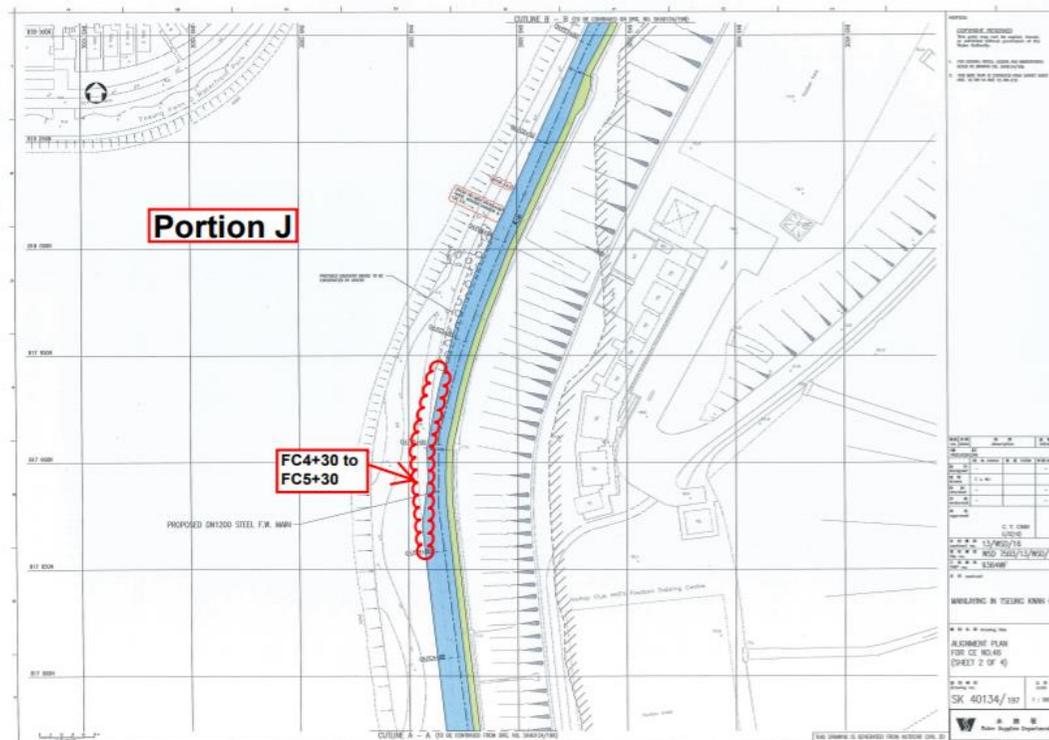


Figure D10c: Location Plan for Portion J – Pit Q

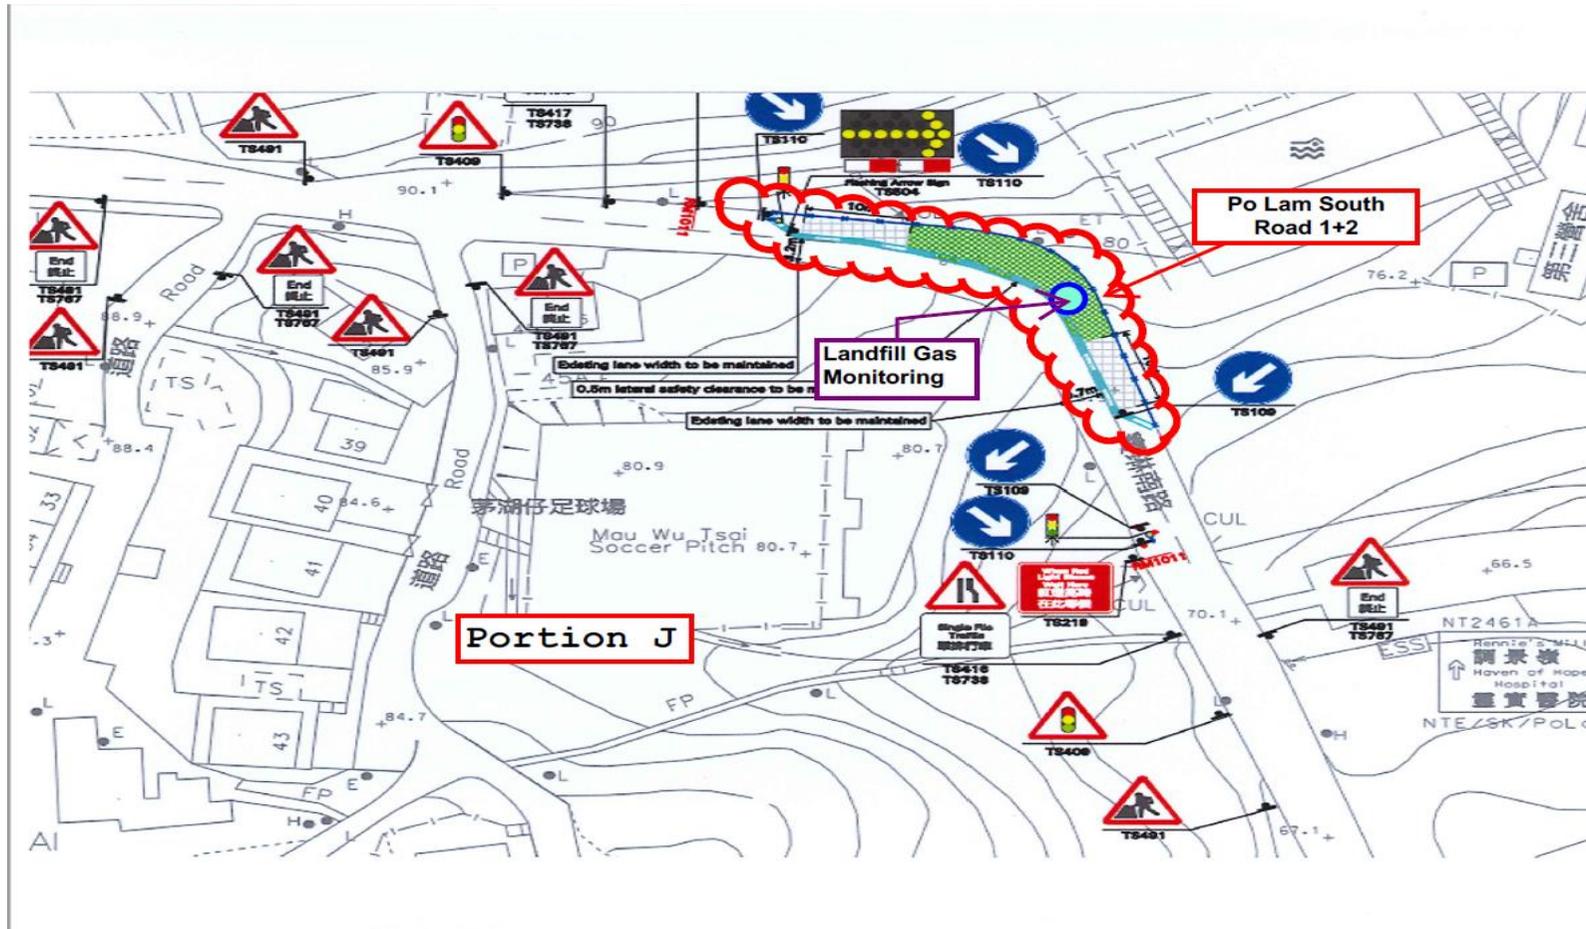


Figure D11: Location Plan for Portion J – Po Lam South Road

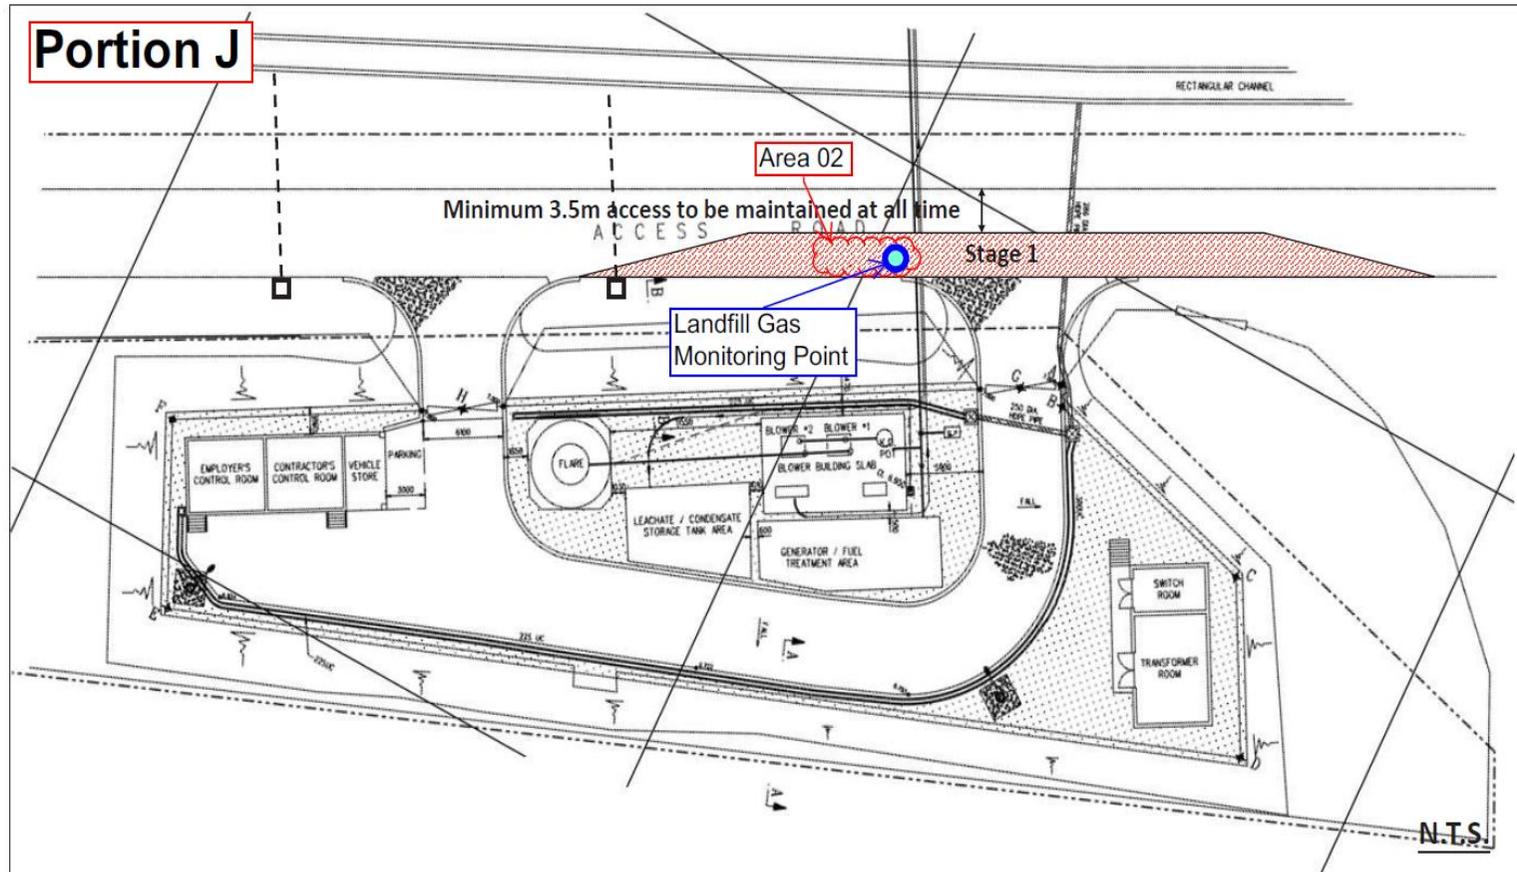


Figure D12: Location Plan for Portion J – Area A02

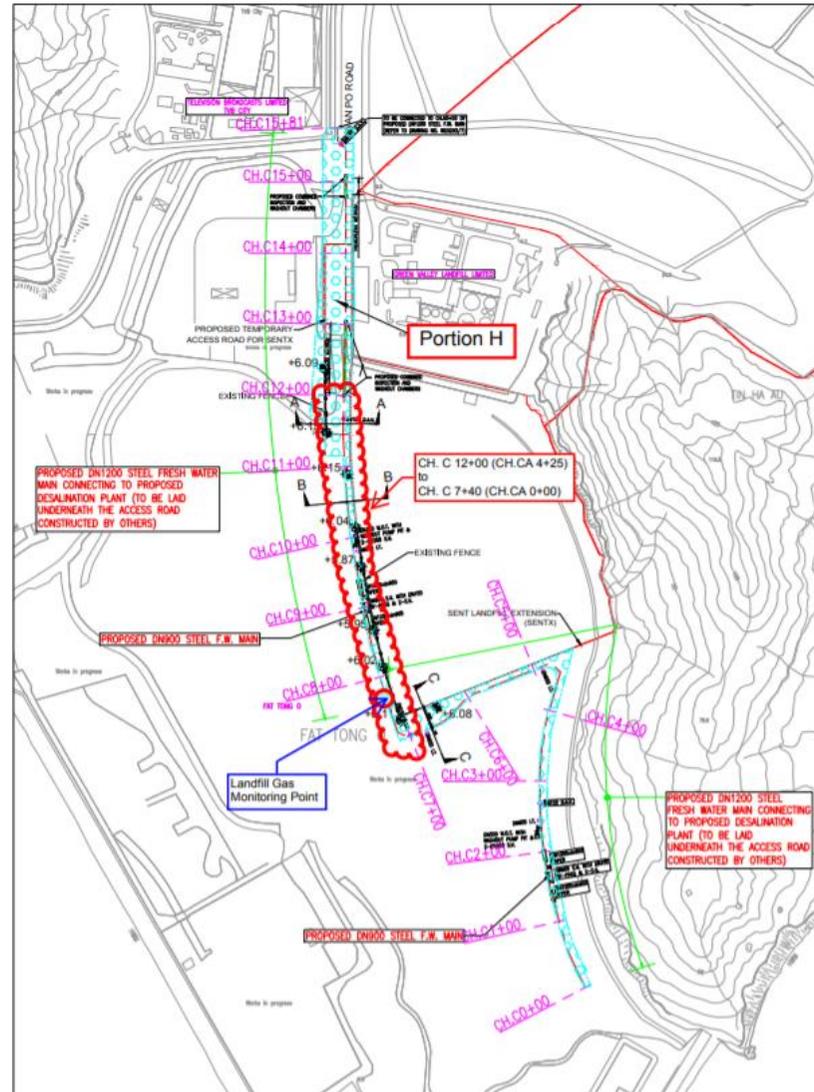


Figure D13. Location Plan for Portion H– CH.C 7+40 (CH.CA 0+00) to CH.C 12+00 (CH.CA 04+25)

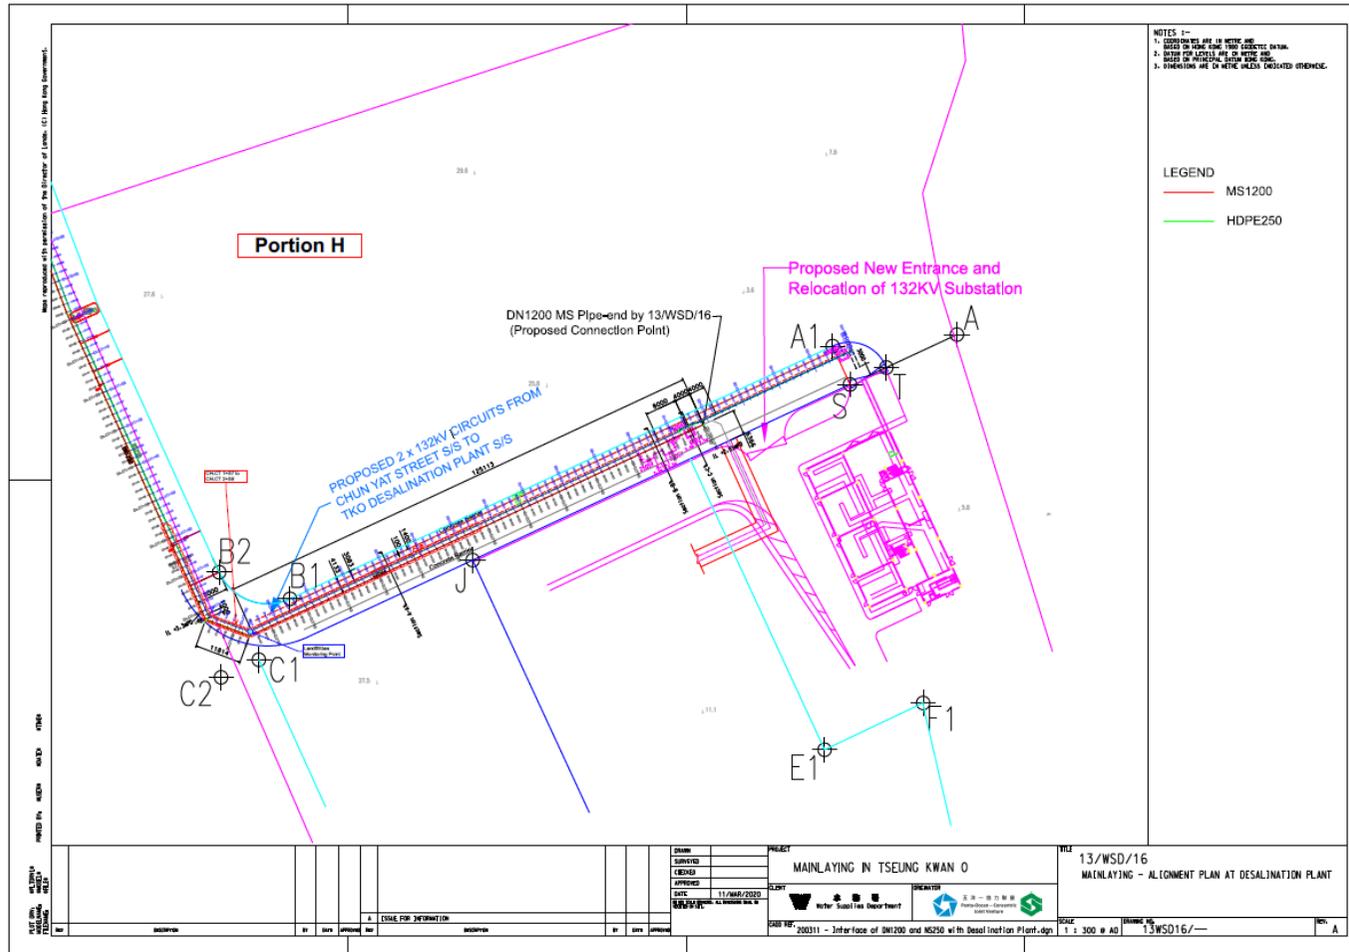


Figure D14a. Location Plan for Portion H: CH.CT 0+07 – 2+58

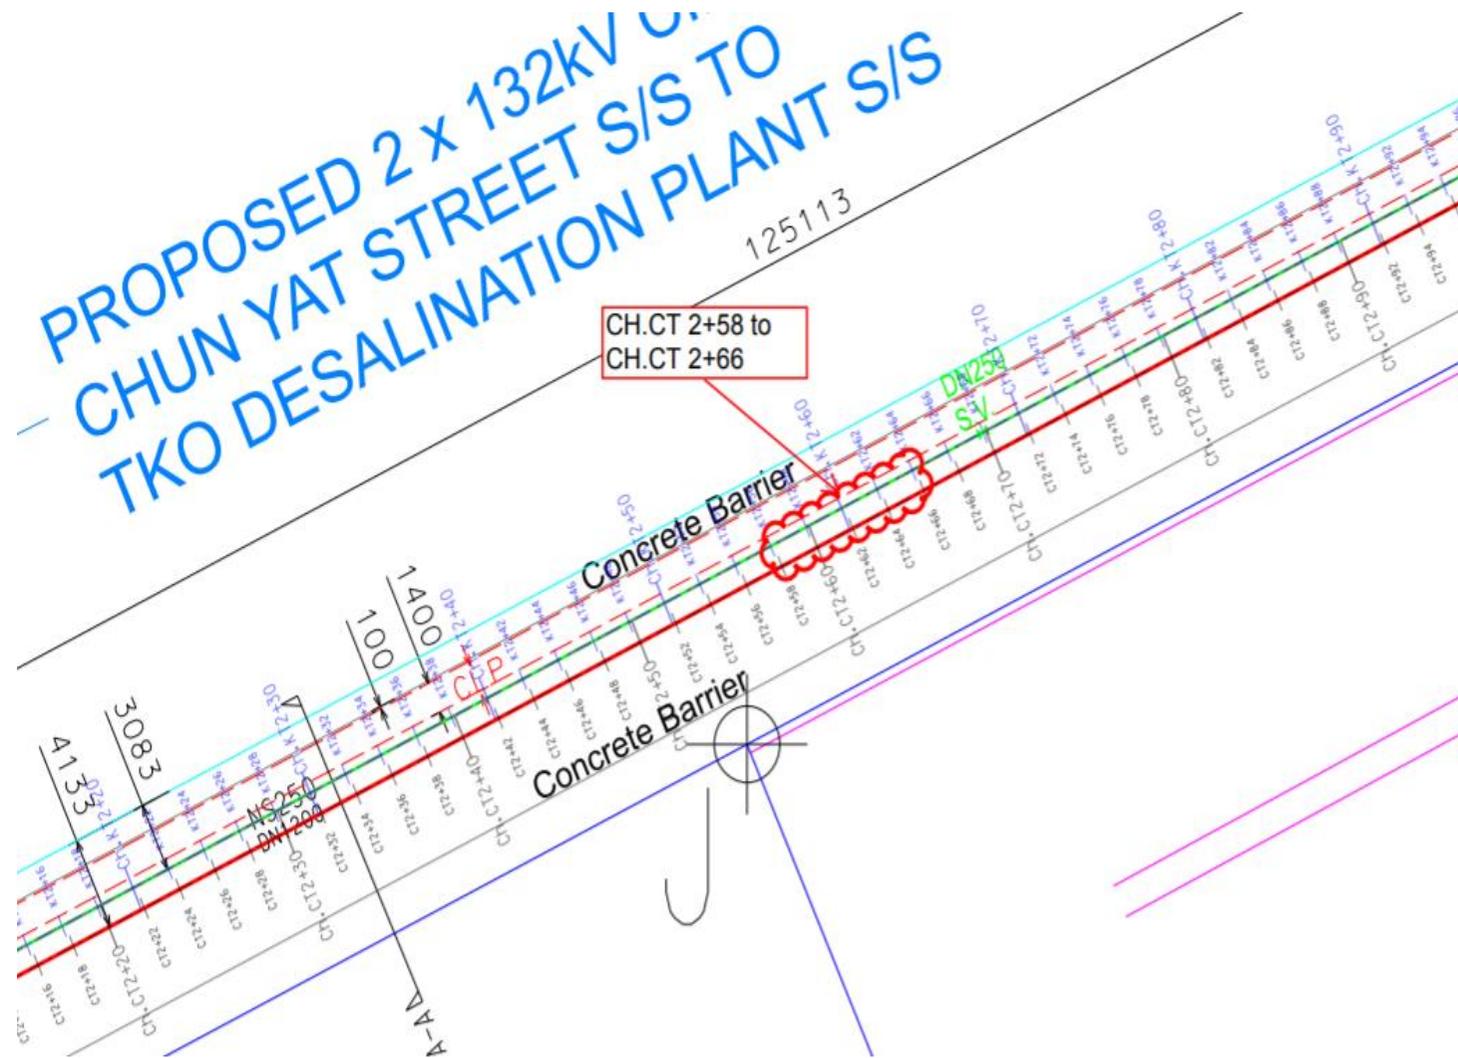


Figure D14b. Location Plan for Portion H: CH.CT 2+58 – 2+66

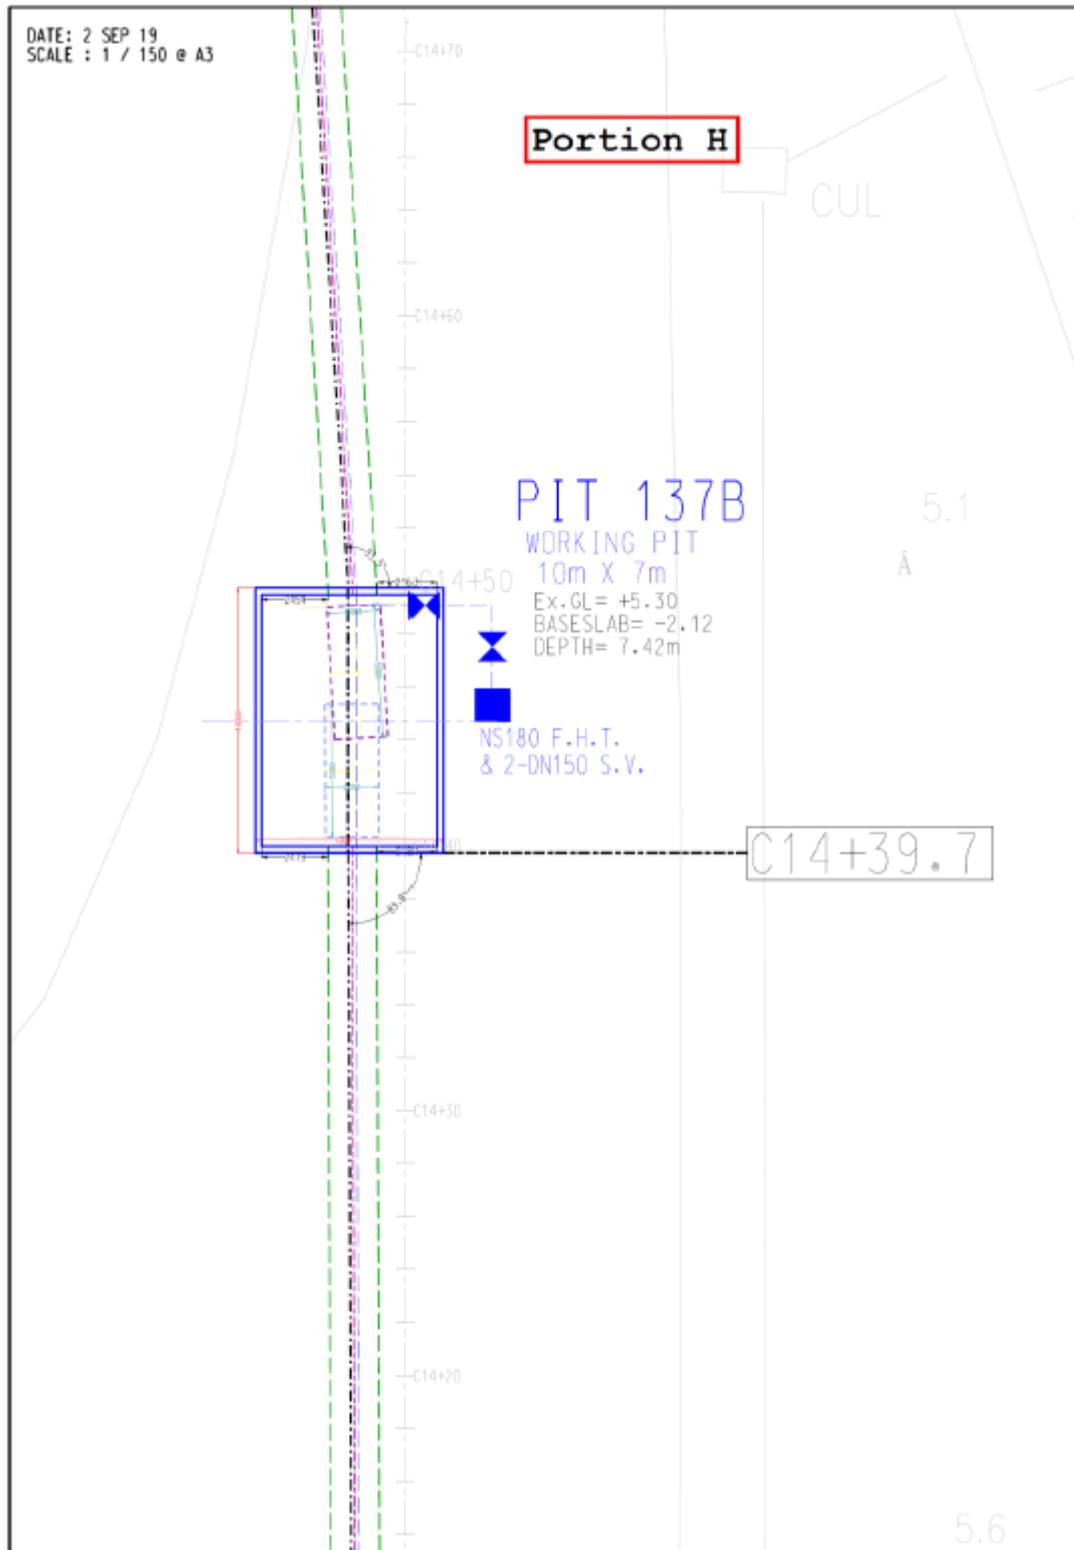


Figure D15a. Location Plan for Portion H – Pit 137 B

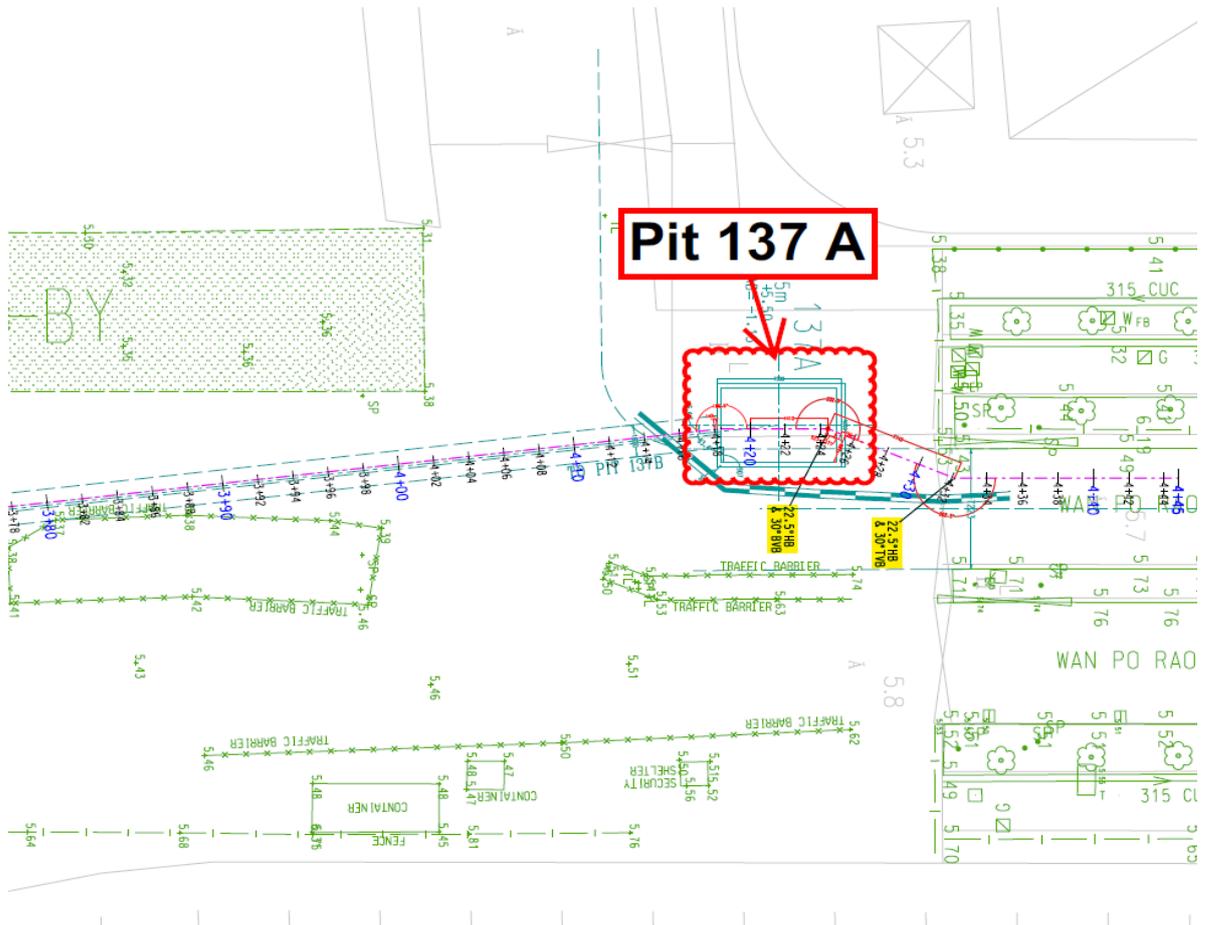


Figure B15b. Location Plan for Portion H- Pit 137A

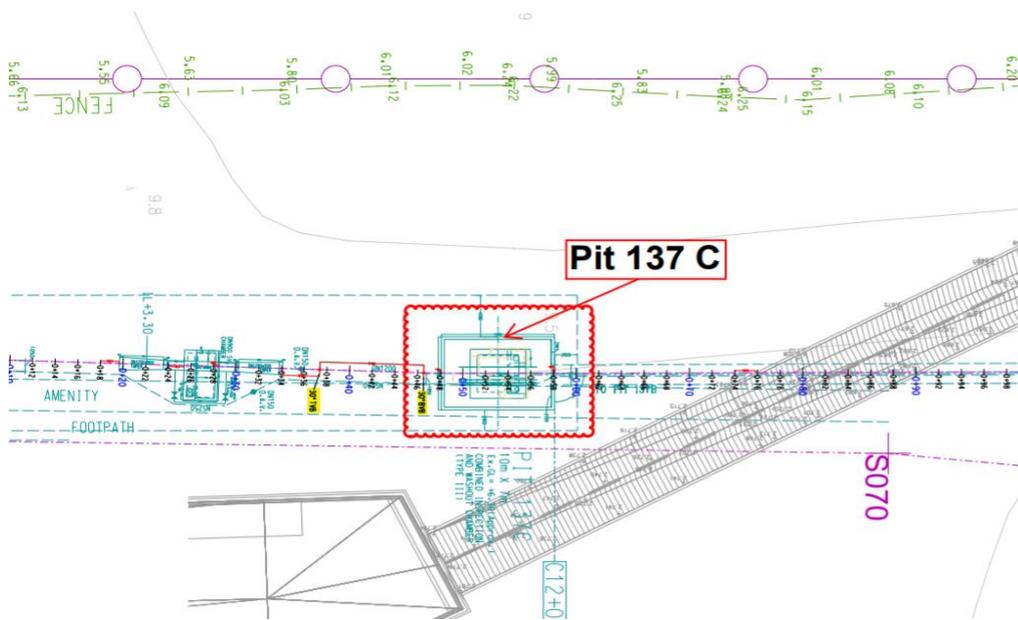


Figure B15c. Location Plan for Portion H- Pit 137C

Appendix E

Waste Flow Table

Monthly Summary Waste Flow Table

Name of Department: WSD Contract No. / Works Order No.: 13/WSD/16

Monthly Summary Waste Flow Table for August to October 2020

Month	Actual Quantities of <u>Inert</u> Construction Waste Generated Monthly					
	Total Quantity Generated (see Note 4)	Hard Rock and Large Broken Concrete (see Note 3)	Reused in the Contract	Reused in other Projects	Disposed of as Public Fill	Imported Fill (see Note 1)
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)
2018	1.157	0.063	0.000	0.000	1.157	0.518
2019	5.178	0.043	2.211	0.000	2.520	3.200
Jan 2020	0.153	0.003	0.000	0.000	0.153	0.077
Feb 2020	0.186	0.010	0.000	0.000	0.186	0.170
Mar 2020	0.282	0.005	0.000	0.000	0.282	0.201
Apr 2020	0.497	0.016	0.000	0.000	0.497	0.069
May 2020	1.294	0.306	0.291	0.000	1.003	0.030
Sub-total	2.412	0.340	0.291	0.000	2.121	0.547
Jun 2020	0.948	0.076	0.000	0.000	0.948	0.200
Jul-2020	1.514	0.021	0.000	0.000	1.514	0.075
Aug-2020	1.272	0.071	0.000	0.000	1.272	0.111
Sep-2020	1.423	0.148	--	--	1.423	0.026
Oct-2020	1.470	0.120	--	--	1.470	0.025
Total for 2020	9.039	0.776	0.291	0.000	8.748	0.984

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



Month	Actual Quantities of <u>Non-inert</u> Construction Waste Generated Monthly				
	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste	Others, e.g. General Refuse disposed at Landfill
	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
2018	0.000	0.417	0.000	0.000	0.139
2019	0.000	0.062	0.000	0.000	0.102
Jan 2020	0.000	0.055	0.000	0.000	0.002
Feb 2020	0.000	0.050	0.000	0.000	0.001
Mar 2020	0.000	0.052	0.000	0.000	0.001
April 2020	0.000	0.043	0.000	0.000	0.002
May 2020	0.000	0.058	0.000	0.000	0.020
Sub-total	0.000	0.258	0.000	0.000	0.026
Jun-2020	0.000	0.057	0.000	0.000	0.003
Jul-2020	0.000	0.050	0.000	0.000	0.001
Aug-2020	0.000	0.048	0.000	0.000	0.000
Sep-2020	0.000	0.045	0.000	0.000	0.003
Oct-2020	0.000	0.040	0.000	0.000	0.002
Total for 2020	0.000	0.498	0.000	0.000	0.035

Notes:

1. The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
2. Plastic refer to plastic bottles/containers, plastic sheets/foam from packaging materials.
3. Broken concrete for recycling into aggregate.

Appendix F

Summary of Implementation Status of Environmental Mitigation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
Air Quality								
S4.8.1	Impervious dust screen or sheeting will be provided to enclose scaffolding from the ground floor level of building for construction of superstructure of the new buildings.	Land site/ During Construction	Contractor(s)		✓		N/A	Air Pollution Control (Construction Dust)
S4.8.1	Impervious sheet will be provided for skip hoist for material transport.	Land site/ During Construction, particularly dry season	Contractor(s)		✓		N/A	
S4.8.1	The area where dusty work takes place should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after dusty activities as far as practicable.	Land site/ During Construction	Contractor(s)		✓		Implemented, rectified after observation	
S4.8.1	All dusty materials should be sprayed with water or a dust suppression chemical immediately prior to any loading, unloading or transfer operation.	Land site/ During Construction	Contractor(s)		✓		Implemented, rectified after observation	
S4.8.1	Dropping heights for excavated materials should be controlled to a practical height to minimise the fugitive dust arising from unloading.	Land site/ During Construction	Contractor(s)		✓		Implemented	
S4.8.1	During transportation by truck, materials should not be loaded to a level higher than the side and tail boards, and should be dampened or covered before transport.	Land site/ During Construction	Contractor(s)		✓		Implemented	
S4.8.1	Wheel washing device should be provided at the exits of the work sites. Immediately before leaving a construction site, every vehicle shall be washed to remove any dusty material from its body and wheels as far as practicable.	Land site/ During Construction	Contractor(s)		✓		N/A	

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S4.8.1	Road sections between vehicle-wash areas and vehicular entrance will be paved.	Land site/ During Construction	Contractor(s)		✓		Implemented	
S4.8.1	Hoarding of not less than 2.4m high from ground level will be provided along the length of the Project Site boundary.	Land site/ During construction	Contractor(s)	✓	✓		N/A	
S4.8.1	Haul roads will be kept clear of dusty materials and will be sprayed with water so as to maintain the entire road surface wet at all times.	Land site/ During construction	Contractor(s)		✓		Implemented, rectified after observation	
S4.8.1	Temporary stockpiles of dusty materials will be either covered entirely by impervious sheets or sprayed with water to maintain the entire surface wet all the time.	Land site/ During construction	Contractor(s)		✓		Implemented, rectified after observation	
S4.8.1	Stockpiles of more than 20 bags of cement, dry pulverised fuel ash and dusty construction materials will be covered entirely by impervious sheeting sheltered on top and 3-sides.	Land site/ During construction	Contractor(s)		✓		Implemented.	
S4.8.1	All exposed areas will be kept wet always to minimise dust emission.	Land site/ During construction	Contractor(s)		✓		Implemented, rectified after observation	
S4.8.1	Ultra-low-sulphur diesel (ULSD) will be used for all construction plant on-site, as defined as diesel fuel containing not more than 0.005% sulphur by weight) as stipulated in Environment, Transport and Works Bureau Technical Circular (ETWB-TC(W)) No 19/2005 on Environmental Management on Construction Sites.	Land site/ During construction/ During Operation	Contractor(s)		✓	✓	Implemented	Environment, Transport and Works Bureau Technical Circular (ETWB- TC(W)) No 19/2005 on Environmental Management on Construction Sites
S4.8.1	The engine of the construction equipment during idling will be switched off.	Land site/ During construction	Contractor(s)		✓		Implemented	

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S4.8.1	Concrete batching plant will be required on site. control measures recommended in the Guidance Note on a Best Practicable Means for Cement Works (Concrete Batching Plant) (BPM 3/2 (93)) will be implemented. The control measures recommended in the Guidance Note on a Best Practicable Means for Cement Works (Concrete Batching Plant) (BPM 3/2 (93)) will be implemented.	Land site/ During construction	Contractor(s)		✓		N/A	Guidance Note on a Best
S4.8.1	Regular maintenance of construction equipment deployed on-site will be conducted to prevent black smoke emission.	Land site/ During construction	Contractor(s)		✓		Implemented	
S4.10	To ensure proper implementation of the recommended dust mitigation measures and good construction site practices during the construction phase, environmental site audits on weekly basis is recommended throughout the construction period.	Land site/ During construction	Contractor(s)/ Environmental Team (ET) & Independent Environmental Checker (IEC)		✓		Implemented	

Note: D – Design stage C – Construction O – Operation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
Noise								
S5.7	Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction phase.	All area/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Silencers or mufflers on construction equipment will be utilised and will be properly maintained during the construction phase.	Noise control/ During construction	Contractor(s)		✓		NA	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Mobile plant, if any, will be sited as far away from NSRs as possible.	Noise control/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum.	Noise control/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Plants known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.	Noise control/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities.	Noise control/ During construction	Contractor(s)		✓		N/A	A Practical Guide for the Reduction of Noise from Construction Works,

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S5.7	Use of Quite Powered Mechanical Equipment (QPME).	Noise control/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Movable noise barriers of 3m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater than its height. The noise barrier material should have a superficial surface density of at least 7 kg m ⁻² and have no openings or gaps.	Noise control/ During construction	Contractor(s)		✓		N/A	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	The noise insulating sheet should be deployed such that there would be no opening or gaps on the joints.	Noise control/ During construction	Contractor(s)		✓		N/A	A Practical Guide for the Reduction of Noise from Construction Works,
S5.7	Construction activities (e.g. excavation/shoring, reinstatement (asphalt), and pipe jacking) will be planned and carried out in sequence, such that items of PME proposed for these activities will not be operated simultaneously.	Noise control/ During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works
S5.7	PMEs will not be used at the works areas near educational institutions with residual impact (ie the “influence area” within a radius of 40m) during school hours in order to reduce impact to the educational institutions.	Noise control / During construction	Contractor(s)		✓		Implemented	A Practical Guide for the Reduction of Noise from Construction Works

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S5.7	Noise enclosures or acoustic sheds would be used to cover stationary PME such as generators. Portable/Movable noise enclosure made of material with superficial surface density of at least 7 kg m ⁻² may be used for screening the noise from operation of the saw/groover, concrete.	Noise control/ Pre-construction/ During construction	Contractor(s)	✓	✓		N/A	
S5.9	Sawcutting pavement, breaking up of pavement, excavation /shoring, pipe laying, backfilling, reinstatement (concrete) and pipe jacking shall be scheduled outside the examination period.	Noise control/ Pre-construction/ During construction	Contractor(s)	✓	✓		Implemented	
S5.9	In view the duration of noise exceedance at Creative Secondary School, PLK Laws Foundation College, TKO Kei Tak Primary School and School of Continuing and Professional Studies-CUHK is limited to 8 weeks, the construction work in the influence areas near the four schools shall be scheduled during long school holidays (eg summer holiday, Easter holiday or Christmas holiday, etc) as far as practicable. Scheduling the construction work for the four schools.	Noise control/ Pre-construction/ During construction	Contractor(s)	✓	✓		N/A	
S5.10	A noise monitoring programme shall be implemented for the construction phase.	Designated monitoring stations as defined in EM&A Manual/During construction phase	Environmental Team (ET)		✓		Implemented	
S5.10	The effectiveness of on-site control measures could also be evaluated through the regular site audits.	All facilities/ During construction	Contractor(s)/ Environmental Team (ET) & Independent Environmental Checker (IEC)		✓		Implemented	-

Note: D – Design stage C – Construction O – Operation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementatio n Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
Water Quality								
S6.9	Dredged marine sediment will be disposed of in a gazetted marine disposal area in accordance with marine dumping permit conditions of the Dumping at Sea Ordinance (DASO).	Marine Dredging/ During construction	Contractor(s)		✓		N/A	Dumping at Sea Ordinance (DASO)
S6.9	Disposal vessels will be fitted with tight bottom seals in order to prevent leakage of material during transport.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	Barges will be filled to a level, which ensures that material does not spill over during transport to the disposal site and that adequate freeboard is maintained to ensure that the decks are not washed by wave action.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	After dredging, any excess materials will be cleaned from decks and exposed fittings before the vessel is moved from the dredging area.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	All vessels should be well maintained and inspected before use to limit any potential discharges to the marine environment.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	All vessels must have a clean ballast system.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	No discharge of sewage/grey wastewater should be allowed. Waste water from potentially contaminated area on working vessels should be minimized and collected. These kinds of wastewater should be brought back to port and discharged at appropriate collection and treatment system.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-
S6.9	No soil waste is allowed to be disposed overboard.	Marine Dredging/ During construction	Contractor(s)		✓		N/A	-

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementatio n Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S6.9	Silt removal facilities such as silt traps or sedimentation facilities will be provided to remove silt particles from runoff to meet the requirements of the TM standard under the WPCO. The design of silt removal facilities will be based on the guidelines provided in ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented, rectified after observation	ProPECC PN 1/94 TM Standard under the WPCO
S6.9	Earthworks to form the final surfaces will be followed up with surface protection and drainage works to prevent erosion caused by rainstorms.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented	-
S6.9	Appropriate surface drainage will be designed and provided where necessary.	Land site & drainage/ During construction	Contractor(s)		✓		N/A	-
S6.9	The precautions to be taken at any time of year when rainstorms are likely together with the actions to be taken when a rainstorm is imminent or forecasted and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented	ProPECC PN 1/94
S6.9	Oil interceptors will be provided in the drainage system where necessary and regularly emptied to prevent the release of oil and grease into the storm water drainage system after accidental spillages.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented	-
S6.9	Temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge, if any, will be adequately designed for the controlled release of storm flows.	Land site & drainage/ During construction	Contractor(s)		✓		N/A	-

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementatio n Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S6.9	The temporary diverted drainage, if any, will be reinstated to the original condition when the construction work has finished or when the temporary diversion is no longer required.	Land site & drainage/ During construction	Contractor(s)		✓		N/A	-
S6.9	Appropriate numbers of portable toilets shall be provided by a licensed contractor to serve the construction workers over the construction site to prevent direct disposal of sewage into the water environment.	Land site & drainage/ During construction	Contractor(s)		✓		Implemented	-
S6.9 and S6.12	The sterilization water should be dechlorinated with total residual chlorine (TRC) level below 1 mg/L before discharge to public sewer. In situ testing of TRC should also be conducted for the discharge of chlorinated water for pipeline disinfection to ensure sufficient dechlorination before discharge to public sewer.	Sterilization of water mains prior to commissioning	Contractor(s)		✓	✓	N/A	Technical Memorandum for Effluents Discharged into Drainage and Sewerage Systems Inland and Coastal Waters
S6.9	The cleaning and flushing water should also be treated and desilted to the relevant discharge requirement stipulated in TM-DSS before discharging.	Sterilization of water mains prior to commissioning	Contractor(s)		✓	✓	N/A	Technical Memorandum for Effluents Discharged into Drainage and Sewerage Systems Inland and Coastal Waters
S6.9	Site drainage should be well maintained and good construction practices should be observed to ensure that oil, fuels, solvents and other chemicals are managed, stored and handled properly and do not enter the nearby water streams.	Land site & drainage/ During construction/ During operation	Contractor(s)		✓	✓	Implemented, rectified after observation	-

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementatio n Agent	Implementation Stage			Implementation status	Relevant Legislation & Guidelines
				D	C	O		
S6.12	Regular site inspections will be carried out in order to confirm that regulatory requirements are being met and that contractors are implementing the standard site practice and mitigation measures as proposed to reduce potential impacts to water quality.	During construction	Contractor(s)/ Environmental Team (ET) & Independent Environmental Checker (IEC)		✓		Implemented	-

Note: D – Design stage C – Construction O – Operation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
Waste Management								
S8.5	Nomination of approved personnel to be responsible for standard site practices, arrangements for collection and effective disposal to an appropriate facility of all wastes generated at the site.	Contract mobilisation/ During construction	Contractor(s)		✓		Implemented	-
S8.5	Training of site personnel in proper waste management and chemical handling procedures. Training will be provided to workers on the concepts of site cleanliness and appropriate waste management procedures, including waste reduction, reuse and recycling at the beginning of the construction works.	Contract mobilisation/ During construction	Contractor(s)		✓		Implemented	-
S8.5	Provision of sufficient waste disposal points and regular collection for disposal.	All area/ During construction/ During operation	Contractor(s)		✓	✓	Implemented	DEVB TC(W) No. 8/2010, Enhanced Specification for Site Cleanliness and Tidiness.
S8.5	Appropriate measures to reduce windblown litter and dust transportation of waste by either covering trucks or by transporting wastes in enclosed containers.	All area/ During construction	Contractor(s)		✓		Implemented	DEVB TC(W) No. 8/2010, Enhanced Specification for Site Cleanliness and Tidiness.
S8.5	A waste management plan (WMP) as stated in the “ <i>ETWB TC(W) No. 19/2005, Environmental Management on Construction Sites</i> ” for the amount of waste generated, recycled and disposed of (including the disposal sites) will be established and implemented during the construction phase as part of the Environmental Management Plan (EMP). The Contractor will be required to prepare the EMP and submits it to the Architect/ Engineer under the Contract for approval prior to implementation.	All area/ During construction	Contractor(s)		✓		Implemented	ETWB TC(W) No. 19/2005, Environmental Management on Construction Sites
S8.5	Separation of chemical wastes for special handling and appropriate treatment at the Chemical Waste Treatment Centre at Tsing Yi.	All area/ During construction	Contractor(s)		✓		Implemented	Chapters 2 & 3 Code of Practice on the Packaging, Labelling Storage of Chemical Wastes published under

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
								the Waste Disposal Ordinance (Cap 354), Section 35
S8.5	Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors.	Land site/ During construction	Contractor(s)		✓		Implemented, rectified after observation	Waste Disposal Ordinance (Cap 354)
S8.5	A recording system for the amount of wastes generated/ recycled and disposal sites. The trip- ticket system will be included as one of the contractual requirements and implemented by the contractor(s).	Land site/ During construction	Contractor(s)		✓		Implemented	DEVB TC(W) No. 6/2010, Trip Ticket System for Disposal of Construction & Demolition Materials
S8.5	Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of material and their proper disposal.	Land site/ During construction/ During operation	Contractor(s)		✓		Implemented	WBTC 32/92, The Use of Tropical Hard Wood on Construction Site
S8.5	Encourage collection of aluminium cans and waste paper by individual collectors during construction with separate labelled bins provided to segregate these wastes from other general refuse by the workforce.	Land site/ During construction	Contractor(s)		✓		Implemented	ETWB TCW No. 33/2002, Management of Construction and Demolition Material Including Rock
S8.5	Any unused chemicals and those with remaining functional capacity will be recycled as far as possible.	Land site/ During construction	Contractor(s)		✓		N/A	-
S8.5	Use of reusable non-timber formwork to reduce the amount of C&D materials.	All areas/ During construction	Contractor(s)		✓		N/A	WBTC 32/92, The Use of Tropical Hard Wood on Construction Site
S8.5	Prior to disposal of construction waste, wood, steel and other metals will be separated to the extent practical, for re-use and/or recycling to reduce the quantity of waste to be disposed of to landfill.	All areas/ During construction	Contractor(s)		✓		Implemented	DEVB TC(W) No. 6/2010, Trip Ticket System for Disposal of Construction & Demolition Materials
S8.5	Proper storage and site practices to reduce the potential for damage or contamination of construction materials.	All areas/ During construction	Contractor(s)		✓		Implemented, rectified after observation	-

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
S8.5	Plan and stock construction materials carefully to reduce amount of waste generated and avoid unnecessary generation of waste.	All areas/ During construction	Contractor(s)		✓		Implemented	-
S8.5	A Sediment Quality Report (SQR) for sampling and chemical testing of the sediment will be prepared and submitted to the EPD for approval. The approved detailed sampling and chemical testing will be carried out prior to the commencement of the dredging activities to confirm the sediment disposal method.	Marine works/ During construction	Contractor(s)		✓		N/A	ETWB TC(W) No. 34/2002 and Dumping at Sea Ordinance (DASO)
S8.5	The management of dredged/ excavated sediment management requirement from <i>ETWB TC(W) No. 34/2002</i> will be incorporated in the Specification of the Contract Documents.	Marine works/ During construction	WSD/ Contractor(s)		✓		Implemented	ETWB TC(W) No. 34/2002 and Dumping at Sea Ordinance (DASO)
S8.5	The contractor will open a billing account with EPD in accordance with the Waste Disposal (Charges for Disposal of Construction Waste) Regulation for the payment of disposal charges.	Contract mobilisation/ During construction	Contractor(s)		✓		Implemented	Cap 354N Waste Disposal (Charges for Disposal of Construction Waste) Regulation
S8.5	A trip-ticket system will be established in accordance with DEVB TC(W) No. 6/2010 to monitor the reuse of surplus excavated materials off-site and disposal of construction waste and general refuse at transfer facilities/ landfills, and to control fly-tipping.	Contract mobilisation/ During construction	Contractor(s)		✓		Implemented	DEVB TC(W) No. 6/2010, Trip Ticket System for Disposal of Construction & Demolition Materials
S8.5	The project proponent will also conduct regular inspection of the waste management measures implemented on site as described in the Waste Management Plan.	All area/ During construction	Contractor(s)/ Environmental Team (ET) & Independent Environmental Checker (IEC)		✓		Implemented	ETWB TC(W) No. 19/2005, Environmental Management on Construction Sites

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
S8.5	A recording system (similar to summary table as shown in Annex 5 and Annex 6 of Appendix G of ETWB TC(W) No. 19/2005) for the amount of waste generated, recycled and disposed of (including the disposal sites) will be established during the construction phase.	All area/ During construction	Contractor(s)		✓		Implemented	Annex 5 and Annex 6 of Appendix G of ETWB TC(W) No. 19/2005
S8.5	Inert C&D materials (public fill) will be reused within the Project as far as practicable.	All area/ During construction	Contractor(s)		✓		N/A	-
S8.5	Public fill and construction waste shall be segregated and stored in different containers or skips to facilitate reuse or recycling of materials and their proper disposal.	All area/ During construction	Contractor(s)		✓		Implemented	-
S8.5	Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable.	All area/ During construction	Contractor(s)		✓		Implemented	-
S8.5	To reduce the potential dust and water quality impacts of site formation works, C&D materials will be wetted as quickly as possible to the extent practice after filling.	All area/ During construction	Contractor(s)		✓		Implemented	Air Pollution Control (Construction Dust) Regulation (Cap 311R); WPCO (Cap 358)
S8.5	Open stockpiles of excavated/ fill materials or construction wastes on-site should be covered with tarpaulin or similar fabric.	Land site/ During Construction, particularly dry season	Contractor(s)		✓		Implemented, rectified after observation	Air Pollution Control (Construction Dust) Regulation (Cap 311R)
S8.5	Chemical waste container shall be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Chemical waste container shall have a capacity of less	All area/ During construction/	Contractor(s)/		✓	✓	Implemented	Waste Disposal

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	than 450 L unless the specifications have been approved by the EPD.	During operation	WSD					(Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	A label in English and Chinese shall be displayed on the chemical container in accordance with instructions prescribed in Schedule 2 of the Regulations.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall be enclosed on at least 3 sides.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall have adequate ventilation.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste)

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
								(General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary).	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Storage areas for chemical waste shall be arranged so that incompatible materials are appropriately separated.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	General refuse will be stored in enclosed bins or compaction units separately from construction and chemical wastes.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Handling and Storage of Chemical Wastes
S8.5	Adequate number of waste containers will be provided to avoid over-spillage of waste.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	DEVB TC(W) No. 8/2010 Enhanced

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
								Specification for Site Cleanliness and Tidiness.
S8.5	A reputable waste collector will be employed by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily basis to minimise odour, pest and litter impacts.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	-
S8.5	Recycling bins will be provided at strategic locations within the Site to facilitate recovery of recyclable materials (including aluminium can, waste paper, glass bottles and plastic bottles) from the Site. Materials recovered will be sold for recycling.	All area/ During construction/ During operation	Contractor(s)/ WSD		✓	✓	Implemented	-
S8.5	To avoid any odour and litter impact, accurate number of portable toilets will be provided for workers on-site.	All area/ During construction	Contractor(s)		✓		Implemented	-
S8.5	The burning of refuse on construction sites is prohibited by law.	All area/ During construction	Contractor(s)		✓		Implemented	Air Pollution Control Ordinance (Cap 311)
S8.7	To facilitate monitoring and control over the contractors' performance on waste management, a waste inspection and audit programme will be implemented throughout the construction phase.	All facilities/ During construction	ET/ IEC		✓		Implemented	-

Note: D – Design stage C – Construction O – Operation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
Ecology								
S9.7	For slope mitigation works within the Clear Water Bay Country Park, to avoid tree felling and damages to trees, the exact locations of the flexible barrier foundation plates, soil nails and rock dowels can be adjusted during detailed design, and a setback distance from existing trees is recommended to be maintained as far as practical. A detailed specification describing the exact locations of the flexible barrier foundation plates, soil nails and rock dowels will be prepared to illustrate how the setback distance from existing trees would be implemented for tree avoidance.	Slope mitigation works area/ During detailed design/ During construction	Contractor(s)	✓	✓		Implemented	-
S9.7	Pruning of tree canopies along the alignment of the flexible barriers shall be limited to a minimum.	Slope mitigation works area/ During construction	Contractor(s)		✓		Implemented	
S9.7	The alignment of flexible barriers shall be optimized to preserve all species of conservation interest and minimize the impact to the existing vegetation as far as practicable. All individuals of <i>Marsdenia lachnostoma</i> within the slope mitigation areas shall be retained <i>in-situ</i> , by positioning the alignment of flexible barrier at a minimum 1.5m in a radius away from these individuals.	Slope mitigation works area/ During detailed design/ During construction	Contractor(s)	✓	✓		N/A	-
S9.7 and 9.10	At the detailed design stage prior to the commencement of the slope mitigation works, a vegetation survey shall be carried out at the slope mitigation areas within the Clear Water Bay Country Park to assess the condition and identify the location of each individual of <i>Marsdenia lachnostoma</i> and other flora species of conservation interest that may be directly affected by the construction works.	Slope mitigation works area/ During detailed design/ During construction	Contractor(s)	✓	✓		N/A	-
S9.7	Temporary fencing will be installed to fence off the concerned species either in groups of individually within the works area and in the close proximity to prevent from being damaged and disturbed during construction. A sign identifying the site shall be attached to the fence and flagging tape shall be attached to the individuals to visualize their locations.	Slope mitigation works area/ During construction	Contractor(s)		✓		N/A	-

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
S9.7 and S9.10	A specification for fencing and demarcating individuals of <i>Marsdenia lachnostoma</i> (or other flora species of conservation interest, if found) adjacent to the proposed alignment of the flexible barriers will be prepared to protect the species.	Slope mitigation works area/ During construction	Contractor(s)		✓		N/A	-
S9.7	Induction training shall also be provided to all site personnel in order to brief them on this flora of conservation interest including the locations and their importance.	Slope mitigation works area/ During construction	Contractor(s)		✓		N/A	-
S9.7	The resident site supervisory staff will closely monitor the conditions of concerned individuals during construction of flexible barriers in the close proximity.	Slope mitigation works area/ During construction	Contractor(s)		✓		Implemented	-
S9.7	Erect fences along the boundary of the works area before the commencement of works to prevent vehicle movements and encroachment of personnel onto adjacent areas.	All area/ During construction	Contractor(s)		✓		Implemented	-
S9.7	Regularly check the work site boundaries to ensure that they are not breached and that damage does not occur to surrounding areas.	All area/ During construction	Contractor(s)/ Environmental Team (ET)		✓		Implemented	-
S9.7	Avoid any damage and disturbance, particularly those caused by filling and illegal dumping, to the surrounding habitats through proper management of waste disposal.	All area/ During construction	Contractor(s)		✓		Implemented	-
S9.7	Reinstate temporarily affected areas, particularly the habitats of plantation and shrubland-grassland immediately after completion of construction works, through on-site tree/shrub planting. The tree/shrub species will be chosen with reference to those in the surrounding area.	All area/ During construction	Contractor(s)		✓		N/A	-
S9.7	Affected habitats within the Clear Water Bay Country Bay shall be reinstated by hydro-seeding and planting of climbers and native shrub seedlings where practical upon completion of the slope mitigation works.	All area/ During construction	Contractor(s)		✓		N/A	-

Note: D – Design stage C – Construction O – Operation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
Landscape & Visual								
S11.10 & 11.11	The construction area and area allowed for temporary structures, such as the contractor's office, will be minimized to a practical minimum. (MM1)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	-
S11.10 & 11.11	At the detailed design stage, the design team will seek to minimize the landscape footprint of the Project and above ground facilities, while satisfying all other requirements. (MM2)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	-
S11.10 & 11.11	Design principles will be adopted to take into account the surrounding area, particularly Clear Water Bay Country Park behind and the nearby waterfront, with due consideration given to: - green roofs where practical (ie without equipment on the roof); - roadside planting; - aesthetic treatment of all structures; - vertical greening; screen planting along application site; and - landscape enhancement with amenity planting where practical including planting along the edge (site boundary) fence with native shrubs where feasible, - to reduce their visual impact and blend them into the surrounding landscape. (MM3)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	-
S11.10 & 11.11	All trees within the Project Site or the potential slope mitigation works area will be carefully protected during construction according to DEVB TCW No. 10/2013 – Tree Preservation (MM4)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	ETWB TCW No. 3/2006 - Tree Preservation.
S11.10 & 11.11	No tree within the Country Park will be felled. Trees within the Site unavoidably affected by the works will be transplanted where necessary and practical. For trees that need to be felled, compensatory planting will be provided to the satisfaction of relevant Government departments. A compensatory tree planting proposal including locations of tree compensation will be submitted to seek relevant government department's approval, in accordance with DEVB TC(W) No. 10/2013.	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	DEVB TC(W) No. 10/2013

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	(MM5)							
S11.10 & 11.11	Any slope mitigation works necessary to address natural terrain hazards, will be minimized to minimize any potential environmental impact to the Country Park e.g. soil nailing and rock stabilization will aim to avoid existing trees e.g. should any restoration of vegetation be necessary, the best planting matrix with native species will be established, with the aim of resembling the existing vegetation. (MM6)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	N/A	
S11.10 & 11.11	Dredging works for the installation of intake structures and outfall diffusers should be minimized to avoid or reduce any potential environmental impacts to as low as reasonably practicable (ALARP). The intake and outfall structures (e.g. intake openings and diffuser heads) will be prefabricated and transferred to site for installation. (MM7)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	N/A	
S11.10 & 11.11	All night-time lighting will be reduced to a practical minimum both in terms of number of level and will be hooded and directional. (MM8) units and lux level and will be hooded and directional. (MM8)	All area/ Detailed design/ During construction/ During operation	WSD/ Contractor(s)	✓	✓	✓	Implemented	-

Note: D – Design stage C – Construction O – Operation

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
Landfill Gas Hazard								
S12.7	During all works, safety procedures should be implemented to minimise the risks of fires and explosions, asphyxiation of workers and toxicity effects resulting from contact with contaminated soil and groundwater.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	-
S12.7	During trenching and excavation as well as creation of confined spaces at near to or below ground level, precautions should be clearly laid down and rigidly Gas detection equipment and appropriate breathing apparatus should be available and used when entering confined spaces or trenches deeper than 1 metre.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	The Contractor should make the workers are aware of potential hazards of working in confined spaces (any chamber, manhole or culvert which is large enough to permit access to personnel). Such work in confined spaces is controlled by the Factories and Industrial Undertakings (Confined Spaces) Regulations of the Factories and Industrial Undertakings Ordinance. Following the Safety Guide to Working in Confined Spaces ensures compliance with the above regulations.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	Safety officers, specifically trained with regard to landfill gas and leachate related hazards and the appropriate actions to take in adverse circumstances, should be present on the site throughout the works, in particular, when works are undertaken below grade.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	All personnel who work on site and all visitors to the site should be made aware of the possibility of ignition of gas in the vicinity of the works, the possible presence of contaminated water and the need to avoid physical contact with it.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	Monitoring for landfill gas should be undertaken in all excavations, manholes, chambers (particularly during pipe jacking) and any confined spaces through the use of an intrinsically safe portable instrument, appropriately calibrated and capable of measuring the concentrations of methane, carbon dioxide and oxygen.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
S12.7	Monitoring frequency and areas to be monitored should be specified prior to commencement of groundwork, either by the Safety Officer, or by an appropriately qualified person. All measurements should be recorded and documented.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	Proceed drilling with adequate care and precautions against the potential hazards which may be encountered.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	Prior to the commencement of the site works, the drilling contractor should devise a 'method-of- working' statement covering all normal and emergency procedures (including but not limited to number of operatives, experience and special skills of operatives, normal method of operations, emergency procedures, supervisors responsibilities, storage and use of safety equipment, safety procedures and signs, barriers and guarding). The site supervisor and all operatives must be familiar with this statement.	All area/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	
S12.7	Where below ground service entries are necessary to the Incoming Switchgear Room, 132 kV Substation and Chlorine Store (I) and (II), the entry point should be sealed to prevent gas entry. In addition, any below grade cable trenches entering the Incoming Switchgear Room and 132 kV Substation can become the pathway for landfill gas and hence gridded metal covers should be used.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	N/A	
S12.7	It is recommended regular landfill gas monitoring should be carried out at the Incoming Switchgear Room, 132 kV Substation and Chlorine Store (I) and (II). The monitoring frequency will be monthly for the first year of operation. If the monitoring results show no sign of landfill gas migration, reduce the monitoring frequency to once every six months.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	N/A	
S12.7	The manholes and utility pits within the Project Site and along the fresh water mains. Each manhole/ utility pit should be monitored with two measurements (at mid depth and base). Each measurement should be	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



EIA Reference	Recommended Environmental Protection Measures/ Mitigation Measures	Objectives of the recommended measures & main concerns to address	Implementation Agent	Implementation Stage			Implementation Status	Relevant Legislation & Guidelines
				D	C	O		
	monitored for a minimum of 10 minutes. A steady reading and peak reading should be recorded at each manhole/ utility pit and for each measurement. The need for venting the manhole/ utility pit and further monitoring will be reviewed after the initial monitoring.							
S12.7	All construction, operation and maintenance personnel working on-site as well as visitors should be made aware of the hazards of landfill gas and its possible presence on-site. This should be achieved through a combination of posting warning signs in prominent places and also by access to detailed information on landfill gas hazards and the designs and procedural means by which these hazards are being minimised on-site.	All area/ Detailed design/ During construction/ During operation	Contractor(s)	✓	✓	✓	Implemented	

Note: D – Design stage C – Construction O – Operation

Appendix G

Action and Limit Level for Noise and Landfill Gas

Action/ Limit Level for Noise Monitoring

Time Period	Action	Limit (dB(A))
0700-1900 hours on normal weekdays	When one documented complaint is received from any one of the noise sensitive receivers	<ul style="list-style-type: none">• 70 dB(A) for school and• 65 dB(A) during examination period
Notes: (a) Limits specified in the GW-TM and IND-TM for construction and operation noise, respectively.		

Action Level for Landfill Gas Monitoring Equipment

Parameters	Level
Oxygen (O ₂)	Action Level < 19% O ₂ Limit Level < 19% O ₂
Methane (CH ₄)	Action Level >10% LEL Limit Level >20% LEL
Carbon Dioxide (CO ₂)	Action Level >0.5% CO ₂ Limit Level >1.5% CO ₂

Appendix H

Landfill Gas Monitoring Results

Date of Measurement	Sampling Location	Depth (m)	Sampling time	Weather Condition	Balance Gas(%)	Flammable gas (methane%)	Carbon Dioxide (%)	Oxygen (%)	Temp (C)	Pressure (m bar)	Measurement Equipment
1/8/2020	Area A	2.5	8:30	Rain	0	0	0	20.9	27	1004	PGM-2400P (QRAE III)
1/8/2020	Area A	2.5	13:30	Rain	0	0	0	20.9	27	1003	PGM-2400P (QRAE III)
1/8/2020	Area A	2.5	17:00	Rain	0	0	0	20.9	27	1004	PGM-2400P (QRAE III)
1/8/2020	Area B	2.5	8:45	Rain	0	0	0	20.9	27	1004	PGM-2400P (QRAE III)
1/8/2020	Area B	2.5	13:45	Rain	0	0	0	20.9	27	1003	PGM-2400P (QRAE III)
1/8/2020	Area B	2.5	16:45	Rain	0	0	0	20.9	27	1004	PGM-2400P (QRAE III)
1/8/2020	CHFC 4+50	2.5	8:55	Rain	0	0	0	20.9	27	1004	PGM-2400P (QRAE III)
1/8/2020	CHFC 4+50	2.5	13:55	Rain	0	0	0	20.9	28	1003	PGM-2400P (QRAE III)
1/8/2020	CHFC O+90	2.5	9:00	Rain	0	0	0	20.9	27	1005	PGM-2400P (QRAE III)
1/8/2020	CHFC O+90	2.5	14:00	Rain	0	0	0	20.9	27	1003	PGM-2400P (QRAE III)
1/8/2020	Pit C	8	9:15	Rain	0	0	0	20.9	27	1005	PGM-2400P (QRAE III)
1/8/2020	Pit C	8	14:15	Rain	0	0	0	20.9	27	1003	PGM-2400P (QRAE III)
1/8/2020	137 CH.C.T.2+66	3.1	9:35	Rain	0	0	0	20.9	28	1005	PGM-2400P (QRAE III)
1/8/2020	137 CH.C.T.2+66	3.1	14:35	Rain	0	0	0	20.9	27	1003	PGM-2400P (QRAE III)
1/8/2020	137 Pit C	3.5	9:45	Rain	0	0	0	20.9	28	1005	PGM-2400P (QRAE III)
1/8/2020	137 Pit C	3.5	14:45	Rain	0	0	0	20.9	27	1003	PGM-2400P (QRAE III)
1/8/2020	137 Pit B	3.1	9:55	Rain	0	0	0	20.9	28	1005	PGM-2400P (QRAE III)
1/8/2020	137 Pit B	3.1	14:55	Rain	0	0	0	20.9	27	1003	PGM-2400P (QRAE III)
1/8/2020	CHA 6+70	3.5	10:05	Rain	0	0	0	20.9	28	1005	PGM-2400P (QRAE III)
1/8/2020	CHA 6+70	3.5	15:05	Rain	0	0	0	20.9	27	1003	PGM-2400P (QRAE III)
1/8/2020	Pit B	8	10:15	Rain	0	0	0	20.9	28	1004	PGM-2400P (QRAE III)
1/8/2020	Pit B	8	15:15	Rain	0	0	0	20.9	27	1003	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



3/8/2020	Area A	2.5	8:30	Rain	0	0	0	20.9	26	1004	PGM-2400P (QRAE III)
3/8/2020	Area A	2.5	13:30	Rain	0	0	0	20.9	25	1003	PGM-2400P (QRAE III)
3/8/2020	Area A	2.5	17:00	Rain	0	0	0	20.9	26	1002	PGM-2400P (QRAE III)
3/8/2020	Area B	2.5	8:45	Rain	0	0	0	20.9	26	1004	PGM-2400P (QRAE III)
3/8/2020	Area B	2.5	13:45	Rain	0	0	0	20.9	25	1003	PGM-2400P (QRAE III)
3/8/2020	Area B	2.5	16:45	Rain	0	0	0	20.9	26	1002	PGM-2400P (QRAE III)
3/8/2020	CHFC 4+50	2.5	8:55	Rain	0	0	0	20.9	26	1004	PGM-2400P (QRAE III)
3/8/2020	CHFC 4+50	2.5	13:55	Rain	0	0	0	20.9	25	1003	PGM-2400P (QRAE III)
3/8/2020	CHFC O+90	2.5	9:00	Rain	0	0	0	20.9	26	1004	PGM-2400P (QRAE III)
3/8/2020	CHFC O+90	2.5	14:00	Rain	0	0	0	20.9	25	1003	PGM-2400P (QRAE III)
3/8/2020	Pit C	8	9:15	Rain	0	0	0	20.9	26	1004	PGM-2400P (QRAE III)
3/8/2020	Pit C	8	14:15	Rain	0	0	0	20.9	25	1003	PGM-2400P (QRAE III)
3/8/2020	137 CH.C.T.2+66	3.1	9:35	Rain	0	0	0	20.9	26	1004	PGM-2400P (QRAE III)
3/8/2020	137 CH.C.T.2+66	3.1	14:35	Rain	0	0	0	20.9	25	1003	PGM-2400P (QRAE III)
3/8/2020	137 Pit C	3.5	9:45	Rain	0	0	0	20.9	26	1004	PGM-2400P (QRAE III)
3/8/2020	137 Pit C	3.5	14:45	Rain	0	0	0	20.9	25	1003	PGM-2400P (QRAE III)
3/8/2020	137 Pit B	3.1	9:55	Rain	0	0	0	20.9	26	1004	PGM-2400P (QRAE III)
3/8/2020	137 Pit B	3.1	14:55	Rain	0	0	0	20.9	25	1002	PGM-2400P (QRAE III)
3/8/2020	CHA 6+70	3.5	10:05	Rain	0	0	0	20.9	26	1004	PGM-2400P (QRAE III)
3/8/2020	CHA 6+70	3.5	15:05	Rain	0	0	0	20.9	26	1002	PGM-2400P (QRAE III)
3/8/2020	Pit B	8	10:15	Rain	0	0	0	20.9	26	1004	PGM-2400P (QRAE III)
3/8/2020	Pit B	8	15:15	Rain	0	0	0	20.9	26	1002	PGM-2400P (QRAE III)
4/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	29	1003	PGM-2400P (QRAE III)
4/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	28	1004	PGM-2400P (QRAE III)
4/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	28	1003	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



4/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	29	1003	PGM-2400P (QRAE III)
4/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	28	1004	PGM-2400P (QRAE III)
4/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	28	1003	PGM-2400P (QRAE III)
4/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	29	1003	PGM-2400P (QRAE III)
4/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	28	1004	PGM-2400P (QRAE III)
4/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	29	1004	PGM-2400P (QRAE III)
4/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	28	1004	PGM-2400P (QRAE III)
4/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	29	1004	PGM-2400P (QRAE III)
4/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	28	1003	PGM-2400P (QRAE III)
4/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	29	1004	PGM-2400P (QRAE III)
4/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	28	1003	PGM-2400P (QRAE III)
4/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	29	1004	PGM-2400P (QRAE III)
4/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	28	1003	PGM-2400P (QRAE III)
4/8/2020	137 Pit B	3.1	9:55	Fine	0	0	0	20.9	29	1004	PGM-2400P (QRAE III)
4/8/2020	137 Pit B	3.1	14:55	Fine	0	0	0	20.9	28	1003	PGM-2400P (QRAE III)
4/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	29	1004	PGM-2400P (QRAE III)
4/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	28	1003	PGM-2400P (QRAE III)
4/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	28	1004	PGM-2400P (QRAE III)
4/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	28	1003	PGM-2400P (QRAE III)
5/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
5/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
5/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
5/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
5/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
5/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)

5/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
5/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
5/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
5/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
5/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
5/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
5/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
5/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
5/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
5/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
5/8/2020	137 Pit B	3.1	9:55	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
5/8/2020	137 Pit B	3.1	14:55	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
5/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
5/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
5/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
5/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
6/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
6/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	31	1009	PGM-2400P (QRAE III)
6/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
6/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
6/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	31	1009	PGM-2400P (QRAE III)
6/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
6/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
6/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	31	1009	PGM-2400P (QRAE III)
6/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



6/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	31	1009	PGM-2400P (QRAE III)
6/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
6/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	31	1009	PGM-2400P (QRAE III)
6/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
6/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	31	1009	PGM-2400P (QRAE III)
6/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
6/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	31	1009	PGM-2400P (QRAE III)
6/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
6/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	31	1009	PGM-2400P (QRAE III)
6/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
6/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	31	1009	PGM-2400P (QRAE III)
6/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
6/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	31	1009	PGM-2400P (QRAE III)
7/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
7/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	32	1008	PGM-2400P (QRAE III)
7/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
7/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
7/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	32	1008	PGM-2400P (QRAE III)
7/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
7/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
7/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	32	1007	PGM-2400P (QRAE III)
7/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
7/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	32	1007	PGM-2400P (QRAE III)
7/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
7/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	32	1007	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



7/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
7/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	32	1007	PGM-2400P (QRAE III)
7/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
7/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	32	1007	PGM-2400P (QRAE III)
7/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
7/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	32	1007	PGM-2400P (QRAE III)
7/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
7/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	32	1007	PGM-2400P (QRAE III)
7/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
7/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	32	1007	PGM-2400P (QRAE III)
8/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
8/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	32	1005	PGM-2400P (QRAE III)
8/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	31	1003	PGM-2400P (QRAE III)
8/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
8/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	32	1005	PGM-2400P (QRAE III)
8/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	31	1003	PGM-2400P (QRAE III)
8/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)
8/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	32	1005	PGM-2400P (QRAE III)
8/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)
8/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	32	1005	PGM-2400P (QRAE III)
8/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
8/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	32	1005	PGM-2400P (QRAE III)
8/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
8/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
8/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



8/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
8/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
8/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
8/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
8/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
8/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
8/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
10/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	29	1005	PGM-2400P (QRAE III)
10/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
10/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	31	1004	PGM-2400P (QRAE III)
10/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	29	1005	PGM-2400P (QRAE III)
10/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
10/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	31	1004	PGM-2400P (QRAE III)
10/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	29	1005	PGM-2400P (QRAE III)
10/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	32	1003	PGM-2400P (QRAE III)
10/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	29	1005	PGM-2400P (QRAE III)
10/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	32	1003	PGM-2400P (QRAE III)
10/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
10/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	32	1003	PGM-2400P (QRAE III)
10/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
10/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	32	1003	PGM-2400P (QRAE III)
10/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
10/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	32	1003	PGM-2400P (QRAE III)
10/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
10/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	32	1003	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



10/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
10/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	32	1003	PGM-2400P (QRAE III)
10/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
10/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	32	1003	PGM-2400P (QRAE III)
11/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)
11/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
11/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
11/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)
11/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
11/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
11/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)
11/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
11/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)
11/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
11/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)
11/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
11/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)
11/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
11/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)
11/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
11/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)
11/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
11/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)
11/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
11/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



11/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
12/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
12/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
12/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
12/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
12/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
12/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
12/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
12/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
12/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
12/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
12/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
12/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	26	1010	PGM-2400P (QRAE III)
12/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
12/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
12/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
12/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
12/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
12/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
12/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
12/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
12/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
12/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
13/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
13/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



13/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
13/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
13/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
13/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
13/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
13/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
13/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
13/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
13/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
13/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
13/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	29	1012	PGM-2400P (QRAE III)
13/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
13/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	29	1012	PGM-2400P (QRAE III)
13/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
13/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	29	1012	PGM-2400P (QRAE III)
13/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
13/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	30	1012	PGM-2400P (QRAE III)
13/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
13/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	30	1012	PGM-2400P (QRAE III)
13/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
14/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
14/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	32	1009	PGM-2400P (QRAE III)
14/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
14/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
14/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	32	1009	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



14/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
14/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
14/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	32	1009	PGM-2400P (QRAE III)
14/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
14/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	31	1009	PGM-2400P (QRAE III)
14/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
14/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	31	1009	PGM-2400P (QRAE III)
14/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
14/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	31	1009	PGM-2400P (QRAE III)
14/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
14/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
14/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
14/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
14/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
14/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
14/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
14/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
15/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
15/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
15/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
15/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
15/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
15/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
15/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
15/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)

15/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
15/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
15/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
15/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
15/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
15/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
15/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
15/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
15/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
15/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
15/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
15/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
15/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
15/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
17/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
17/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
17/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	27	1008	PGM-2400P (QRAE III)
17/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
17/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
17/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	27	1008	PGM-2400P (QRAE III)
17/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
17/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
17/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
17/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
17/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)

17/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	27	1008	PGM-2400P (QRAE III)
17/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
17/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
17/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
17/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
17/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
17/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
17/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
17/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
17/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
17/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
18/8/2020	Area A	2.5	8:30	Rain	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
18/8/2020	Area A	2.5	13:30	Rain	0	0	0	20.9	28	1006	PGM-2400P (QRAE III)
18/8/2020	Area A	2.5	17:00	Rain	0	0	0	20.9	25	1005	PGM-2400P (QRAE III)
18/8/2020	Area B	2.5	8:45	Rain	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
18/8/2020	Area B	2.5	13:45	Rain	0	0	0	20.9	28	1006	PGM-2400P (QRAE III)
18/8/2020	Area B	2.5	16:45	Rain	0	0	0	20.9	25	1005	PGM-2400P (QRAE III)
18/8/2020	CHFC 4+50	2.5	8:55	Rain	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
18/8/2020	CHFC 4+50	2.5	13:55	Rain	0	0	0	20.9	27	1006	PGM-2400P (QRAE III)
18/8/2020	CHFC O+90	2.5	9:00	Rain	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
18/8/2020	CHFC O+90	2.5	14:00	Rain	0	0	0	20.9	27	1006	PGM-2400P (QRAE III)
18/8/2020	Pit C	8	9:15	Rain	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
18/8/2020	Pit C	8	14:15	Rain	0	0	0	20.9	27	1006	PGM-2400P (QRAE III)
18/8/2020	137 CH.C.T.2+66	3.1	9:35	Rain	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
18/8/2020	137 CH.C.T.2+66	3.1	14:35	Rain	0	0	0	20.9	26	1006	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



18/8/2020	137 Pit C	3.5	9:45	Rain	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
18/8/2020	137 Pit C	3.5	14:45	Rain	0	0	0	20.9	26	1006	PGM-2400P (QRAE III)
18/8/2020	137 Pit B	1	9:55	Rain	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
18/8/2020	137 Pit B	1	14:55	Rain	0	0	0	20.9	27	1005	PGM-2400P (QRAE III)
18/8/2020	CHA 6+70	3.5	10:05	Rain	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
18/8/2020	CHA 6+70	3.5	15:05	Rain	0	0	0	20.9	27	1005	PGM-2400P (QRAE III)
18/8/2020	Pit B	8	10:15	Rain	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
18/8/2020	Pit B	8	15:15	Rain	0	0	0	20.9	27	1005	PGM-2400P (QRAE III)
19/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	25	1005	PGM-2400P (QRAE III)
19/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
19/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	27	1006	PGM-2400P (QRAE III)
19/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	25	1005	PGM-2400P (QRAE III)
19/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
19/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	27	1006	PGM-2400P (QRAE III)
19/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	23	1006	PGM-2400P (QRAE III)
19/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
19/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	25	1006	PGM-2400P (QRAE III)
19/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
19/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	25	1006	PGM-2400P (QRAE III)
19/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
19/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	25	1007	PGM-2400P (QRAE III)
19/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
19/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	25	1007	PGM-2400P (QRAE III)
19/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
19/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	25	1007	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



19/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
19/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	25	1007	PGM-2400P (QRAE III)
19/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
19/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	25	1007	PGM-2400P (QRAE III)
19/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
20/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
20/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
20/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
20/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
20/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
20/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
20/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
20/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
20/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
20/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
20/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
20/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
20/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
20/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
20/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
20/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
20/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
20/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
20/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
20/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)

20/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
20/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
20/8/2020	WPR IP1	2	10:30	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
20/8/2020	WPR IP1	2	15:30	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
21/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
21/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	31	1009	PGM-2400P (QRAE III)
21/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
21/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
21/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	31	1009	PGM-2400P (QRAE III)
21/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
21/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
21/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	31	1009	PGM-2400P (QRAE III)
21/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
21/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
21/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
21/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
21/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
21/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
21/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
21/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
21/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
21/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
21/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
21/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
21/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)

21/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
21/8/2020	WPR IP1	2	10:30	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
21/8/2020	WPR IP1	2	15:30	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
22/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
22/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
22/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
22/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
22/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
22/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
22/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
22/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
22/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
22/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
22/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
22/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
22/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
22/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
22/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
22/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
22/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
22/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
22/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
22/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
22/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
22/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)

22/8/2020	WPR IP1	2	10:30	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
22/8/2020	WPR IP1	2	15:30	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
24/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	29	1006	PGM-2400P (QRAE III)
24/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
24/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	32	1003	PGM-2400P (QRAE III)
24/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	29	1006	PGM-2400P (QRAE III)
24/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
24/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	32	1003	PGM-2400P (QRAE III)
24/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)
24/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
24/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)
24/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	32	1003	PGM-2400P (QRAE III)
24/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)
24/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	32	1003	PGM-2400P (QRAE III)
24/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)
24/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	32	1003	PGM-2400P (QRAE III)
24/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)
24/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	32	1003	PGM-2400P (QRAE III)
24/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)
24/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	32	1003	PGM-2400P (QRAE III)
24/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)
24/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	32	1003	PGM-2400P (QRAE III)
24/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
24/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	32	1003	PGM-2400P (QRAE III)
24/8/2020	WPR IP1	2	10:30	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)

24/8/2020	WPR IP1	2	15:30	Fine	0	0	0	20.9	32	1003	PGM-2400P (QRAE III)
25/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	30	1004	PGM-2400P (QRAE III)
25/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	33	1003	PGM-2400P (QRAE III)
25/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	32	1002	PGM-2400P (QRAE III)
25/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	30	1004	PGM-2400P (QRAE III)
25/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	33	1003	PGM-2400P (QRAE III)
25/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	32	1002	PGM-2400P (QRAE III)
25/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	30	1004	PGM-2400P (QRAE III)
25/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	33	1003	PGM-2400P (QRAE III)
25/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	30	1004	PGM-2400P (QRAE III)
25/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	33	1003	PGM-2400P (QRAE III)
25/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	30	1004	PGM-2400P (QRAE III)
25/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	33	1002	PGM-2400P (QRAE III)
25/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	30	1004	PGM-2400P (QRAE III)
25/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	33	1002	PGM-2400P (QRAE III)
25/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	31	1004	PGM-2400P (QRAE III)
25/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	33	1002	PGM-2400P (QRAE III)
25/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	31	1004	PGM-2400P (QRAE III)
25/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	33	1002	PGM-2400P (QRAE III)
25/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	31	1004	PGM-2400P (QRAE III)
25/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	33	1002	PGM-2400P (QRAE III)
25/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	31	1004	PGM-2400P (QRAE III)
25/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	32	1002	PGM-2400P (QRAE III)
25/8/2020	WPR IP1	2	10:30	Fine	0	0	0	20.9	31	1004	PGM-2400P (QRAE III)
25/8/2020	WPR IP1	2	15:30	Fine	0	0	0	20.9	32	1002	PGM-2400P (QRAE III)

26/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	30	1003	PGM-2400P (QRAE III)
26/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	31	1000	PGM-2400P (QRAE III)
26/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	30	1000	PGM-2400P (QRAE III)
26/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	30	1003	PGM-2400P (QRAE III)
26/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	31	1000	PGM-2400P (QRAE III)
26/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	30	1000	PGM-2400P (QRAE III)
26/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	30	1003	PGM-2400P (QRAE III)
26/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	31	1000	PGM-2400P (QRAE III)
26/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	30	1003	PGM-2400P (QRAE III)
26/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	31	1000	PGM-2400P (QRAE III)
26/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	30	1003	PGM-2400P (QRAE III)
26/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	31	1000	PGM-2400P (QRAE III)
26/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	30	1003	PGM-2400P (QRAE III)
26/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	30	1000	PGM-2400P (QRAE III)
26/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	30	1003	PGM-2400P (QRAE III)
26/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	30	1000	PGM-2400P (QRAE III)
26/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	30	1003	PGM-2400P (QRAE III)
26/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	31	1000	PGM-2400P (QRAE III)
26/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	31	1003	PGM-2400P (QRAE III)
26/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	31	1000	PGM-2400P (QRAE III)
26/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	31	1003	PGM-2400P (QRAE III)
26/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	31	1000	PGM-2400P (QRAE III)
26/8/2020	WPR IP1	2	10:30	Fine	0	0	0	20.9	31	1003	PGM-2400P (QRAE III)
26/8/2020	WPR IP1	2	15:30	Fine	0	0	0	20.9	31	1000	PGM-2400P (QRAE III)
27/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	28	1001	PGM-2400P (QRAE III)

27/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	31	999	PGM-2400P (QRAE III)
27/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	29	999	PGM-2400P (QRAE III)
27/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	28	1001	PGM-2400P (QRAE III)
27/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	31	999	PGM-2400P (QRAE III)
27/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	29	999	PGM-2400P (QRAE III)
27/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	28	1001	PGM-2400P (QRAE III)
27/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	31	999	PGM-2400P (QRAE III)
27/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	28	1001	PGM-2400P (QRAE III)
27/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	31	999	PGM-2400P (QRAE III)
27/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	28	1001	PGM-2400P (QRAE III)
27/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	31	999	PGM-2400P (QRAE III)
27/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	28	1001	PGM-2400P (QRAE III)
27/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	31	999	PGM-2400P (QRAE III)
27/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	28	1001	PGM-2400P (QRAE III)
27/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	30	999	PGM-2400P (QRAE III)
27/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	28	1001	PGM-2400P (QRAE III)
27/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	30	999	PGM-2400P (QRAE III)
27/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	28	1001	PGM-2400P (QRAE III)
27/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	30	999	PGM-2400P (QRAE III)
27/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	28	1001	PGM-2400P (QRAE III)
27/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	30	999	PGM-2400P (QRAE III)
27/8/2020	WPR IP1	2	10:30	Fine	0	0	0	20.9	29	1001	PGM-2400P (QRAE III)
27/8/2020	WPR IP1	2	15:30	Fine	0	0	0	20.9	30	999	PGM-2400P (QRAE III)
28/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	29	1003	PGM-2400P (QRAE III)
28/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	32	1002	PGM-2400P (QRAE III)

28/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	28	1002	PGM-2400P (QRAE III)
28/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	29	1003	PGM-2400P (QRAE III)
28/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	32	1002	PGM-2400P (QRAE III)
28/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	28	1002	PGM-2400P (QRAE III)
28/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	29	1003	PGM-2400P (QRAE III)
28/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	32	1002	PGM-2400P (QRAE III)
28/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	29	1003	PGM-2400P (QRAE III)
28/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	32	1002	PGM-2400P (QRAE III)
28/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	29	1003	PGM-2400P (QRAE III)
28/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	32	1002	PGM-2400P (QRAE III)
28/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	29	1003	PGM-2400P (QRAE III)
28/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	31	1002	PGM-2400P (QRAE III)
28/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	30	1003	PGM-2400P (QRAE III)
28/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	31	1002	PGM-2400P (QRAE III)
28/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	30	1003	PGM-2400P (QRAE III)
28/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	30	1002	PGM-2400P (QRAE III)
28/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	30	1003	PGM-2400P (QRAE III)
28/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	29	1002	PGM-2400P (QRAE III)
28/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	30	1003	PGM-2400P (QRAE III)
28/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	28	1002	PGM-2400P (QRAE III)
28/8/2020	WPR IP1	2	10:30	Fine	0	0	0	20.9	30	1003	PGM-2400P (QRAE III)
28/8/2020	WPR IP1	2	15:30	Fine	0	0	0	20.9	27	1002	PGM-2400P (QRAE III)
29/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
29/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	32	1003	PGM-2400P (QRAE III)
29/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	31	1003	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



29/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
29/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	32	1003	PGM-2400P (QRAE III)
29/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	31	1003	PGM-2400P (QRAE III)
29/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
29/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	31	1003	PGM-2400P (QRAE III)
29/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
29/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	31	1003	PGM-2400P (QRAE III)
29/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
29/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	28	1003	PGM-2400P (QRAE III)
29/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
29/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	27	1003	PGM-2400P (QRAE III)
29/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
29/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	28	1003	PGM-2400P (QRAE III)
29/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
29/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	29	1003	PGM-2400P (QRAE III)
29/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
29/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	29	1003	PGM-2400P (QRAE III)
29/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
29/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	30	1003	PGM-2400P (QRAE III)
29/8/2020	WPR IP1	2	10:30	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
29/8/2020	WPR IP1	2	15:30	Fine	0	0	0	20.9	30	1003	PGM-2400P (QRAE III)
29/8/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)
31/8/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
31/8/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	29	1004	PGM-2400P (QRAE III)
31/8/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



31/8/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
31/8/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	29	1004	PGM-2400P (QRAE III)
31/8/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
31/8/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
31/8/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
31/8/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
31/8/2020	Pit C	8	9:15	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
31/8/2020	Pit C	8	14:15	Fine	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
31/8/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
31/8/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
31/8/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
31/8/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
31/8/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
31/8/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
31/8/2020	CHA 6+70	3.5	10:05	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
31/8/2020	CHA 6+70	3.5	15:05	Fine	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
31/8/2020	Pit B	8	10:15	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
31/8/2020	Pit B	8	15:15	Fine	0	0	0	20.9	31	1004	PGM-2400P (QRAE III)
31/8/2020	WPR IP1	2	10:30	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
31/8/2020	WPR IP1	2	15:30	Fine	0	0	0	20.9	29	1004	PGM-2400P (QRAE III)
1/9/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)
1/9/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	33	1004	PGM-2400P (QRAE III)
1/9/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
1/9/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)
1/9/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	33	1004	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



1/9/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
1/9/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
1/9/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
1/9/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
1/9/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
1/9/2020	Pit C	8	9:15	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
1/9/2020	Pit C	8	14:15	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
1/9/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
1/9/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
1/9/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
1/9/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
1/9/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
1/9/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
1/9/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
1/9/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
1/9/2020	Pit B	8	10:35	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
1/9/2020	Pit B	8	15:35	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
1/9/2020	WPR IP1	2	10:50	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
1/9/2020	WPR IP1	2	15:50	Fine	0	0	0	20.9	32	1004	PGM-2400P (QRAE III)
2/9/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)
2/9/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	32	1006	PGM-2400P (QRAE III)
2/9/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	29	1005	PGM-2400P (QRAE III)
2/9/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)
2/9/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	32	1006	PGM-2400P (QRAE III)
2/9/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	29	1005	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



2/9/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)
2/9/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	33	1005	PGM-2400P (QRAE III)
2/9/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)
2/9/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	33	1005	PGM-2400P (QRAE III)
2/9/2020	Pit C	8	9:15	Fine	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)
2/9/2020	Pit C	8	14:15	Fine	0	0	0	20.9	33	1005	PGM-2400P (QRAE III)
2/9/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)
2/9/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	33	1005	PGM-2400P (QRAE III)
2/9/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
2/9/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	32	1005	PGM-2400P (QRAE III)
2/9/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
2/9/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
2/9/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
2/9/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	29	1005	PGM-2400P (QRAE III)
2/9/2020	Pit B	8	10:35	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
2/9/2020	Pit B	8	15:35	Fine	0	0	0	20.9	29	1005	PGM-2400P (QRAE III)
2/9/2020	WPR IP1	2	10:50	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
2/9/2020	WPR IP1	2	15:50	Fine	0	0	0	20.9	29	1005	PGM-2400P (QRAE III)
3/9/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
3/9/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
3/9/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
3/9/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
3/9/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
3/9/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
3/9/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



3/9/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
3/9/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
3/9/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
3/9/2020	Pit C	8	9:15	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
3/9/2020	Pit C	8	14:15	Fine	0	0	0	20.9	27	1008	PGM-2400P (QRAE III)
3/9/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
3/9/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	27	1008	PGM-2400P (QRAE III)
3/9/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
3/9/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	27	1008	PGM-2400P (QRAE III)
3/9/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
3/9/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
3/9/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
3/9/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
3/9/2020	Pit B	8	10:35	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
3/9/2020	Pit B	8	15:35	Fine	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)
4/9/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
4/9/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
4/9/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)
4/9/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
4/9/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
4/9/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)
4/9/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
4/9/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	39	1008	PGM-2400P (QRAE III)
4/9/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
4/9/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



4/9/2020	Pit C	8	9:15	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
4/9/2020	Pit C	8	14:15	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
4/9/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
4/9/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
4/9/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
4/9/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
4/9/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
4/9/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	31	1008	PGM-2400P (QRAE III)
4/9/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	31	1010	PGM-2400P (QRAE III)
4/9/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
4/9/2020	Pit B	8	10:35	Fine	0	0	0	20.9	31	1010	PGM-2400P (QRAE III)
4/9/2020	Pit B	8	15:35	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
5/9/2020	Area A	2.5	8:30	Rain	0	0	0	20.9	27	1008	PGM-2400P (QRAE III)
5/9/2020	Area A	2.5	13:30	Rain	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)
5/9/2020	Area A	2.5	17:00	Rain	0	0	0	20.9	29	1006	PGM-2400P (QRAE III)
5/9/2020	Area B	2.5	8:45	Rain	0	0	0	20.9	27	1008	PGM-2400P (QRAE III)
5/9/2020	Area B	2.5	13:45	Rain	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)
5/9/2020	Area B	2.5	16:45	Rain	0	0	0	20.9	29	1006	PGM-2400P (QRAE III)
5/9/2020	CHFC 4+50	2.5	8:55	Rain	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
5/9/2020	CHFC 4+50	2.5	13:55	Rain	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)
5/9/2020	CHFC O+90	2.5	9:00	Rain	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
5/9/2020	CHFC O+90	2.5	14:00	Rain	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)
5/9/2020	Pit C	8	9:15	Rain	0	0	0	20.9	26	1010	PGM-2400P (QRAE III)
5/9/2020	Pit C	8	14:15	Rain	0	0	0	20.9	24	1006	PGM-2400P (QRAE III)
5/9/2020	137 CH.C.T.2+66	3.1	9:35	Rain	0	0	0	20.9	24	1010	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



5/9/2020	137 CH.C.T.2+66	3.1	14:35	Rain	0	0	0	20.9	29	1006	PGM-2400P (QRAE III)
5/9/2020	137 Pit C	3.5	9:45	Rain	0	0	0	20.9	24	1010	PGM-2400P (QRAE III)
5/9/2020	137 Pit C	3.5	14:45	Rain	0	0	0	20.9	29	1006	PGM-2400P (QRAE III)
5/9/2020	137 Pit B	1	9:55	Rain	0	0	0	20.9	24	1010	PGM-2400P (QRAE III)
5/9/2020	137 Pit B	1	14:55	Rain	0	0	0	20.9	29	1006	PGM-2400P (QRAE III)
5/9/2020	CHA 6+70	3.5	10:15	Rain	0	0	0	20.9	24	1010	PGM-2400P (QRAE III)
5/9/2020	CHA 6+70	3.5	15:15	Rain	0	0	0	20.9	29	1006	PGM-2400P (QRAE III)
5/9/2020	Pit B	8	10:35	Rain	0	0	0	20.9	24	1010	PGM-2400P (QRAE III)
5/9/2020	Pit B	8	15:35	Rain	0	0	0	20.9	29	1006	PGM-2400P (QRAE III)
7/9/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
7/9/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
7/9/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	29	1006	PGM-2400P (QRAE III)
7/9/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
7/9/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
7/9/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	29	1006	PGM-2400P (QRAE III)
7/9/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
7/9/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
7/9/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
7/9/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
7/9/2020	Pit C	8	9:15	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
7/9/2020	Pit C	8	14:15	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
7/9/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
7/9/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
7/9/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
7/9/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



7/9/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
7/9/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
7/9/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
7/9/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	32	1007	PGM-2400P (QRAE III)
7/9/2020	Pit B	8	10:35	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
7/9/2020	Pit B	8	15:35	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
8/9/2020	Area A	2.5	8:30	Rain	0	0	0	20.9	25	1012	PGM-2400P (QRAE III)
8/9/2020	Area A	2.5	13:30	Rain	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
8/9/2020	Area A	2.5	17:00	Rain	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
8/9/2020	Area B	2.5	8:45	Rain	0	0	0	20.9	25	1012	PGM-2400P (QRAE III)
8/9/2020	Area B	2.5	13:45	Rain	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
8/9/2020	Area B	2.5	16:45	Rain	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
8/9/2020	CHFC 4+50	2.5	8:55	Rain	0	0	0	20.9	25	1012	PGM-2400P (QRAE III)
8/9/2020	CHFC 4+50	2.5	13:55	Rain	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
8/9/2020	CHFC O+90	2.5	9:00	Rain	0	0	0	20.9	25	1012	PGM-2400P (QRAE III)
8/9/2020	CHFC O+90	2.5	14:00	Rain	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
8/9/2020	Pit C	8	9:15	Rain	0	0	0	20.9	25	1012	PGM-2400P (QRAE III)
8/9/2020	Pit C	8	14:15	Rain	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
8/9/2020	137 CH.C.T.2+66	3.1	9:35	Rain	0	0	0	20.9	25	1012	PGM-2400P (QRAE III)
8/9/2020	137 CH.C.T.2+66	3.1	14:35	Rain	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
8/9/2020	137 Pit C	3.5	9:45	Rain	0	0	0	20.9	25	1012	PGM-2400P (QRAE III)
8/9/2020	137 Pit C	3.5	14:45	Rain	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
8/9/2020	137 Pit B	1	9:55	Rain	0	0	0	20.9	25	1012	PGM-2400P (QRAE III)
8/9/2020	137 Pit B	1	14:55	Rain	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
8/9/2020	CHA 6+70	3.5	10:15	Rain	0	0	0	20.9	25	1012	PGM-2400P (QRAE III)

8/9/2020	CHA 6+70	3.5	15:15	Rain	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
8/9/2020	Pit B	8	10:35	Rain	0	0	0	20.9	25	1012	PGM-2400P (QRAE III)
8/9/2020	Pit B	8	15:35	Rain	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
9/9/2020	Area A	2.5	8:30	Rain	0	0	0	20.9	27	1012	PGM-2400P (QRAE III)
9/9/2020	Area A	2.5	13:30	Rain	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
9/9/2020	Area A	2.5	17:00	Rain	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
9/9/2020	Area B	2.5	8:45	Rain	0	0	0	20.9	27	1012	PGM-2400P (QRAE III)
9/9/2020	Area B	2.5	13:45	Rain	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
9/9/2020	Area B	2.5	16:45	Rain	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
9/9/2020	CHFC 4+50	2.5	8:55	Rain	0	0	0	20.9	27	1012	PGM-2400P (QRAE III)
9/9/2020	CHFC 4+50	2.5	13:55	Rain	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
9/9/2020	CHFC O+90	2.5	9:00	Rain	0	0	0	20.9	27	1012	PGM-2400P (QRAE III)
9/9/2020	CHFC O+90	2.5	14:00	Rain	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
9/9/2020	Pit C	8	9:15	Rain	0	0	0	20.9	27	1012	PGM-2400P (QRAE III)
9/9/2020	Pit C	8	14:15	Rain	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
9/9/2020	137 CH.C.T.2+66	3.1	9:35	Rain	0	0	0	20.9	27	1012	PGM-2400P (QRAE III)
9/9/2020	137 CH.C.T.2+66	3.1	14:35	Rain	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
9/9/2020	137 Pit C	3.5	9:45	Rain	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
9/9/2020	137 Pit C	3.5	14:45	Rain	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
9/9/2020	137 Pit B	1	9:55	Rain	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
9/9/2020	137 Pit B	1	14:55	Rain	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
9/9/2020	CHA 6+70	3.5	10:15	Rain	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
9/9/2020	CHA 6+70	3.5	15:15	Rain	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
9/9/2020	Pit B	8	10:35	Rain	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
9/9/2020	Pit B	8	15:35	Rain	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



10/9/2020	Area A	2.5	8:30	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
10/9/2020	Area A	2.5	13:30	Rain	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
10/9/2020	Area A	2.5	17:00	Rain	0	0	0	20.9	29	1006	PGM-2400P (QRAE III)
10/9/2020	Area B	2.5	8:45	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
10/9/2020	Area B	2.5	13:45	Rain	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
10/9/2020	Area B	2.5	16:45	Rain	0	0	0	20.9	29	1006	PGM-2400P (QRAE III)
10/9/2020	CHFC 4+50	2.5	8:55	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
10/9/2020	CHFC 4+50	2.5	13:55	Rain	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
10/9/2020	CHFC O+90	2.5	9:00	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
10/9/2020	CHFC O+90	2.5	14:00	Rain	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
10/9/2020	Pit C	8	9:15	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
10/9/2020	Pit C	8	14:15	Rain	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
10/9/2020	137 CH.C.T.2+66	3.1	9:35	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
10/9/2020	137 CH.C.T.2+66	3.1	14:35	Rain	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
10/9/2020	137 Pit C	3.5	9:45	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
10/9/2020	137 Pit C	3.5	14:45	Rain	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
10/9/2020	137 Pit B	1	9:55	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
10/9/2020	137 Pit B	1	14:55	Rain	0	0	0	20.9	31	1005	PGM-2400P (QRAE III)
10/9/2020	CHA 6+70	3.5	10:15	Rain	0	0	0	20.9	27	1008	PGM-2400P (QRAE III)
10/9/2020	CHA 6+70	3.5	15:15	Rain	0	0	0	20.9	29	1005	PGM-2400P (QRAE III)
10/9/2020	Pit B	8	10:35	Rain	0	0	0	20.9	27	1008	PGM-2400P (QRAE III)
10/9/2020	Pit B	8	15:35	Rain	0	0	0	20.9	29	1005	PGM-2400P (QRAE III)
11/9/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
11/9/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
11/9/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



11/9/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
11/9/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
11/9/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	28	1007	PGM-2400P (QRAE III)
11/9/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
11/9/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
11/9/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
11/9/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
11/9/2020	Pit C	8	9:15	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
11/9/2020	Pit C	8	14:15	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
11/9/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
11/9/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
11/9/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
11/9/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
11/9/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
11/9/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
11/9/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
11/9/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
11/9/2020	Pit B	8	10:35	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
11/9/2020	Pit B	8	15:35	Fine	0	0	0	20.9	30	1007	PGM-2400P (QRAE III)
12/9/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
12/9/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
12/9/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
12/9/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
12/9/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
12/9/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



12/9/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
12/9/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	25	1011	PGM-2400P (QRAE III)
12/9/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
12/9/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	25	1011	PGM-2400P (QRAE III)
12/9/2020	Pit C	8	9:15	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
12/9/2020	Pit C	8	14:15	Fine	0	0	0	20.9	25	1010	PGM-2400P (QRAE III)
12/9/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	30	1011	PGM-2400P (QRAE III)
12/9/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	25	1010	PGM-2400P (QRAE III)
12/9/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	30	1011	PGM-2400P (QRAE III)
12/9/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	25	1010	PGM-2400P (QRAE III)
12/9/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	30	1011	PGM-2400P (QRAE III)
12/9/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	26	1010	PGM-2400P (QRAE III)
12/9/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	30	1011	PGM-2400P (QRAE III)
12/9/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	26	1010	PGM-2400P (QRAE III)
12/9/2020	Pit B	8	10:35	Fine	0	0	0	20.9	30	1011	PGM-2400P (QRAE III)
12/9/2020	Pit B	8	15:35	Fine	0	0	0	20.9	26	1010	PGM-2400P (QRAE III)
14/9/2020	Area A	2.5	8:30	Rain	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
14/9/2020	Area A	2.5	13:30	Rain	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
14/9/2020	Area A	2.5	17:00	Rain	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
14/9/2020	Area B	2.5	8:45	Rain	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
14/9/2020	Area B	2.5	13:45	Rain	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
14/9/2020	Area B	2.5	16:45	Rain	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
14/9/2020	CHFC 4+50	2.5	8:55	Rain	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
14/9/2020	CHFC 4+50	2.5	13:55	Rain	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
14/9/2020	CHFC O+90	2.5	9:00	Rain	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)

14/9/2020	CHFC O+90	2.5	14:00	Rain	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
14/9/2020	Pit C	8	9:15	Rain	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
14/9/2020	Pit C	8	14:15	Rain	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
14/9/2020	137 CH.C.T.2+66	3.1	9:35	Rain	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
14/9/2020	137 CH.C.T.2+66	3.1	14:35	Rain	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
14/9/2020	137 Pit C	3.5	9:45	Rain	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
14/9/2020	137 Pit C	3.5	14:45	Rain	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
14/9/2020	137 Pit B	1	9:55	Rain	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
14/9/2020	137 Pit B	1	14:55	Rain	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
14/9/2020	WPR1	2.2	10:05	Rain	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
14/9/2020	WPR1	2.2	15:05	Rain	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
14/9/2020	CHA 6+70	3.5	10:15	Rain	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
14/9/2020	CHA 6+70	3.5	15:15	Rain	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
14/9/2020	Pit B	8	10:35	Rain	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
14/9/2020	Pit B	8	15:35	Rain	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
15/9/2020	Area A	2.5	8:30	Rain	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
15/9/2020	Area A	2.5	13:30	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
15/9/2020	Area A	2.5	17:00	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
15/9/2020	Area B	2.5	8:45	Rain	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
15/9/2020	Area B	2.5	13:45	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
15/9/2020	Area B	2.5	16:45	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
15/9/2020	CHFC 4+50	2.5	8:55	Rain	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
15/9/2020	CHFC 4+50	2.5	13:55	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
15/9/2020	CHFC O+90	2.5	9:00	Rain	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
15/9/2020	CHFC O+90	2.5	14:00	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



15/9/2020	Pit C	8	9:15	Rain	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
15/9/2020	Pit C	8	14:15	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
15/9/2020	137 CH.C.T.2+66	3.1	9:35	Rain	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
15/9/2020	137 CH.C.T.2+66	3.1	14:35	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
15/9/2020	137 Pit C	3.5	9:45	Rain	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
15/9/2020	137 Pit C	3.5	14:45	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
15/9/2020	137 Pit B	1	9:55	Rain	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
15/9/2020	137 Pit B	1	14:55	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
15/9/2020	WPR1	2.2	10:05	Rain	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
15/9/2020	WPR1	2.2	15:05	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
15/9/2020	CHA 6+70	3.5	10:15	Rain	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
15/9/2020	CHA 6+70	3.5	15:15	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
15/9/2020	Pit B	8	10:35	Rain	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
15/9/2020	Pit B	8	15:35	Rain	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
16/9/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
16/9/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
16/9/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)
16/9/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
16/9/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
16/9/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	30	1006	PGM-2400P (QRAE III)
16/9/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
16/9/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
16/9/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
16/9/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
16/9/2020	Pit C	8	9:15	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



16/9/2020	Pit C	8	14:15	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
16/9/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
16/9/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	31	1007	PGM-2400P (QRAE III)
16/9/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
16/9/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
16/9/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
16/9/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
16/9/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
16/9/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
16/9/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
16/9/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
16/9/2020	Pit B	8	10:35	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
16/9/2020	Pit B	8	15:35	Fine	0	0	0	20.9	31	1006	PGM-2400P (QRAE III)
17/9/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)
17/9/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	29	1006	PGM-2400P (QRAE III)
17/9/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	29	1005	PGM-2400P (QRAE III)
17/9/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
17/9/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	29	1006	PGM-2400P (QRAE III)
17/9/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	29	1005	PGM-2400P (QRAE III)
17/9/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
17/9/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	29	1005	PGM-2400P (QRAE III)
17/9/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
17/9/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
17/9/2020	Pit C	8	9:15	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
17/9/2020	Pit C	8	14:15	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)

17/9/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
17/9/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
17/9/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
17/9/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
17/9/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
17/9/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	30	1005	PGM-2400P (QRAE III)
17/9/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
17/9/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	29	1005	PGM-2400P (QRAE III)
17/9/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	28	1007	PGM-2400P (QRAE III)
17/9/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	29	1005	PGM-2400P (QRAE III)
17/9/2020	Pit B	8	10:35	Fine	0	0	0	20.9	28	1007	PGM-2400P (QRAE III)
17/9/2020	Pit B	8	15:35	Fine	0	0	0	20.9	29	1005	PGM-2400P (QRAE III)
18/9/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
18/9/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
18/9/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
18/9/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
18/9/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
18/9/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
18/9/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
18/9/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
18/9/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
18/9/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
18/9/2020	Pit C	8	9:15	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
18/9/2020	Pit C	8	14:15	Fine	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)
18/9/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)

18/9/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)
18/9/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
18/9/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	29	1007	PGM-2400P (QRAE III)
18/9/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
18/9/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	28	1007	PGM-2400P (QRAE III)
18/9/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
18/9/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	28	1007	PGM-2400P (QRAE III)
18/9/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
18/9/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	28	1007	PGM-2400P (QRAE III)
18/9/2020	Pit B	8	10:35	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
18/9/2020	Pit B	8	15:35	Fine	0	0	0	20.9	28	1007	PGM-2400P (QRAE III)
19/9/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
19/9/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
19/9/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
19/9/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
19/9/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
19/9/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
19/9/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
19/9/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
19/9/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
19/9/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
19/9/2020	Pit C	8	9:15	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
19/9/2020	Pit C	8	14:15	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
19/9/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
19/9/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)

19/9/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
19/9/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
19/9/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	29	1012	PGM-2400P (QRAE III)
19/9/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
19/9/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	29	1012	PGM-2400P (QRAE III)
19/9/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
19/9/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	29	1012	PGM-2400P (QRAE III)
19/9/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
19/9/2020	Pit B	8	10:35	Fine	0	0	0	20.9	29	1012	PGM-2400P (QRAE III)
19/9/2020	Pit B	8	15:35	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
21/9/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
21/9/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
21/9/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
21/9/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
21/9/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
21/9/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
21/9/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
21/9/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	26	1010	PGM-2400P (QRAE III)
21/9/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
21/9/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	26	1010	PGM-2400P (QRAE III)
21/9/2020	Pit C	8	9:15	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
21/9/2020	Pit C	8	14:15	Fine	0	0	0	20.9	26	1010	PGM-2400P (QRAE III)
21/9/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
21/9/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	26	1010	PGM-2400P (QRAE III)
21/9/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



21/9/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	26	1010	PGM-2400P (QRAE III)
21/9/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
21/9/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	26	1010	PGM-2400P (QRAE III)
21/9/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
21/9/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
21/9/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
21/9/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
21/9/2020	Pit B	8	10:35	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
21/9/2020	Pit B	8	15:35	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
22/9/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
22/9/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
22/9/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
22/9/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
22/9/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
22/9/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
22/9/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
22/9/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
22/9/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
22/9/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
22/9/2020	Pit C	8	9:15	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
22/9/2020	Pit C	8	14:15	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
22/9/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
22/9/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
22/9/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
22/9/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)

22/9/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
22/9/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
22/9/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
22/9/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
22/9/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
22/9/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
22/9/2020	Pit B	8	10:35	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
22/9/2020	Pit B	8	15:35	Fine	0	0	0	20.9	30	1008	PGM-2400P (QRAE III)
23/9/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
23/9/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
23/9/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
23/9/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
23/9/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
23/9/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
23/9/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
23/9/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
23/9/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
23/9/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
23/9/2020	Pit C	8	9:15	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
23/9/2020	Pit C	8	14:15	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
23/9/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
23/9/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
23/9/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
23/9/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
23/9/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)

23/9/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
23/9/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	30	1011	PGM-2400P (QRAE III)
23/9/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
23/9/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	30	1011	PGM-2400P (QRAE III)
23/9/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
23/9/2020	Pit B	8	10:35	Fine	0	0	0	20.9	30	1011	PGM-2400P (QRAE III)
23/9/2020	Pit B	8	15:35	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
24/9/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
24/9/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
24/9/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
24/9/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
24/9/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
24/9/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
24/9/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	27	1012	PGM-2400P (QRAE III)
24/9/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
24/9/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	27	1012	PGM-2400P (QRAE III)
24/9/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	30	1010	PGM-2400P (QRAE III)
24/9/2020	Pit C	8	9:15	Fine	0	0	0	20.9	27	1012	PGM-2400P (QRAE III)
24/9/2020	Pit C	8	14:15	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
24/9/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	27	1012	PGM-2400P (QRAE III)
24/9/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
24/9/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	27	1012	PGM-2400P (QRAE III)
24/9/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
24/9/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	27	1012	PGM-2400P (QRAE III)
24/9/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)

24/9/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
24/9/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
24/9/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
24/9/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
24/9/2020	WPR3	1.5	10:25	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
24/9/2020	WPR3	1.5	15:25	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
24/9/2020	Pit B	8	10:35	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
24/9/2020	Pit B	8	15:35	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
25/9/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
25/9/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
25/9/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
25/9/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
25/9/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
25/9/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
25/9/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
25/9/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
25/9/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
25/9/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
25/9/2020	Pit C	8	9:15	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
25/9/2020	Pit C	8	14:15	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
25/9/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
25/9/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
25/9/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
25/9/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
25/9/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)

25/9/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
25/9/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
25/9/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
25/9/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
25/9/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
25/9/2020	WPR3	1.5	10:25	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
25/9/2020	WPR3	1.5	15:25	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
25/9/2020	Pit B	8	10:35	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
25/9/2020	Pit B	8	15:35	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
26/9/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
26/9/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
26/9/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	27	1008	PGM-2400P (QRAE III)
26/9/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
26/9/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
26/9/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	27	1008	PGM-2400P (QRAE III)
26/9/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
26/9/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
26/9/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
26/9/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
26/9/2020	Pit C	8	9:15	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
26/9/2020	Pit C	8	14:15	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
26/9/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
26/9/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
26/9/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
26/9/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)

26/9/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
26/9/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
26/9/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
26/9/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
26/9/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
26/9/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
26/9/2020	WPR3	1.5	10:25	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
26/9/2020	WPR3	1.5	15:25	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
26/9/2020	Pit B	8	10:35	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
26/9/2020	Pit B	8	15:35	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
28/9/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
28/9/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	26	1010	PGM-2400P (QRAE III)
28/9/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
28/9/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
28/9/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	26	1010	PGM-2400P (QRAE III)
28/9/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	28	1009	PGM-2400P (QRAE III)
28/9/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
28/9/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
28/9/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
28/9/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
28/9/2020	Pit C	8	9:15	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
28/9/2020	Pit C	8	14:15	Fine	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
28/9/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
28/9/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
28/9/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)

28/9/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
28/9/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
28/9/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
28/9/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
28/9/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
28/9/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
28/9/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
28/9/2020	WPR3	1.5	10:25	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
28/9/2020	WPR3	1.5	15:25	Fine	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
28/9/2020	Pit B	8	10:35	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
28/9/2020	Pit B	8	15:35	Fine	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
29/9/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
29/9/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
29/9/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	27	1006	PGM-2400P (QRAE III)
29/9/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
29/9/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
29/9/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	27	1006	PGM-2400P (QRAE III)
29/9/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
29/9/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
29/9/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	27	1009	PGM-2400P (QRAE III)
29/9/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	26	1008	PGM-2400P (QRAE III)
29/9/2020	Pit C	8	9:15	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
29/9/2020	Pit C	8	14:15	Fine	0	0	0	20.9	26	1007	PGM-2400P (QRAE III)
29/9/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
29/9/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	26	1007	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



29/9/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
29/9/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	26	1006	PGM-2400P (QRAE III)
29/9/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
29/9/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	26	1006	PGM-2400P (QRAE III)
29/9/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
29/9/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	26	1006	PGM-2400P (QRAE III)
29/9/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
29/9/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	26	1006	PGM-2400P (QRAE III)
29/9/2020	WPR3	1.5	10:25	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
29/9/2020	WPR3	1.5	15:25	Fine	0	0	0	20.9	26	1006	PGM-2400P (QRAE III)
29/9/2020	Pit B	8	10:35	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
29/9/2020	Pit B	8	15:35	Fine	0	0	0	20.9	26	1006	PGM-2400P (QRAE III)
30/9/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	28	1007	PGM-2400P (QRAE III)
30/9/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	27	1006	PGM-2400P (QRAE III)
30/9/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	28	1005	PGM-2400P (QRAE III)
30/9/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	28	1007	PGM-2400P (QRAE III)
30/9/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	27	1006	PGM-2400P (QRAE III)
30/9/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	28	1005	PGM-2400P (QRAE III)
30/9/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
30/9/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	27	1006	PGM-2400P (QRAE III)
30/9/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
30/9/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	27	1006	PGM-2400P (QRAE III)
30/9/2020	Pit C	8	9:15	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
30/9/2020	Pit C	8	14:15	Fine	0	0	0	20.9	27	1006	PGM-2400P (QRAE III)
30/9/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)

30/9/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	27	1006	PGM-2400P (QRAE III)
30/9/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
30/9/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	27	1006	PGM-2400P (QRAE III)
30/9/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
30/9/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	27	1006	PGM-2400P (QRAE III)
30/9/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
30/9/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	27	1005	PGM-2400P (QRAE III)
30/9/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
30/9/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	27	1005	PGM-2400P (QRAE III)
30/9/2020	WPR3	1.5	10:25	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
30/9/2020	WPR3	1.5	15:25	Fine	0	0	0	20.9	27	1005	PGM-2400P (QRAE III)
30/9/2020	Pit B	8	10:35	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
30/9/2020	Pit B	8	15:35	Fine	0	0	0	20.9	27	1005	PGM-2400P (QRAE III)
3/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	27	1012	PGM-2400P (QRAE III)
3/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
3/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
3/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	27	1012	PGM-2400P (QRAE III)
3/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
3/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
3/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	27	1012	PGM-2400P (QRAE III)
3/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
3/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	27	1012	PGM-2400P (QRAE III)
3/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
3/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
3/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



3/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
3/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
3/10/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
3/10/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
3/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
3/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
3/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	29	1012	PGM-2400P (QRAE III)
3/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	30	1009	PGM-2400P (QRAE III)
3/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	29	1012	PGM-2400P (QRAE III)
3/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
3/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	29	1012	PGM-2400P (QRAE III)
3/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
3/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	29	1012	PGM-2400P (QRAE III)
3/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	29	1009	PGM-2400P (QRAE III)
5/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	25	1011	PGM-2400P (QRAE III)
5/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
5/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
5/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	25	1011	PGM-2400P (QRAE III)
5/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	29	1010	PGM-2400P (QRAE III)
5/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
5/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	25	1011	PGM-2400P (QRAE III)
5/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
5/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	25	1011	PGM-2400P (QRAE III)
5/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
5/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	25	1011	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



5/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
5/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
5/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
5/10/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
5/10/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
5/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
5/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
5/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
5/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
5/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
5/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
5/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
5/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
5/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
5/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
6/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	24	1014	PGM-2400P (QRAE III)
6/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
6/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
6/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	24	1014	PGM-2400P (QRAE III)
6/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
6/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
6/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	24	1014	PGM-2400P (QRAE III)
6/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
6/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	25	1014	PGM-2400P (QRAE III)
6/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



6/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	25	1014	PGM-2400P (QRAE III)
6/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
6/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	25	1014	PGM-2400P (QRAE III)
6/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
6/10/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	25	1014	PGM-2400P (QRAE III)
6/10/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
6/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	25	1014	PGM-2400P (QRAE III)
6/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
6/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	25	1014	PGM-2400P (QRAE III)
6/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
6/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
6/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
6/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
6/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
6/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
6/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
7/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
7/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
7/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	25	1012	PGM-2400P (QRAE III)
7/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
7/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
7/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	25	1012	PGM-2400P (QRAE III)
7/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
7/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
7/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



7/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
7/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
7/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
7/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
7/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
7/10/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
7/10/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	25	1012	PGM-2400P (QRAE III)
7/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
7/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	25	1012	PGM-2400P (QRAE III)
7/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	24	1017	PGM-2400P (QRAE III)
7/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	25	1012	PGM-2400P (QRAE III)
7/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
7/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	25	1012	PGM-2400P (QRAE III)
7/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
7/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	25	1012	PGM-2400P (QRAE III)
7/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
7/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	25	1012	PGM-2400P (QRAE III)
8/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	23	1016	PGM-2400P (QRAE III)
8/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	27	1014	PGM-2400P (QRAE III)
8/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
8/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	23	1016	PGM-2400P (QRAE III)
8/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	27	1014	PGM-2400P (QRAE III)
8/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
8/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	23	1016	PGM-2400P (QRAE III)
8/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



8/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	23	1016	PGM-2400P (QRAE III)
8/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
8/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	23	1017	PGM-2400P (QRAE III)
8/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
8/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	23	1016	PGM-2400P (QRAE III)
8/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
8/10/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	23	1016	PGM-2400P (QRAE III)
8/10/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
8/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	23	1016	PGM-2400P (QRAE III)
8/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
8/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
8/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
8/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
8/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
8/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
8/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
8/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
8/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
9/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
9/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
9/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	27	1012	PGM-2400P (QRAE III)
9/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
9/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
9/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	27	1012	PGM-2400P (QRAE III)
9/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



9/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
9/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
9/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
9/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
9/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
9/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
9/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
9/10/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	25	1016	PGM-2400P (QRAE III)
9/10/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
9/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	25	1016	PGM-2400P (QRAE III)
9/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
9/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	25	1016	PGM-2400P (QRAE III)
9/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
9/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	26	1016	PGM-2400P (QRAE III)
9/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
9/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	26	1016	PGM-2400P (QRAE III)
9/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
9/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	26	1016	PGM-2400P (QRAE III)
9/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
10/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	24	1014	PGM-2400P (QRAE III)
10/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
10/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
10/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	24	1014	PGM-2400P (QRAE III)
10/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
10/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



10/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
10/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
10/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
10/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
10/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
10/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
10/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
10/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
10/10/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
10/10/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
10/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
10/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
10/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
10/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
10/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
10/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
10/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
10/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
10/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
10/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	28	1010	PGM-2400P (QRAE III)
12/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
12/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)
12/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	28	1007	PGM-2400P (QRAE III)
12/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
12/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	29	1008	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



12/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	28	1007	PGM-2400P (QRAE III)
12/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
12/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
12/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
12/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	28	1008	PGM-2400P (QRAE III)
12/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
12/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	28	1007	PGM-2400P (QRAE III)
12/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
12/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	28	1007	PGM-2400P (QRAE III)
12/10/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
12/10/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	28	1007	PGM-2400P (QRAE III)
12/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
12/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	28	1007	PGM-2400P (QRAE III)
12/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
12/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	28	1007	PGM-2400P (QRAE III)
12/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
12/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	28	1007	PGM-2400P (QRAE III)
12/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
12/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	28	1007	PGM-2400P (QRAE III)
12/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	27	1010	PGM-2400P (QRAE III)
12/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	28	1007	PGM-2400P (QRAE III)
14/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
14/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
14/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
14/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



14/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
14/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
14/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
14/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
14/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
14/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
14/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
14/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
14/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
14/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
14/10/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
14/10/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
14/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
14/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
14/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
14/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
14/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
14/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
14/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
14/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
14/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
14/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	26	1012	PGM-2400P (QRAE III)
15/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	25	1015	PGM-2400P (QRAE III)
15/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
15/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



15/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	25	1015	PGM-2400P (QRAE III)
15/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
15/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
15/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	25	1015	PGM-2400P (QRAE III)
15/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
15/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	25	1015	PGM-2400P (QRAE III)
15/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
15/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	25	1015	PGM-2400P (QRAE III)
15/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
15/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	25	1015	PGM-2400P (QRAE III)
15/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
15/10/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	25	1015	PGM-2400P (QRAE III)
15/10/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	28	1012	PGM-2400P (QRAE III)
15/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	25	1015	PGM-2400P (QRAE III)
15/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
15/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	26	1015	PGM-2400P (QRAE III)
15/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
15/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	26	1015	PGM-2400P (QRAE III)
15/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	28	1011	PGM-2400P (QRAE III)
15/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	26	1015	PGM-2400P (QRAE III)
15/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
15/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	26	1015	PGM-2400P (QRAE III)
15/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
16/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	25	1014	PGM-2400P (QRAE III)
16/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	30	1012	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



16/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
16/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	25	1014	PGM-2400P (QRAE III)
16/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	30	1012	PGM-2400P (QRAE III)
16/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
16/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
16/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	30	1011	PGM-2400P (QRAE III)
16/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
16/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	30	1011	PGM-2400P (QRAE III)
16/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
16/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	30	1011	PGM-2400P (QRAE III)
16/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
16/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	30	1011	PGM-2400P (QRAE III)
16/10/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
16/10/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
16/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
16/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
16/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	27	1014	PGM-2400P (QRAE III)
16/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	29	1011	PGM-2400P (QRAE III)
16/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	27	1014	PGM-2400P (QRAE III)
16/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	30	1011	PGM-2400P (QRAE III)
16/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	27	1014	PGM-2400P (QRAE III)
16/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	30	1011	PGM-2400P (QRAE III)
16/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	27	1014	PGM-2400P (QRAE III)
16/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	30	1011	PGM-2400P (QRAE III)
17/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	25	1016	PGM-2400P (QRAE III)

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



17/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
17/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
17/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	25	1016	PGM-2400P (QRAE III)
17/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
17/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
17/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	25	1015	PGM-2400P (QRAE III)
17/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
17/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	25	1015	PGM-2400P (QRAE III)
17/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
17/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	25	1015	PGM-2400P (QRAE III)
17/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
17/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	25	1015	PGM-2400P (QRAE III)
17/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
17/10/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	26	1015	PGM-2400P (QRAE III)
17/10/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
17/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	26	1015	PGM-2400P (QRAE III)
17/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
17/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	26	1015	PGM-2400P (QRAE III)
17/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
17/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	26	1015	PGM-2400P (QRAE III)
17/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
17/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	26	1015	PGM-2400P (QRAE III)
17/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
17/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	26	1015	PGM-2400P (QRAE III)
17/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



19/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	22	1017	PGM-2400P (QRAE III)
19/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
19/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
19/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	22	1017	PGM-2400P (QRAE III)
19/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
19/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
19/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	22	1017	PGM-2400P (QRAE III)
19/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	25	1014	PGM-2400P (QRAE III)
19/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	22	1017	PGM-2400P (QRAE III)
19/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	25	1014	PGM-2400P (QRAE III)
19/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	22	1017	PGM-2400P (QRAE III)
19/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	25	1014	PGM-2400P (QRAE III)
19/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	23	1017	PGM-2400P (QRAE III)
19/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
19/10/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	23	1017	PGM-2400P (QRAE III)
19/10/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
19/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	24	1017	PGM-2400P (QRAE III)
19/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
19/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	24	1017	PGM-2400P (QRAE III)
19/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
19/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	24	1017	PGM-2400P (QRAE III)
19/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
19/10/2020	WPR3	1.5	10:25	Fine	0	0	0	20.9	24	1017	PGM-2400P (QRAE III)
19/10/2020	WPR3	1.5	15:25	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
19/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	24	1017	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



19/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
20/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	23	1016	PGM-2400P (QRAE III)
20/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	27	1013	PGM-2400P (QRAE III)
20/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
20/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	23	1016	PGM-2400P (QRAE III)
20/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	27	1013	PGM-2400P (QRAE III)
20/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
20/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
20/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	27	1013	PGM-2400P (QRAE III)
20/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
20/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	27	1013	PGM-2400P (QRAE III)
20/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
20/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	27	1013	PGM-2400P (QRAE III)
20/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
20/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	27	1013	PGM-2400P (QRAE III)
20/10/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	25	1016	PGM-2400P (QRAE III)
20/10/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	27	1013	PGM-2400P (QRAE III)
20/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	25	1016	PGM-2400P (QRAE III)
20/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	27	1013	PGM-2400P (QRAE III)
20/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	25	1016	PGM-2400P (QRAE III)
20/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	28	1013	PGM-2400P (QRAE III)
20/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	25	1016	PGM-2400P (QRAE III)
20/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	28	1013	PGM-2400P (QRAE III)
20/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	25	1016	PGM-2400P (QRAE III)
20/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	27	1013	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



20/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	25	1016	PGM-2400P (QRAE III)
20/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	27	1013	PGM-2400P (QRAE III)
21/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	22	1013	PGM-2400P (QRAE III)
21/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	26	1010	PGM-2400P (QRAE III)
21/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
21/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	22	1013	PGM-2400P (QRAE III)
21/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	26	1010	PGM-2400P (QRAE III)
21/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
21/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	22	1013	PGM-2400P (QRAE III)
21/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	26	1010	PGM-2400P (QRAE III)
21/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	22	1013	PGM-2400P (QRAE III)
21/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	26	1010	PGM-2400P (QRAE III)
21/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	22	1013	PGM-2400P (QRAE III)
21/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
21/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	22	1013	PGM-2400P (QRAE III)
21/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
21/10/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	22	1013	PGM-2400P (QRAE III)
21/10/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
21/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	23	1013	PGM-2400P (QRAE III)
21/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
21/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	23	1013	PGM-2400P (QRAE III)
21/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
21/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	23	1013	PGM-2400P (QRAE III)
21/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
21/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	23	1013	PGM-2400P (QRAE III)

21/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
21/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	23	1013	PGM-2400P (QRAE III)
21/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	26	1009	PGM-2400P (QRAE III)
22/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	23	1009	PGM-2400P (QRAE III)
22/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
22/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	24	1008	PGM-2400P (QRAE III)
22/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	23	1009	PGM-2400P (QRAE III)
22/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	27	1007	PGM-2400P (QRAE III)
22/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	24	1008	PGM-2400P (QRAE III)
22/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	23	1009	PGM-2400P (QRAE III)
22/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	26	1007	PGM-2400P (QRAE III)
22/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	23	1009	PGM-2400P (QRAE III)
22/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	26	1007	PGM-2400P (QRAE III)
22/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	23	1010	PGM-2400P (QRAE III)
22/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	26	1007	PGM-2400P (QRAE III)
22/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	23	1010	PGM-2400P (QRAE III)
22/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	26	1007	PGM-2400P (QRAE III)
22/10/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	24	1010	PGM-2400P (QRAE III)
22/10/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	26	1007	PGM-2400P (QRAE III)
22/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	24	1010	PGM-2400P (QRAE III)
22/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	26	1007	PGM-2400P (QRAE III)
22/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	24	1010	PGM-2400P (QRAE III)
22/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	26	1007	PGM-2400P (QRAE III)
22/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	24	1010	PGM-2400P (QRAE III)
22/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	26	1007	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



22/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	24	1010	PGM-2400P (QRAE III)
22/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	26	1007	PGM-2400P (QRAE III)
22/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	24	1010	PGM-2400P (QRAE III)
22/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	26	1007	PGM-2400P (QRAE III)
23/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	22	1011	PGM-2400P (QRAE III)
23/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	23	1010	PGM-2400P (QRAE III)
23/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	23	1010	PGM-2400P (QRAE III)
23/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	22	1011	PGM-2400P (QRAE III)
23/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	23	1010	PGM-2400P (QRAE III)
23/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	23	1010	PGM-2400P (QRAE III)
23/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	22	1011	PGM-2400P (QRAE III)
23/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	23	1010	PGM-2400P (QRAE III)
23/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	22	1011	PGM-2400P (QRAE III)
23/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	23	1010	PGM-2400P (QRAE III)
23/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	22	1011	PGM-2400P (QRAE III)
23/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	23	1010	PGM-2400P (QRAE III)
23/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	22	1011	PGM-2400P (QRAE III)
23/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	23	1010	PGM-2400P (QRAE III)
23/10/2020	137 Pit C	3.5	9:45	Fine	0	0	0	20.9	22	1011	PGM-2400P (QRAE III)
23/10/2020	137 Pit C	3.5	14:45	Fine	0	0	0	20.9	23	1010	PGM-2400P (QRAE III)
23/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	22	1011	PGM-2400P (QRAE III)
23/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	23	1010	PGM-2400P (QRAE III)
23/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	22	1011	PGM-2400P (QRAE III)
23/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	23	1010	PGM-2400P (QRAE III)
23/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	22	1011	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



23/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	23	1010	PGM-2400P (QRAE III)
23/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	22	1011	PGM-2400P (QRAE III)
23/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	23	1010	PGM-2400P (QRAE III)
23/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	22	1011	PGM-2400P (QRAE III)
23/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	23	1010	PGM-2400P (QRAE III)
24/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	22	1015	PGM-2400P (QRAE III)
24/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	24	1012	PGM-2400P (QRAE III)
24/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	24	1012	PGM-2400P (QRAE III)
24/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	22	1015	PGM-2400P (QRAE III)
24/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	24	1012	PGM-2400P (QRAE III)
24/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	24	1012	PGM-2400P (QRAE III)
24/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	22	1015	PGM-2400P (QRAE III)
24/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	24	1012	PGM-2400P (QRAE III)
24/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	22	1015	PGM-2400P (QRAE III)
24/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	24	1012	PGM-2400P (QRAE III)
24/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	23	1015	PGM-2400P (QRAE III)
24/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	24	1012	PGM-2400P (QRAE III)
24/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	23	1015	PGM-2400P (QRAE III)
24/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	24	1012	PGM-2400P (QRAE III)
24/10/2020	137 Pit C	1.4	9:45	Fine	0	0	0	20.9	23	1015	PGM-2400P (QRAE III)
24/10/2020	137 Pit C	1.4	14:45	Fine	0	0	0	20.9	24	1012	PGM-2400P (QRAE III)
24/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	23	1015	PGM-2400P (QRAE III)
24/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	24	1012	PGM-2400P (QRAE III)
24/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	23	1014	PGM-2400P (QRAE III)
24/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	24	1012	PGM-2400P (QRAE III)

24/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	23	1015	PGM-2400P (QRAE III)
24/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	24	1012	PGM-2400P (QRAE III)
24/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	23	1015	PGM-2400P (QRAE III)
24/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	24	1012	PGM-2400P (QRAE III)
24/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	23	1015	PGM-2400P (QRAE III)
24/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	24	1012	PGM-2400P (QRAE III)
27/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	24	1013	PGM-2400P (QRAE III)
27/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
27/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
27/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	24	1013	PGM-2400P (QRAE III)
27/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
27/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
27/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
27/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
27/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
27/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
27/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
27/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	27	1011	PGM-2400P (QRAE III)
27/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	25	1014	PGM-2400P (QRAE III)
27/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
27/10/2020	137 Pit C	1.4	9:45	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
27/10/2020	137 Pit C	1.4	14:45	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
27/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)
27/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
27/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	26	1014	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



27/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
27/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
27/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
27/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
27/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
27/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
27/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	26	1011	PGM-2400P (QRAE III)
28/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	23	1016	PGM-2400P (QRAE III)
28/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
28/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	22	1014	PGM-2400P (QRAE III)
28/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	23	1016	PGM-2400P (QRAE III)
28/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	26	1013	PGM-2400P (QRAE III)
28/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	22	1014	PGM-2400P (QRAE III)
28/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
28/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
28/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
28/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
28/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
28/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
28/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
28/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	25	1013	PGM-2400P (QRAE III)
28/10/2020	137 Pit C	1.4	9:45	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
28/10/2020	137 Pit C	1.4	14:45	Fine	0	0	0	20.9	24	1013	PGM-2400P (QRAE III)
28/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
28/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	23	1013	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



28/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	25	1016	PGM-2400P (QRAE III)
28/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	23	1013	PGM-2400P (QRAE III)
28/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	25	1015	PGM-2400P (QRAE III)
28/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	23	1014	PGM-2400P (QRAE III)
28/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	25	1015	PGM-2400P (QRAE III)
28/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	23	1014	PGM-2400P (QRAE III)
28/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	25	1015	PGM-2400P (QRAE III)
28/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	23	1014	PGM-2400P (QRAE III)
29/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	24	1018	PGM-2400P (QRAE III)
29/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	26	1016	PGM-2400P (QRAE III)
29/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	25	1016	PGM-2400P (QRAE III)
29/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	24	1018	PGM-2400P (QRAE III)
29/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	26	1016	PGM-2400P (QRAE III)
29/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	25	1016	PGM-2400P (QRAE III)
29/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	24	1018	PGM-2400P (QRAE III)
29/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	26	1016	PGM-2400P (QRAE III)
29/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	24	1018	PGM-2400P (QRAE III)
29/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	26	1016	PGM-2400P (QRAE III)
29/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	24	1018	PGM-2400P (QRAE III)
29/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	26	1015	PGM-2400P (QRAE III)
29/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	25	1018	PGM-2400P (QRAE III)
29/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	26	1015	PGM-2400P (QRAE III)
29/10/2020	137 Pit C	1.4	9:45	Fine	0	0	0	20.9	25	1018	PGM-2400P (QRAE III)
29/10/2020	137 Pit C	1.4	14:45	Fine	0	0	0	20.9	26	1015	PGM-2400P (QRAE III)
29/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	25	1018	PGM-2400P (QRAE III)

29/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	26	1015	PGM-2400P (QRAE III)
29/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	25	1018	PGM-2400P (QRAE III)
29/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	26	1015	PGM-2400P (QRAE III)
29/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	25	1018	PGM-2400P (QRAE III)
29/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	26	1015	PGM-2400P (QRAE III)
29/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	25	1018	PGM-2400P (QRAE III)
29/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	26	1015	PGM-2400P (QRAE III)
29/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	25	1018	PGM-2400P (QRAE III)
29/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	26	1015	PGM-2400P (QRAE III)
30/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	23	1019	PGM-2400P (QRAE III)
30/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	26	1016	PGM-2400P (QRAE III)
30/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	24	1017	PGM-2400P (QRAE III)
30/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	23	1019	PGM-2400P (QRAE III)
30/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	26	1016	PGM-2400P (QRAE III)
30/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	24	1017	PGM-2400P (QRAE III)
30/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	23	1019	PGM-2400P (QRAE III)
30/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	26	1016	PGM-2400P (QRAE III)
30/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	23	1019	PGM-2400P (QRAE III)
30/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	26	1016	PGM-2400P (QRAE III)
30/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	23	1019	PGM-2400P (QRAE III)
30/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	26	1016	PGM-2400P (QRAE III)
30/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	23	1019	PGM-2400P (QRAE III)
30/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	26	1016	PGM-2400P (QRAE III)
30/10/2020	137 Pit C	1.4	9:45	Fine	0	0	0	20.9	23	1019	PGM-2400P (QRAE III)
30/10/2020	137 Pit C	1.4	14:45	Fine	0	0	0	20.9	26	1016	PGM-2400P (QRAE III)

Contract No. 13/WSD/16

Mainlaying in Tseung Kwan O

9th Quarterly EM&A Report for August 2020 to October 2020



30/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	23	1019	PGM-2400P (QRAE III)
30/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	25	1016	PGM-2400P (QRAE III)
30/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	23	1019	PGM-2400P (QRAE III)
30/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
30/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	23	1019	PGM-2400P (QRAE III)
30/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
30/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	23	1019	PGM-2400P (QRAE III)
30/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
30/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	23	1019	PGM-2400P (QRAE III)
30/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	24	1016	PGM-2400P (QRAE III)
31/10/2020	Area A	2.5	8:30	Fine	0	0	0	20.9	22	1020	PGM-2400P (QRAE III)
31/10/2020	Area A	2.5	13:30	Fine	0	0	0	20.9	25	1016	PGM-2400P (QRAE III)
31/10/2020	Area A	2.5	17:00	Fine	0	0	0	20.9	23	1015	PGM-2400P (QRAE III)
31/10/2020	Area B	2.5	8:45	Fine	0	0	0	20.9	22	1020	PGM-2400P (QRAE III)
31/10/2020	Area B	2.5	13:45	Fine	0	0	0	20.9	25	1016	PGM-2400P (QRAE III)
31/10/2020	Area B	2.5	16:45	Fine	0	0	0	20.9	23	1015	PGM-2400P (QRAE III)
31/10/2020	CHFC 4+50	2.5	8:55	Fine	0	0	0	20.9	22	1020	PGM-2400P (QRAE III)
31/10/2020	CHFC 4+50	2.5	13:55	Fine	0	0	0	20.9	25	1016	PGM-2400P (QRAE III)
31/10/2020	CHFC O+90	2.5	9:00	Fine	0	0	0	20.9	22	1020	PGM-2400P (QRAE III)
31/10/2020	CHFC O+90	2.5	14:00	Fine	0	0	0	20.9	25	1016	PGM-2400P (QRAE III)
31/10/2020	Pit C	8	9:15	Fine	0	0	0	20.9	22	1020	PGM-2400P (QRAE III)
31/10/2020	Pit C	8	14:15	Fine	0	0	0	20.9	25	1015	PGM-2400P (QRAE III)
31/10/2020	137 CH.C.T.2+66	3.1	9:35	Fine	0	0	0	20.9	22	1020	PGM-2400P (QRAE III)
31/10/2020	137 CH.C.T.2+66	3.1	14:35	Fine	0	0	0	20.9	25	1015	PGM-2400P (QRAE III)
31/10/2020	137 Pit C	1.4	9:45	Fine	0	0	0	20.9	22	1020	PGM-2400P (QRAE III)

Contract No. 13/WSD/16**Mainlaying in Tseung Kwan O****9th Quarterly EM&A Report for August 2020 to October 2020**

31/10/2020	137 Pit C	1.4	14:45	Fine	0	0	0	20.9	25	1015	PGM-2400P (QRAE III)
31/10/2020	137 Pit B	1	9:55	Fine	0	0	0	20.9	22	1020	PGM-2400P (QRAE III)
31/10/2020	137 Pit B	1	14:55	Fine	0	0	0	20.9	25	1015	PGM-2400P (QRAE III)
31/10/2020	WPR1	2.2	10:05	Fine	0	0	0	20.9	22	1020	PGM-2400P (QRAE III)
31/10/2020	WPR1	2.2	15:05	Fine	0	0	0	20.9	25	1015	PGM-2400P (QRAE III)
31/10/2020	CHA 6+70	3.5	10:15	Fine	0	0	0	20.9	22	1020	PGM-2400P (QRAE III)
31/10/2020	CHA 6+70	3.5	15:15	Fine	0	0	0	20.9	24	1015	PGM-2400P (QRAE III)
31/10/2020	WPR3	2.5	10:25	Fine	0	0	0	20.9	22	1020	PGM-2400P (QRAE III)
31/10/2020	WPR3	2.5	15:25	Fine	0	0	0	20.9	24	1015	PGM-2400P (QRAE III)
31/10/2020	Pit B	8	10:35	Fine	0	0	0	20.9	22	1020	PGM-2400P (QRAE III)
31/10/2020	Pit B	8	15:35	Fine	0	0	0	20.9	24	1015	PGM-2400P (QRAE III)

Appendix I

Complaint Log and Regulatory Compliance Proforma

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020

Statistical Summary of Environmental Complaints

Reporting Period	Environmental Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
1 August 2020-31 October 2020	0	0	N/A

Statistical Summary of Environmental Summons

Reporting Period	Environmental Summons Statistics		
	Frequency	Cumulative	Details
1 August 2020-31 October 2020	0	0	N/A

Statistical Summary of Environmental Prosecution

Reporting Period	Environmental Prosecution Statistics		
	Frequency	Cumulative	Details
1 August 2020-31 October 2020	0	0	N/A

Appendix J

Noise Impact Monitoring Result

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020

Date	Time	Weather	Leq-5min, dB(A)						Leq-30min, dB(A)	Leq30 (min) L ₁₀ dB(A)	Leq30 (min) L ₉₀ dB(A)	Limit Level, dB(A)
			Reading (1)	Reading (2)	Reading (3)	Reading (4)	Reading (5)	Reading (6)				
16/10/2020	14:10 - 14:40	Sunny	63.9	65.0	63.8	64.1	64.1	64.9	64.3	66.1	60.2	70.0
24/10/2020	11:15 - 11:45	Sunny	57.6	57.6	57.7	58.4	58.1	57.0	57.8	58.4	57.1	70.0
30/10/2020	11:05 - 11:35	Sunny	63.2	60.4	61.5	62.7	61.8	61.1	61.9	64.0	59.9	70.0

No examination was scheduled in the reporting month. Hence the noise limit level will be 70.0 dB(A) Academic School Calendar can be found in Appendix O.



16/10/2020



24/10/2020



30/10/2020

Appendix K

Academic School Calendar

Contract No. 13/WSD/16
Mainlaying in Tseung Kwan O
9th Quarterly EM&A Report for August 2020 to October 2020



CREATIVE SECONDARY SCHOOL CALENDAR 2020-2021

	Su	Mo	Tu	We	Th	Fr	Sa		
August		9	10	11	12	13	14	15	
	16	17	18	19	20	21	22	19/8 First School day	
1	23	24A	25B	26C	27D	28E	29		
	30	31F							
September	2		1	2A	3B	4C	5	1/8 Staff Development Day 1	
3	6	7	8D	9E	10F	11A	12	Legco election 6 Sep, EDB declare 7/9 as school holiday	
	13	14B	15C	16D	17E	18F	19	18/09 Swimming gala	
4	20	21A	22B	23C	24D	25E	26		
5	27	28F	29A	30B					
October							3	1/10 National Day, 2/10 The Day following Mid-Autumn Festival	
4	5C	6D	7E	8F	9A	10			
6	11	12B	13C	14D	15E	16F	17		
	18	19	20	21	22	23	24	19-24 Term Break	
7	25	26	27A	28B	29C	30D	31	26/10 Chung Yeung Festival Holiday.	
November	8	1	2E	3F	4A	5B	6C	7	5/11 University Fair
	8	9	10D	11E	12F	13A	14	9/11/2020 Staff Development Day 2	
9	15	16B	17C	18D	19E	20F	21		
10	22	23A	24B	25C	26D	27E	28		
	29	30F							
December	11		1A	2B	3C	4	5	04/12 Sports Day	
12	6	7D	8E	9F	10A	11B	12		
	13	14C	15D	16E	17F	18A	19		
	20	21	22	23	24	25	26	25/12 Christmas Day 16/12 The First Weekday after Christmas Day	
	27	28	29	30	31			21/12-2/1 Christmas & New Year Holiday	
January							2	1/1 New Year's Day	
13	3	4B	5C	6D	7E	8F	9		
14	10	11A	12B	13C	14D	15E	16		
15	17	18F	19A	20B	21C	22D	23		
16	24	25E	26F	27A	28B	29C	30		
	31								
February	17	1D	2E	3F	4A	5B	6		
	7	8C	9D	10	11	12	13	12-15 New year Holiday, 10-20/2 Chinese New Year Holiday	
	14	15	16	17	18	19	20		
18	21	22E	23F	24A	25B	26C	27		
	28								
March	19	1D	2E	3F	4A	5B	6		
	7	8C	9D	10E	11F	12A	13		
20	14	15B	16C	17D	18E	19F	20		
	21	22	23	24	25	26	27	Creative Week	
21	28	29A	30B	31C					
April							1	01/04-10/04 Easter Holiday, 02/04 Good Friday, 03/04 The Day following Good Friday	
	4	5	6	7	8	9	10	04/04 Ching Ming Festival, 05/04 Easter Monday	
22	11	12D	13E	14F	15A	16B	17		
	18	19C	20D	21E	22F	23A	24		
23	25	26B	27C	28D	29E	30F			
May							1	Labour Day	
24	2	3A	4B	5C	6D	7E	8		
25	9	10F	11A	12B	13C	14D	15		
26	16	17E	18F	19A	20B	21C	22	Birthday of Buddha	
	23	24C	25D	26E	27F	28A	29		
27	30	31B							
June			1C	2D	3E	4F	5		
28	6	7A	8B	9C	10D	11E	12		
29	13	14	15F	16A	17B	18C	19	14/06 Tuen Ng Festival	
30	20	21D	22E	23F	24A	25B	26		
	27	28C	29D	30E					
July							2	01/07 HKSAR Establishment Day	
	4	5	6	7	8	9	10		
	11	12	13	14	15	16	17		
	18	19	20	21	22	23	24		
	25	26	27	28	29	30	31		
August	1	2	3	4	5	6	7		
	8	9	10	11	12	13	14		
	15	16	17	18	19	20	21		
	22	23	24	25	26	27	28		
	29	30	31						

Total number of school days: 189days	Total number of school holidays: 93days
Total number of additional discretionary holidays: 0 day	Total number of Staff development days (no school) : 3 days

Remark: 1st Trimester: 24 Aug 2020 - 20 Nov 2020; 2nd Trimester: 23 Nov 2020 - 3 Mar 2021; 3rd Trimester: 4 Mar 2021 - 4 Jun 2021
 (For Form 1/ Form 2 Arts and Technology and Form 3 Science)

School Day
Public Holiday
School Holiday
Staff Development Day
Sunday
Saturday
